NOVI cityofnovi.org

CITY of NOVI CITY COUNCIL

Agenda Item C October 20, 2014

SUBJECT: Approval of the final payment to RCL Construction Company, Inc., for the 2014 Bridge Rehabilitation Project in the amount of \$25,741.64.

SUBMITTING DEPARTMENT: Department of Public Services, Engineering Division &

CITY MANAGER APPROVAL:

EXPENDITURE REQUIRED	\$ 8,725.60 (Cranbrooke/Willowbrook Bridges)
	\$ 6,447.50 (Brookfarm Park Pedestrian Bridge)
	\$ 10,568.54 (Retainage Account 204-000.00-019.141)
	\$ 25,741.64 Total
AMOUNT BUDGETED	\$ 24,209.00 (Cranbrooke/Willowbrook Bridges)
	\$ 6,448.00 (Brookfarm Park Pedestrian Bridge)
	\$ 30,657.00 Total
LINE ITEM NUMBER	204-204.00-866.011 (Cranbrooke/Willowbrook Bridges)
	204-204.00-974.060 (Brookfarm Park Pedestrian Bridge)

BACKGROUND INFORMATION:

The City is required to perform inspections on each of the bridges under the City's control every two years. This project included preventative maintenance on two of the structures as recommended by the previous inspection reports. The following improvements were completed as part of this project:

Cranbrooke Drive Bridge

- Replacement of the settled concrete pavement sections on the bridge.
- Joint and crack sealing on the bridge deck on the southbound side.
- Repair of the south abutment delamination.

Willowbrook Drive Bridge

- Stabilization of the slopes at the abutments.
- Repair of the abutment spalls at beam seats.
- Completion of a 5-foot wide sidewalk along the west side of Willowbrook from the south side of the bridge over Ingersol Creek to the north property line of Brookfarm Park.
- Elimination of open curb drainage from the bridge.
- Enclosure of the ditch along Willowbrook and installation of storm sewer.
- Installation of new guardrail and terminal for the southbound approach to the bridge.
- Removal of the existing small wooden pedestrian bridge over the wet area at the northeast corner of Brookfarm Park, north of Willowbrook Bridge.
- Regrade/reconstruct the sidewalk in the park to make an ADA compliant connection to the proposed Willowbrook Drive sidewalk.

This project also included the replacement of the pedestrian bridge over Ingersol Creek between Brookfarm Park and the Village Oaks Elementary School property. During a recent inspection, City staff observed noticeable deterioration of the bridge's structure. With the assistance of Orchard, Hiltz & McCliment (OHM), staff determined that the bridge was unsafe it was closed immediately. The replacement of this pedestrian bridge was then added to this project.

The construction contract was awarded for this project at the January 6, 2014 City Council meeting to RCL Construction Co., in the amount of \$115,102.


Engineering staff worked with the engineering consultant for this project, OHM, to review and verify the final contract payment amount of \$25,741.64 that is due the contractor (Final Pay Estimate No. 3, attached). The City Attorney reviewed the documentation and found it to be in an acceptable form (Beth Saarela's September 25, 2014 letter, attached).

There was one (1) approved change order issued for this project resulting in a net increase of \$1,277.02 to the construction contract, or 1.1% over the awarded amount. This change order was due to added storm sewer near the ditch enclosure at Willowbrook Drive; the fabrication of bridge rail extensions for the pedestrian bridge; and an overall balancing of all contract line items. The approved change order resulted in a final contract price of \$116,378.52.

RECOMMENDED ACTION: Approval of the final payment to RCL Construction Company, Inc., for the 2014 Bridge Rehabilitation Project in the amount of \$25,741.64.

	1	2	Υ	N
Mayor Gatt				
Mayor Pro Tem Staudt				
Council Member Casey				
Council Member Fischer				

	1	2	Υ	N
Council Member Markham				
Council Member Mutch				
Council Member Wrobel				

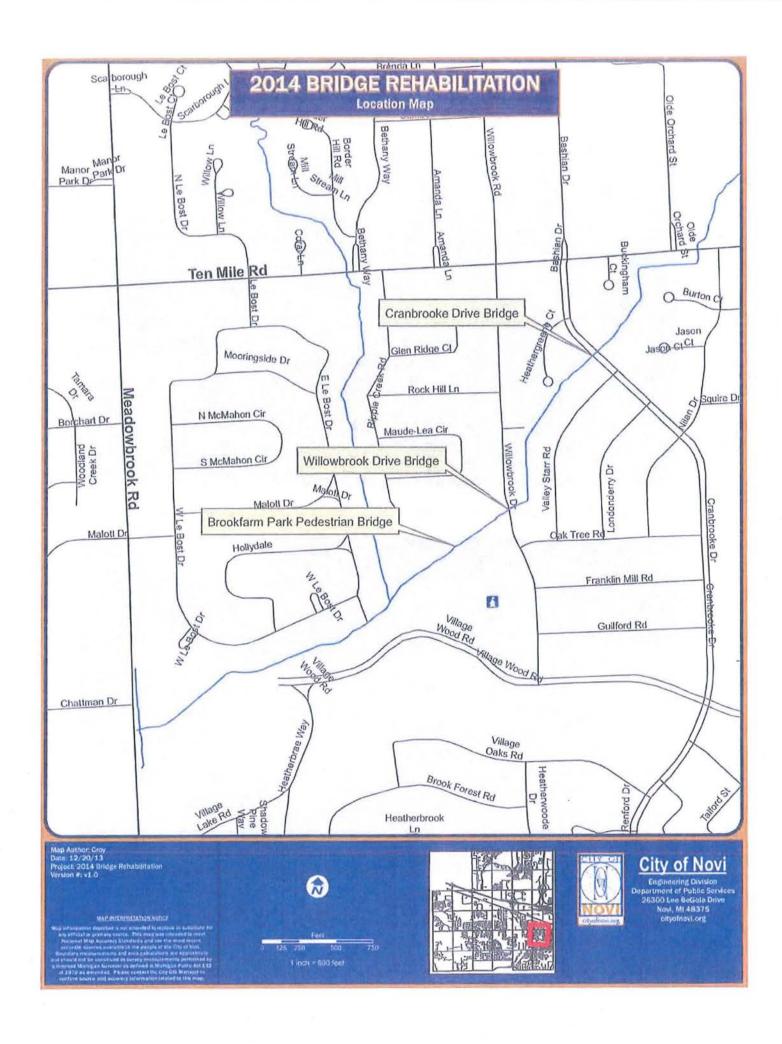

Photos of Completed Bridge Projects



Newly replaced pedestrian bridge connecting Brookfarm Park to Village Oaks Elementary.



Rehabilitated Cranbrooke Drive Bridge over Ingersol Creek.



Willowbrook Drive Bridge Rehab and New Pathway along Willowbrook Drive and connection to Brookfarm Park Pathway



Another view of Willowbrook Drive.



JOHNSON ROSATI SCHULTZ JOPPICH PC

27555 Executive Drive Suite 250 — Farmington Hills, Michigan 48331 Phone; 248,489,4100 | Fax: 248,489,1726

Elizabeth Kudla Saarela esaarela@jrsjlaw.com

www.jrsjlaw.com

September 25, 2014

Aaron Staup, Engineering Coordinator CITY OF NOVI Department of Public Services Field Services Complex 26300 Lee BeGole Drive Novi, MI 48375

Re:

2014 Bridge Rehabilitation

Closing Documents

Dear Mr. Staup:

We have received and reviewed closing documents for the 2014 Bridge Rehabilitation Project:

- 1. Application for Final Payment
- Contractor's Sworn Statement
- Waivers of Lien Consent of Surety
- 4. General Purpose Bond Rider

Subject to approval of the Application for Final Payment by appropriate City staff, the closing documents appear to be in order.

We note that the General Contractor's Waiver of Lien is conditioned upon receipt of final payment in the amount of \$25,741.64. Based on the condition, the Contractor's final check should be held by the City and provided in exchange for the final "unconditional" waiver of lien. The Contractor will be required to pick it up from the City in person.

Please feel free to contact me with any questions or concerns in regard to this matter.

Very truly yours,

JOHNSON, ROSATI, SCHULTZ & JOPPICH, P.C.

Elizabeth Kudla Saarela

FARMINGTON HILLS II LANSING M MARSHALL III ST. CLAIR SHORES

Aaron Staup, Construction Engineering Coordinator September 25, 2014 Page 2

EKS

C:

Maryanne Cornelius, Clerk Rob Hayes, Public Services Director Carl Johnson, Finance Director / Chief Financial Officer Brian Coburn, Engineering Manager Ben Croy, Civil Engineer Chris Donajkowski, OHM Thomas R. Schultz, Esquire



BALANCE DUE THIS PAYMENT:

S 25,741.64 26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

APPLICATION FOR FINAL PAYMENT

2014 Bridge Renabilitation

OWNER:

City of Novi 45175 W. Ten Mile Road Novi, Michigan 48375

ENGINEER:

OHM Advisors, Inc 34000 Plymouth Road Livonia, Michigan 48150 (734) 522-6711

PAYMENT NO.: CONTRACTOR:

RCL Construction, Inc. 777 W. Maynard Road Sanford, Michigan 48657 (989) 687-7319

CONTRACT AMOUNT

\$115,101.50

June 4, 2014 July 28, 2014 July 24, 2014

FINAL COMPLETION DATES

DATES OF ESTIMATE FROM:

June 29, 2014 July 24, 2014

ORIGINAL: REVISED:

\$116,378.52

ORIGINAL: REVISED: ACTUAL:

SECTION 1,									COST OF COMPLETED WORK TO DATE												
tem No.	Civision A - Willowbrook & Crant GL6 204-204,00-866-011 Description of flem	Quareity	CON	CostUnit	Revised) Total Arti	Quantity	91	Arroutt		TOTAL TO DATE Outroity Amount											
	Constr. Inspection "Crew Day"	Unit	Quantity 30.00	15	640 00	Total Acrt 5 19 200		15			0.50	Is	320.00	2%	23.00	15	14,720,00	77%			
1	Mobilization Max 10%	LS	100	Is	9,000.00			15				1				5	9,000,00	100%			
2	Guardrail, Rem	LF		5	9.00			15				1			34.00	5	306.00	100%			
3	Pavt. Rem	SY	96.00	5	40.00	3 3,840	00 87.70	5							87.70	5	3,508.00	100%			
4	Sidewalk Rem	SY	47.00	5	800	\$ 376	00 47.00	5	8.00 9						47.00	5	376.00	100%			
5	Structures, Rem.	LS	1.00	5	2.880.00	5 2,880	00 100	5	2.880.00 9	2,880.00		1			1.00	15	2,880.00	100%			
6	Embankment, CIP	CY	61.00	S	36.00	\$ 2,196	00 76.00	5	36.00 8	2,736 00	15,00	S	540.00	20%	76.00	\$	2,736.00	100%			
7	Erosion Control, Silt Fence	LF	400.00	5	3.00	\$ 1,200	00 290 00	S	3.00 5	870.00	-	1		11,140	290.00	S	870.00	100%			
8	Erosion Control, Check Dam	LF	40.00	5	29.00	\$ 1,160	00 40.00	5	29 00 3	1,160.00				Yang and	40.00	5	1,160.00	100%			
9	Aggregate Base, 6-inch	SY	155,00	5	9.30	5 1,441	50 148.80	5	9.30 9	1,383.84					148.80	5	1,383.84	100%			
10	Culv End Sect, 12-inch	EA	1.00	5	300 00	\$ 300	00 1.00	15	300.00 3	300 00					1.00	5	300.00	100%			
11	Sewer, Cl IV. 12-inch, Tr Det A	LF	105.00	3	27.00	\$ 2.835	00 99.40	5	27.00 \$	2,683.80		1			99.40	15	2,683.80	100%			
12	Dr Structure Cover, Type G	EA	1.00	5	725.00	\$ 725	00 200	15	725.00 5	1,450.00	1.00	S	725.00	50%	2.00	5	1,450,00	100%			
13	Dr Structure, 45-inch Dia	EA	1.00	5	2,500.00	5 2,500	00 2.00	S	2,500.00 \$	5,000.00	1.00	3	2,500,00	50%	200	15	5,000.00	100%			
14	Underdrain Bank 4-inch	LF	35,00	S	6.00	\$ 210	00 46.40	5	6.00 5	278.40	11.40	5	68.40	25%	46,40	5	278 40	100%			
15	HMA Crack Treatment	LF	125.00	S	3.00	5 375	00 181.00	15	3.00 5	483.00	36.00	5	108.00	22%	161.00	5	483.00	100%			
16	Conc Part, Misc. Nonreint, 8-inch	SY	96,00	5	48.00	\$ 4,608	00 87.70	15	48.00 5	4,209 60				P. P. Marie	87.70	5	4,209 60	100%			
17	Bridge Curb	LF	100.00	5	23.00	\$ 2,300	00 95.10	5	23.00 9	2,187 30					95.10	\$	2,187,30	100%			
15	Modular Slock Retaining Wall	SF	68 00	\$	70.00	5 4,760	00 67.00	S	70.00 5	4,690.00				ű	57.00	\$	4,690,00	100%			
19	Hand Chipping, Other than Deck	CF	20.00	5	300.00	\$ 6,000	00 1430	5	300.00 5	4,290.00					14,30	\$	4,290,00	100%			
20	Patch, Forming	SF	40.00	5	19.00	\$ 760	00 28.20	15	19 00 5	535 80				4	28.20	S	535.80	100%			
21	Patching Conc C-L	CY	200	5	3,691.00	5 7,380	00 0.53	5	3,691.00	1,956.23					0.53	5	1,956.23	100%			
22	Curb and Gutter, Bridge Approach	LF	86.00	5	26.00	5 2,236	00 97.70	S	26.00 9	2,540.20	11.70	3	304:20	12%	97.70	15	2,540.20	100%			
23	Sidewalk, Conc. 4-inch	SF	1110.00	5	5.00	\$ 5,550	00 106425	5	500 5	5,321,25			50-00-5		1064.25	S	5,321.25	100%			
24	Guardrail, Type B	LF	15.00	5	65.00	\$ 975	00 15.00	15	65.00 5	975.00					15.00	S	975.00	100%			

TOTAL THIS SHEET

63,915.50

59,120.42

4,245.60

59,120.42 100%



26309 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

APPLICATION FOR FINAL PAYMENT
NOVI PROJECT NO.: 14-7001

PROJECT:

2014 Bridge Rehabilitation

PAYMENT NO .:

FINAL

	SECTION 1.								COST	OF C	OMPLETED	WORK TO	DATE					
ten No	Division A - Willowbrook & Cranbro GL# 204-204 00-965 011 Description of limm	ook, Cont'd	CONTRACT ITEMS (O		(Original) Total Ant	Quartity		DACT ITEMS		nds Total Annt	Quantity	THIS PERIOD Amount	76	Quartity		TAL TO DATE	- 16	
25	Guardrail Appr Term., Type 1B	I EA	1.00	15	800:00		1.00	Is	300.00		00 008				1.00		800.00	100%
	Fence, Moving	LF	21.00	15	THE RESERVE OF STREET			s	25.00		525 00				21.00	-	525.00	1001
	Sign, Type II, Erect, Salv	EA	1 00	5	300.00	\$ 300.00		S	300.00		101.12				0.00	_	1000.00	
	Flexible Slope Paving	SY	67.00	S	140.00	\$ 9,380.00		S	140.00	2	9.380.00				67.00	5	9.380.00	1009
29	Crack Sealing, Conc Pavt	LF	360.00	S	3.00			Is	3.00	5	1.080.00				380.00		1,080.00	1001
30	Restoration	LS	1.00	5	4.050.00	\$ 4,050.00	1.00	S	4,050.00	5	4.050.00					\$	4,050.00	1001
31	Minor Traffic Devices	LS	1.00	S	3,800.00				3.500.00		3,800.00				1.00	s	3.800.00	1009
-	The state of the s	-	1.00	1	0.000.00	0.00000	1.00	1	5.050.00	-	0,000,00				1.00	*	0.000.00	100
				1				_										
								+							1			
				1				1							1			-
_								1						_		-		
_				-			_	-				-		_	-	-		
_		-	-	-	_		_	-										_
_		-	-	-		-	-	-	_	_								_
_				-		-		-										
				1				-										-
_																4		
								1										
																-		
				1														
				1														7
				1		-		1										
		_		1				1										
_		_	1	+		-	-	1							+			-
_			1	+			-	1										
-		_	-	+			_	-							-			
_		_	-	+			-	-		-			_		-			
_			-	-			-	-		-					-	_		_
		_	-	-			_	-		_				_	-	_		_
				-			_											
				-				-		_					_			
			100	1			1											
	TOTAL FROM THIS SHE	ET				\$ 19,935.00				\$	19,635.00		5 -			\$	19,635.00	
	TOTAL FROM OTHER SHE					\$ 83,915.50				5	59,120.42		5 4.245.60			5	59,120.42	
	SUBTOT					5 83.850.50					78.755.42		\$ 4,245.60			5	78,755.42	100



26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

APPLICATION FOR FINAL PAYMENT
14-7001

PROJECT:

2014 Bridge Rehabilitation

NOVI PROJECT NO .:

PAYMENT NO .:

	SECTION 1.					COS	OF	COMPLETED	WORK TO	DATE				1112						
Rem	Givision B - Brookfarm Park Ped GL# 704-704 00-974-060	RACTITEMS	ESTA TRANSPORT				RACT ITEMS	iRevi		THIS PERIOD				TOTAL TO DATE						
No.	Description of item	Unit	Quantity	7	Cost/Unit	Total Arts	_	Duantity	T .	CostUnt	7.7	Total Arrit	Quartery	-	Amount	76	Quantity		Ampuni	
32	Mobilization, Max, 10%	LS	1,00	5	3,100,00		0.00	1.00	5	3,100.00	_	3,100,00		-			1.00	5	3,100.00	100
35	Pavt, Rem	SY	3.00	\$	37.00		1.00	2.30	\$	37.00		85.10		-			2.30	2	35.10	100
34	Sidewalk, Rem	SY	8.00	\$	45.00		0.00	6.90	5	45.00	\$	310.50		-			6.90	5	310.50	100
35	Structures, Rem Portions	LS	1.00	5	1,200.00	-	00.00	1.00	5	1.200.00	\$	1,200.00					1.00	S	1,200.00	100
36	Prefabricated Pedestrian Bridge	LS	1.00	\$	24,500.00	\$ 24,50	0.00	1.00	5	24,500.00	\$	24,500.00					1.00	5	24,500.00	1001
37	Sidewalk, Conc. 4-inch	SP	118.00	5	500	\$ 59	0.00	124.00	5	5.00	5	620.00	6.00	5	30.00	5%	124 00	\$	620.00	100
38	Fence, Moving	LF	44 00	5	10.00	5 44	0.00	45.00	5	10.00	5	450.00	1.00	\$	1000	2%	45.00	5	450.00	100
39	Restoration	LS	1.00	5	950 00	5 95	0.00	1.00	5	950.00	5	950.00		1	-		1.00	5	950.00	100
	TOTAL FROM THIS SHEET TOTAL FROM OTHER SHEET					\$ 31.2i \$ 83.8i \$ 115.1i	0 50				y 10	31,215.60 78,755.42 109,971.02		5 5	40 00 4,245 60 4,285 60			S S	31,215.00 78,755.42 109,971.02	100%



26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

APPLICATION FOR FINAL PAYMENT

PROJECT:

2014 Bridge Rehabilitation

14-7001

PAYMENT NO :

NEW CONTRACT ITEMS

	SECTION 1.						cos	OFC	OMPLETED	WORK TO	DATE						
tem	97777984200420	0.00					CONTRAC					SPERIOD					
No.	Description of flem	Unt	Division	GL#	Quartity	_	cost/Unit		ctal Arra	Quartity	_	Amount	- %	Quantity		Amount .	*
32.	Sewer, CL IV, 18 inch, Tr Det A	Ft	A	GL#204-204.00-896.011	7.00	5	57.50		402.50	7.00	\$	402.50	100%	7.00	\$	402.50	100
33	Conn. Between 18" Conc. & 18" CMP	Ea	A	GL#204-204.00-868.011	1.00	5	598.00	-	598.00	1.00	S	598.00	100%	1.00	5	598.00	100
40	Bridge Rail Extension	LS	8	GL#204-204.00-974.060	1.00	S	5,407,00	\$	5,407.00	1.00	S	5,407.00	100%	1.00	5	5,407.00	100
			0	0	0.00	5		\$	-					0.00	S	-	
			0	0	0.00	5	-	\$	-					0.00	\$	-	
			0	0	0.00	5		\$						0.00	2	~ .	
			0	0	0.00	5		5	- 10					0.00	\$	-	
			0	Ó	0.00	5		\$						0.00	5		
			0	0	0.00	5		\$			-			0.00	5		
			0	0	0.00	5		5	4		1			0.00	5	-	
		V	0	0	0.00	\$		5						0.00	5		
			0	0	0.00	5	- ter	5					The same	0.00	5		
			0	0	0.00	15	-	s						0.00	8	-	
			0	0	0.00	5		s	100	-				0.00	\$	+	
	2		0	0	0.00	5		\$	- 0-1					0.00	S		
			0	0	0.00	5		5						0.00	5		
			0	0	0.00	5		5						0.00	5	-	
	Lame to the second	r	0	0	0.00	S		s						0.00	5		
		i i	0	0	0.00	15		s						0.00	s	-	
			0	0	0.00	15	-	s						0.00	S	-	
			0	0	0.00	18		5						0.00	5		
			0	0	0.00	15		s	7.47					0.00	5	-	
			0	0	0.00	5		s						0.00	s		
			0	0	0.00	15		s						0.00	s		
			0	0	0.00	18		5						0.00	5		
			0	0	0.00	5		s						0.00	s		
_			0	0	0.00	5		s						0.00	5		
			0	0	0.00	5		5						0.00	5		
_	TOTAL FROM THIS SHEET				0.00	3		5	6.407.50		5	8.407.50		7.00	5	6,407.50	
	TOTAL FROM OTHER SHEETS			\$ 115,101.5	0				109.971.02			4.285.60				109,971.02	
	GRAND TOTAL			\$ 115,101.1					118,378.52		5	10,693.10				116,378.52	100%



26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

	Section 2.								
			APPLICATION I	FOR FINA	L PAYME	NT			
PROJECT:	2014 Bridge Rehabilitation	NOVI PRO				22-5-11111	PAYM	ENT NO.: FINAL	
Original Cont	ract Amount:	\$	115,101,50		СНА	NGE ORDE	RS		
hange Orde	rs:	s	1,277 02	No	<u>Date</u>		4	Amount	
djusted Con	stract Amount to Date:	\$	116,378.52		July 28, 2014		\$	1,277,02	
otal Cost of	Work Performed to Date:	s	116,378.52				S	,	
INUS Retain	nage: [0% S	9.				S		
	ction "Crew Days": To Date	23.00 S 0.50					5	4)	
et Amt. Earne	This Pay [ed of Contract and Extra Work to Date:	s s	116,378 52				5		
INUS L.D.'s		s	4				5	7	
Subtotal:	\$ amount/day = \$400	s	116,378 52				S S		
DD Incentiv	e "Crew Days", if under:	\$	4,480.00			TOTAL:	\$	1,277.02	
subtotal:		o \$	120,858.52						
IINUS Amou	int of Previous Payments: 45749 1 5 99,746,04 2 5 25,370,37 3 5 75,370,37	5 A	95,116.88						
	2 5 25,370.87				inspection "Crew C				
	7. 7				Additional "Crew D			30.00	
	5 \$ - 6 \$ -				Total Inspection "C Inspection "Crew C			23.00	
	7 \$				Inspection "Crew D			7.00	
	8 \$.							- Louis Control	
	10 S -	122/14/2014							
BALANCI	E DUE THIS PAYMENT:	\$	25,741.64						



26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

Section 3.

Chns S. Donajkowski Print Name

APPLICATION FOR FINAL PAYMENT

PROJECT:

2014 Bridge Rehabilitation

NOVI PROJECT NO .:

14.7001

PAYMENT NO .:

is recommended

Payment of the above AMOUNT DUE THIS APPLICATION

FINAL

The undersigned CONTRACTOR certifies that. (1) Any previous progress payments received from OWNIER on amount of Work done under the Contract referred to above have been applied to discharge in full all obligations of CONTRACTOR incurred in connection with Work covered by prior Applications for Payment; (2) title to all Work, materials, and equipment incorporated in said Work of otherwise listed in or covered by this Application for Payment will pass to OWNIER at time of payment free and clear of all leins, claims, security interest, and encumberences (except such as are covered by Bond acceptable to OWNIER interest, and encumberence is such lens, claims security interest, or encumberence); and (3) all Work covered by this Application for Payment is in accordance with the Contract Documents and not defective as that term is defined in the Contract Documents.

RCL Construction, Inc.	Date:	9/2/14	Dated: 10/6/14
Contractor Company Contractor Authorized Signature			ACI
By Rodale E. Bauer			By Brian Coburn, PE., Engineering Manager
OHM Advisors, Inc.	Date:	1-23-2014	Dated: 10/6/14
Chas Danisania			en received from each subcontractor and/or supplier, reviewed and approved

All Full Unconditional Waivers of lien have been received from each subcontractor and/or supplier, reviewed and approved by the Consultant Also, attached to this Final Payment is a copy of the Contractor's Sworn Statement, Consent of Surety, and a new Maintenance and Guarantee Bond (if the amount is greater than the final contract price) or a Maintenance Bond Rider covering the difference between (he final contract price and the awarded amount).

CREW DAYS - TRACKING BY DIVISION

Project: 2014 Bridge Renabilitation

Novi Project No.: 14-7001

Contractor, RCL Construction, Inc.

Engineer, OHM Advisors, Inc.

	USED (By Pay Estimate) D PEW1 PEW2 PEW3 PEW4 PEW5 PEW5 PEW7 PEW6 PEW9 PEW10 FINAL TOTAL																					
REMAINING	TOTAL	FINAL	PE#10	PE#9	PERA	PE#7	PE#6	PE#S	PE#4	PE#3	FE#2	PEWI	REVISED	CO#	ADD/DEDUCT	ORIGINAL	DESCRIPTION	NOISIVIC				
6.	19.00	0.00							2		6.50	12.50	25.00			25.00	Willowproak/Cranbrke	A				
6.	4.00	0.50									0.00	3.50	5.00			5.00	Brooklarm Ped Bridge	8				
													C									
			1																			
						July 1																
																	1					
		100						Cont.	- 9				5									
		1				3																
		160									- 1											
											1	A										
1111											-											
					1		201111						1									
																-						
		1											_									
								-			1 1											
	A Comment											- 0										
7.5	23.00	0.50	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	6.50	15.00	30.00		0.00	30,00	TOTALS					

RCI Construction, Inc. Contractor Company	(25/14) CITY OF HOAT
Contractor Authorized Signature	By: Aeron J. Staup, Construction Engineering Coordinator
By: Sam Loedtke	Date: 10/6/14
OHM Advisors, Inc. Date:	125/14 BC
Consultant Authorized Signature	By: Erlan Coburn, P.E. Engineering /Manager
Ex. Chis S. Danajkowski	Date 15/6/14

^{*} Consiliant to provide Engineering Services Amendment form with any Pay Application, adding or deducting crew days to as from the contractor.



to the plans and specifications.

CONTRACTORS SWORN STATEMENT

The general contractor must execute this Sworn Statement. Prior to execution, the general contractor shall on Schedule B of this Sworn Statement list the names of all persons, firms, or corporations engaged by the General Contractor to furnish services, equipment, labor and/or materials in connection with the work performed on the premises including the type of work materials furnished by each.

The examining attorney shall verify that every person or firm listed in Schedule B has properly executed appropriate waivers of lien prior to issuance of any final payments.

t of ed by the
or repair
îrm, or
to said
ndersigned amed in

The undersigned further states that all material (except as disclosed on said Schedule B) has been or will be furnished from his/her own stock and has been paid for in full; that there are no other contracts or subcontracts for said work outstanding, and that there is nothing due or to become due to any person for services, equipment, material, labor, or any other work done or to be done in connections with said work other than the stated on Schedule B. There are no chattel mortgages, personal property leases, conditional sale contracts or any other agreements given are now outstanding as to nay fixtures, equipment, appliances or materials placed upon or installed in or upon the aforementioned premises or improvements thereon. All waivers are true, correct, and genuine and are delivered unconditionally. Furthermore, there is no claim, either legal or equitable; to defeat the validity of said waivers.

the Schedule B of this Sworn Statement, has been fully accepted by the owner and completed according

Signed this 2nd day of September , 2014	-
Name: RCL Construction Co., Inc.	
(individual/corporation/partnership)	
By: Attest: Sam Luedtke, Project	et Mgr.
Subscribed and sworn to before me this day of	, 20
Notary Public: My J. Karri	
Sherry L. Harris	
My Commision Expires: 07/14/17	

NOTARY SEAL

SHERRY L. HARRIS
NOTARY PUBLIC - STATE OF MICHIGAN
COUNTY OF GLADWIN
My Commission expires July 14, 2017
Acting in the County of Michigan

SCHEDULE B - CONTRACTORS SWORN STATEMENT

Name of Subcontracting Firm	Material Furnished	Amount of Contract	Previously Paid to Date	Current Request	Retainage to Date	Balance Due
Chippewa Asphalt	Joint Sealant	\$1,700.00	\$1,700.00		0.0%	\$0.00
Finishing Touch Photo	Video	\$1,125.00	\$1,125.00		0.0%	\$0.00
Riteway Fence	Guardrail	\$2,000.00	\$2,000.00		0.0%	\$0.00
All Labor and Material Paid to date						\$0.00
	-					
TOTALS		\$4,825.00	\$4,825.00	\$0.00		\$0.00

RECAPITULATION

Amount of Original Contract:	\$115,101.50	Work Completed to Date:	\$116,378.52
Plus: Extras to Contract:	\$1,277.02	Less: Total Retainage:	\$0.00
Total: Contract plus Extras:	\$116,378.52	Less: Amount Previously Paid:	\$95,116.88
Less: Credits to Contract:		Less: Amount of this Request:	\$25,741.64
Total: Adjusted Contract:	\$116,378.52	Total Balance Due:	-\$4,480.00



FULL UNCONDITIONAL WAIVER OF LIEN

My/our contract with	RCL Construction Co., Inc. to provide (Prime Contracting Party)
Crack Sealant (Type of service)	for the improvement of the property
described as	2014 Bridge Rehabilitation (Project Name)
	satisfied, by signing this waiver, all my/our construction erty are hereby waived and released.
owner or lessee of the prop Notice of Furnishing from m the owner, lessee, or design us, the owner, lessee, or des	ded to property that is a residential structure and if the erty or the owner's or lessee's designee has received a e/one or us or if I/we are not required to provide one, and ee has not received this waiver directly from me/one of ignee may not rely upon it without contacting me/one of hone, or personally, to verify that it is authentic.
Signed on: 4/11/14	(Signature of Lien Claimant)
	Localee Begalle (Printed Name of Lien Claimant)
	Office 6 ADMIN (Title of Lien Claimant)
Company Name: All Parish	Fox 515, Clip ME 48420

DO NOT SIGN BLANK OR INCOMPLETE FORMS. RETAIN A COPY.





FULL UNCONDITIONAL WAIVER OF LIEN

My/our contract with		to provide
	(Prime Contracting Party)	
audio Video au	nite Servey for the improvem	ent of the property
described as	2014 Bridge Rehabilitation (Project Name)	
	d satisfied, by signing this waiver, all roperty are hereby waived and released.	my/our construction
owner or lessee of the pr Notice of Furnishing from the owner, lessee, or desi us, the owner, lessee, or desi	roperty or the owner's or lessee's design me/one or us or if I/we are not required gnee has not received this waiver direct lesignee may not rely upon it without collephone, or personally, to verify that it is	nee has received a to provide one, and tly from me/one of ontacting me/one of
Signed on: 9/13/14	(Signature of Lier Car	imant)
	C. HWLLEY (Printed Name of Lien C	laimant)
	(Title de Lien Clair	mant)
Company Name:	FINISHING TOUCH	
Address:	PHOTO & VIDEO 25095-25-MILE RD.	
Telephone:	CHESTERFIELD, MI 48051 (586) 749-3340	

DO NOT SIGN BLANK OR INCOMPLETE FORMS. RETAIN A COPY.



FULL UNCONDITIONAL WAIVER OF LIEN

My/our contract with RCL Construction Co., Inc. to provide

	(Prime Contracting Party)
Guard Rail	for the improvement of the property
	4 Bridge Rehabilitation (Project Name)
	(ridget state)
having been fully paid and satisf lien rights against such property a	ied, by signing this waiver, all my/our construction re hereby waived and released.
owner or lessee of the property Notice of Furnishing from me/one the owner, lessee, or designee ha us, the owner, lessee, or designee	to property that is a residential structure and if the or the owner's or lessee's designee has received a cor us or if I/we are not required to provide one, and as not received this waiver directly from me/one of may not rely upon it without contacting me/one of or personally, to verify that it is authentic.
Signed on: 912214	Mity Grundner General General General Chairmant)
	Christy Grundner (Pringed Name of Lien Claimant)
	Covityol Lew (Title of Lien Claimant)
Company Name: <u>Rite Wo</u> Address: <u>16539 Burrol</u> Telephone: (586) 262	aghs Avc. Sterling Heights MI 3730 46314

DO NOT SIGN BLANK OR INCOMPLETE FORMS. RETAIN A COPY.

FULL CONDITIONAL WAIVER

My/our contract with <u>City of Novi</u> to provide service for the improvement to the property described as: <u>Novi 2014 Bridge Rehabilitation</u> having been fully paid and satisfied, all my/our construction lien rights against such property are hereby waived and released.

This waiver is conditional on actual payment of

\$ 25,741.64

Rodney E. Bauer, Vice-President (signature of lien claimant)

RCL Construction Co., Inc.

Signed on: 9/02/14

Address: 777 W. Maynard Rd.

Telephone: 989-687-7319

Sanford, MI 48657

H:\fullwaiv.doc

CONSENT OF SURETY TO FINAL PAYMENT

AIA Document G707



Bond No. MIC60587

City of Novi 26300 Lee Be Gole Dr. Novi, MI 48375 PROJECT: Name and address 2014 Bridge Rehabilitation In accordance with the provisions of the Contract between the Owner and the Contractor as indicated above, the Insert name and address of Surety) Merchants Bonding Company (Mutual) PO Box 3018 Bothell, WA 98041-3018 Insert name and address of Contractor) RCL Construction Company, Inc. PTY W. Maynard Rd. Sanford, MI 48657 Insert name and address of Owner) City of Novi City of	TO OWNER:	ARCHITECT'S PROJECT NO:
28300 Lee Be Gole Dr. Novi, MI 48375 PROJECT: Novi, MI 48375 PROJECT: CONTRACT DATED: Name and address) 2014 Bridge Rehabilitation In accordance with the provisions of the Contract between the Owner and the Contractor as indicated above, the dinsert name and address of Surety) Merchants Bonding Company (Mutual) PO Box 3018 Bothell, WA 98041-3018 In bond of dinsert name and address of Contractor) RCL Construction Company, Inc. 777 W. Maynard Rd. Sanford, MI 48657 Interest name and address of Owner) City of Novi 18300 Lee Be Gole Dr. Novi, MI 48375 In set forth in said Surety's bond number MIC60587 NOVINER, Merchants Bonding Company (Mutual) Merchants Bonding Company (Mutual) (Surity) Merchants Bonding Company (Mutual) (Surity) Merchants Bonding Company (Mutual) (Surity) Theresa A. Lamb, Attorney-in-Fact (Printed name and title)	(Name and Address)	
Novi, MI 48375 PROJECT: CONTRACT DATED: Name and address) 2014 Bridge Rehabilitation In accordance with the provisions of the Contract between the Owner and the Contractor as indicated above, the Insert name and address of Surety) Merchants Bonding Company (Mutual) PO Box 3018 Bothell, WA 98041-3018 In bond of Insert name and address of Contractor) RCL Construction Company, Inc. PTT W. Maynard Rd. Sanford, MI 48657 Insert name and address of Owner; City of Novi Sayou Lee Be Gole Dr. Novi, MI 48375 In set forth in said Surety's bond number MIC60587 NOVINERS WHEREOF, the Surety has hereunto set its hand on this date: 09/03/2014 Insert in writing the month followed by the numeric date and year) Merchants Bonding Company (Mutual) (Surity) (Signature of authorized representative) Theresa A. Lamb, Attorney-in-Fact (Printed name and tite)		CONTRACT FOR: Construction
PROJECT: Name and address) 2014 Bridge Rehabilitation In accordance with the provisions of the Contract between the Owner and the Contractor as indicated above, the Insert name and address of Surety) Merchants Bonding Company (Mutual) PO Box 3018 Bothell, WA 98041-3018 Insert name and address of Contractor) RCL Construction Company, Inc. PROJECT (CONTRACTOR) RCL Construction Company, Inc. RCL Construction Company, Inc. RCL Construction of the final payment to the Contractor, and agrees that final payment to the Contractor shall not relieve interty of any of its obligations to insert name and address of Owner) City of Novi REGOOD Lee Be Gole Dr. Rowl, MI 48375 In Set forth in said Surety's bond number MIC60587 N WITNESS WHEREOF, the Surety has hereunto set its hand on this date: 09/03/2014 Merchants Bonding Company (Mutual) (Surary) Merchants Bonding Company (Mutual) (Surary) (Signature of authorized representative) Theresa A. Lamb, Attorney-in-Fact (Printed name and title)		
Name and address) 2014 Bridge Rehabilitation In accordance with the provisions of the Contract between the Owner and the Contractor as indicated above, the Insert name and address of Surery) Merchants Bonding Company (Mutual) PO Box 3018 Bothell, WA 98041-3018 In bond of Insert name and address of Contractor) RCL Construction Company, Inc. 1777 W. Maynard Rd. Sanford, MI 48657 CONTRACTOR, tereby approves of the final payment to the Contractor, and agrees that final payment to the Contractor shall not relieve interty of any of its obligations to Insert name and address of Owner) 2010 of Novi 20300 Lee Be Gole Dr. Novi, MI 48375 Set forth in said Surety's bond number MIC60587 N WITNESS WHEREOF, the Surety has hereunto set its hand on this date: 09/03/2014 Insert in writing the month followed by the numeric date and year) Merchants Bonding Company (Mutual) (Surary) (Signature of authorized representative) Theresa A. Lamb, Attorney-in-Fact	AND THE STANDARD TO A CONTROL OF STANDARD STANDAR	CONTRACTORATED
Merchants Bonding Company (Mutual) PO Box 3018 Bothell, WA 98041-3018	(Name and address) 2014 Bridge Rehabilitation	CONTRACT DATED:
Bothell, WA 98041-3018 Bothell, WA 98041-3018 In bond of Insert name and address of Contractor) RCL Construction Company, Inc. 777 W. Maynard Rd. Sanford, MI 48657 CONTRACTOR, erreby approves of the final payment to the Contractor, and agrees that final payment to the Contractor shall not relieve insert name and address of Owner) City of Novi 26300 Lee Be Gole Dr. Novi, MI 48375 Set forth in said Surety's bond number MIC60587 N WITNESS WHEREOF, the Surety has bereunto set its hand on this date: 09/03/2014 Insert in writing the month followed by the numeric date and year) Merchants Bonding Company (Mutual) (Surary) (Signature of authorized representative) Theresa A. Lamb, Attorney-in-Fact (Printed name and title)	In accordance with the provisions of the Contract between the (Insert name and address of Surety)	Owner and the Contractor as indicated above, the
Bothell, WA 98041-3018 Bothell, WA 98041-3018 In bond of Insert name and address of Contractor) RCL Construction Company, Inc. 777 W. Maynard Rd. Sanford, MI 48657 CONTRACTOR, erreby approves of the final payment to the Contractor, and agrees that final payment to the Contractor shall not relieve insert name and address of Owner) City of Novi 26300 Lee Be Gole Dr. Novi, MI 48375 Set forth in said Surety's bond number MIC60587 N WITNESS WHEREOF, the Surety has bereunto set its hand on this date: 09/03/2014 Insert in writing the month followed by the numeric date and year) Merchants Bonding Company (Mutual) (Surary) (Signature of authorized representative) Theresa A. Lamb, Attorney-in-Fact (Printed name and title)	Merchants Bonding Company (Mutual)	
Bothell, WA 98041-3018 , surety, on bond of Insert name and address of Contractor) RCL Construction Company, Inc. 777 W. Maynard Rd. Sanford, MI 48657 , CONTRACTOR, dereby approves of the final payment to the Contractor, and agrees that final payment to the Contractor shall not relieve insert name and address of Owner) City of Novi 26300 Lee Be Gole Dr. Novi, MI 48375 , set forth in said Surety's bond number MIC60587 N WITNESS WHEREOF, the Surety has hereunto set its hand on this date: 09/03/2014 Insert in writing the month followed by the numeric date and year) Merchants Bonding Company (Mutual) (Signature of authorized representative) Theresa A. Lamb, Attorney-in-Fact (Printed name and title)	PO Box 3018	
Insert name and address of Contractor) RCL Construction Company, Inc. 777 W. Maynard Rd. Sanford, MI 48657 , CONTRACTOR, dereby approves of the final payment to the Contractor, and agrees that final payment to the Contractor shall not relieve functy of any of its obligations to finsert name and address of Owner) City of Novi 26300 Lee Be Gole Dr. Novi, MI 48375 s set forth in said Surety's bond number MIC60587 N WITNESS WHEREOF, the Surety has hereunto set its hand on this date: 09/03/2014 Insert in writing the month followed by the numeric date and year) Merchants Bonding Company (Mutual) (Surgry) (Signature of authorized representative) Theresa A. Lamb, Attorney-in-Fact (Printed name and title)		
Insert name and address of Contractor) RCL Construction Company, Inc. 777 W. Maynard Rd. Sanford, MI 48657 , CONTRACTOR, dereby approves of the final payment to the Contractor, and agrees that final payment to the Contractor shall not relieve functy of any of its obligations to finsert name and address of Owner) City of Novi 26300 Lee Be Gole Dr. Novi, MI 48375 s set forth in said Surety's bond number MIC60587 N WITNESS WHEREOF, the Surety has hereunto set its hand on this date: 09/03/2014 Insert in writing the month followed by the numeric date and year) Merchants Bonding Company (Mutual) (Surety) (Signature of authorized representative) Theresa A. Lamb, Attorney-in-Fact (Printed name and title)		, SURETY,
RCL Construction Company, Inc. 777 W. Maynard Rd. Sanford, MI 48657 , CONTRACTOR, dereby approves of the final payment to the Contractor, and agrees that final payment to the Contractor shall not relieve interest of any of its obligations to insert name and address of Owner) City of Novi 26300 Lee Be Gole Dr. Novi, MI 48375 s set forth in said Surety's bond number MIC60587 N WITNESS WHEREOF, the Surety has hereunto set its hand on this date: 09/03/2014 (Insert in writing the month followed by the numeric date and year) Merchants Bonding Company (Mutual) (Surâry) (Signature of authorized representative) Theresa A. Lamb, Attorney-in-Fact (Printed name and title)		
CONTRACTOR, CONTRACTOR, CONTRACTOR, CONTRACTOR, CONTRACTOR, Contractor of the final payment to the Contractor, and agrees that final payment to the Contractor shall not relieve inverty of any of its obligations to insert name and address of Owner) City of Novi 26300 Lee Be Gole Dr. Novi, MI 48375 Seet forth in said Surety's bond number MIC60587 N WITNESS WHEREOF, the Surety has bereunto set its hand on this date: 09/03/2014 Insert in writing the month followed by the numeric date and year) Merchants Bonding Company (Mutual) (Surary) (Signature of authorized representative) Theresa A. Lamb, Attorney-in-Fact (Printed name and title)	California de la Carres de California de Colonia de Colonia de California de Californi	
Sanford, MI 48657 CONTRACTOR, acreby approves of the final payment to the Contractor, and agrees that final payment to the Contractor shall not relieve interest of any of its obligations to insert name and address of Owner) City of Novi 26300 Lee Be Gole Dr. Novi, MI 48375 s set forth in said Surety's bond number MIC60587 N WITNESS WHEREOF, the Surety has hereunto set its hand on this date: 09/03/2014 Insert in writing the month followed by the numeric date and year) Merchants Bonding Company (Mutual) (Surgny) (Signature of authorized representative) Theresa A. Lamb, Attorney-in-Fact (Printed name and title)	50 May 19 19 19 19 19 19 19 19 19 19 19 19 19	
CONTRACTOR, acreby approves of the final payment to the Contractor, and agrees that final payment to the Contractor shall not relieve durety of any of its obligations to dissert name and address of Owner) City of Novi 26300 Lee Be Gole Dr. Novi, MI 48375 s set forth in said Surety's bond number MIC60587 N WITNESS WHEREOF, the Surety has hereunto set its hand on this date: 09/03/2014 Insert in writing the month followed by the numeric date and year) Merchants Bonding Company (Mutual) (Surary) (Signature of authorized representative) Theresa A. Lamb, Attorney-in-Fact (Printed name and title)		
Movi, MI 48375 s set forth in said Surety's bond number MIC60587 N WITNESS WHEREOF, the Surety has hereunto set its hand on this date: 09/03/2014 Insert in writing the month followed by the numeric date and year) Merchants Bonding Company (Mutual) (Surary) (Signature of authorized representative) Theresa A. Lamb, Attorney-in-Fact (Printed name and title)	Surety of any of its obligations to (Insert name and address of Owner)	
N WITNESS WHEREOF, the Surety has hereunto set its hand on this date: 09/03/2014 Insert in writing the month followed by the numeric date and year) Merchants Bonding Company (Mutual) (Surary) (Signature of authorized representative) Theresa A. Lamb, Attorney-in-Fact (Printed name and title)	500 50 pt 100 50 50 pt 100 pt	
NWITNESS WHEREOF, the Surety has hereunto set its hand on this date: 09/03/2014 Insert in writing the month followed by the numeric date and year) Merchants Bonding Company (Mutual) (Surary) (Signature of authorized representative) Theresa A. Lamb, Attorney-in-Fact (Printed name and title)		
N WITNESS WHEREOF, the Surety has hereunto set its hand on this date: 09/03/2014 Insert in writing the month followed by the numeric date and year) Merchants Bonding Company (Mutual) (Surary) (Signature of authorized representative) Theresa A. Lamb, Attorney-in-Fact (Printed name and title)	NOVI, IVII 463/3	OWNER.
Merchants Bonding Company (Mutual) (Surary) (Signature of authorized representative) Theresa A. Lamb, Attorney-in-Fact (Printed name and title)	as set forth in said Surety's bond number MIC60587	300 100 2000
(Signature of authorized representative) Theresa A. Lamb, Attorney-in-Fact (Printed name and title)	N WITNESS WHEREOF, the Surety has hereunto set its ha Insert in writing the month followed by the numeric date and	nd on this date: 09/03/2014 year)
(Signature of authorized representative) Theresa A. Lamb, Attorney-in-Fact (Printed name and title)		Merchants Bonding Company (Mutual)
Theresa A. Lamb, Attorney-in-Fact		(Surgery) 1124 (1 Lamb
(Printed name and title)		(Signature of authorized representative)
(Printed name and title)	War V Mine Joxest	
Witness		

AIA DOCUMENT G707- CONSENT OF SURETY TO FINAL PAYMENT-1994 EDITION • AIA G1994 • THE AMERICAN INSTITUTE OF ARCHITECTS, 1735 NEW YORK AVENUE, NW.WASH-INGTON, D.C. 20006-5292 • WARNING: Unlicensed photocopying violates U.S. copyright laws and will subject the violator to legal prosecution.

G707-1994



Know All Persons By These Presents, that MERCHANTS BONDING COMPANY (MUTUAL) and MERCHANTS NATIONAL BONDING, INC., both being corporations duly organized under the laws of the State of lowa (herein collectively called the "Companies"). and that the Companies do hereby make, constitute and appoint, individually,

Andy D. Prill: Brandon K Bush: Chad M Epple: Darlene Jakielski; Jim S Kuich; Jim W Doyle; Julie M Glover: Michael A Murphy: Nancy J Osborne: S M Scott; Steve Wagner: Theresa A Lamb

their true and lawful Attorney-in-Fact, with full power and State of Washington and authority hereby conferred in their name, place and stead, to sign, execute, acknowledge and deliver in their behalf as surely any and all bonds, undertakings, recognizances or other written obligations in the nature thereof, subject to the limitation that any such instrument shall not exceed the amount of

FIFTEEN MILLION (\$15,000,000.00) DOLLARS


and to bind the Companies thereby as fully and to the same extent as if such bond or undertaking was signed by the duly authorized officers of the Companies, and all the acts of said Attorney-in-Fact, pursuant to the authority herein given, are hereby ratified and confirmed.

This Power-of-Attorney is made and executed pursuant to and by authority of the following By-Laws adopted by the Board of Directors of the Merchants Bonding Company (Mutual) on April 23, 2011 and adopted by the Board of Directors of Merchants National Bonding, Inc., on October 24, 2011.

"The President, Secretary, Treasurer, or any Assistant Treasurer or any Assistant Secretary or any Vice President shall have power and authority to appoint Attorneys-in-Fact, and to authorize them to execute on behalf of the Company, and attach the seal of the Company thereto, bonds and undertakings, recognizances, contracts of indemnity and other writings obligatory in the nature thereof.

The signature of any authorized officer and the seal of the Company may be affixed by facsimile or electronic transmission to any Power of Altorney or Certification thereof authorizing the execution and delivery of any bond, undertaking, recognizance, or other suretyship obligations of the Company, and such signature and seal when so used shall have the same force and effect as though manually fixed.

In Witness Whereof, the Companies have caused this instrument to be signed and sealed this 24thday of January, 2014.



MERCHANTS BONDING COMPANY (MUTUAL) MERCHANTS NATIONAL BONDING, INC.

President

On this 24th day of January . 2014, before me appeared Larry Taylor, to me personally known, who being by me duly sworn did say that he is President of the MERCHANTS BONDING COMPANY (MUTUAL) and MERCHANTS NATIONAL BONDING, INC.; and that the seals affixed to the foregoing instrument is the Corporate Seals of the Companies; and that the said instrument was signed and sealed in behalf of the Companies by authority of their respective Boards of Directors,

In Testimony Whereof, I have hereunto set my hand and affixed my Official Seal at the City of Des Moines, lowa, the day and year first above written.



Notary Public, Polk County, Iowa

STATE OF IOWA COUNTY OF POLK ss.

STATE OF IOWA

COUNTY OF POLK ss.

I. William Warner, Jr., Secretary of the MERCHANTS BONDING COMPANY (MUTUAL) and MERCHANTS NATIONAL BONDING, INC., do hereby certify that the above and foregoing is a true and correct copy of the POWER-OF-ATTORNEY executed by said Companies, which is still in full force and effect and has not been amended or revoked.

In Wilness Whereof, I have hereunto set my hand and affixed the seal of the Companies on



William Warner Jo.

POA 0014 (11/11)

INCREASE/DECREASE RIDER

RIDER to be attached to and form a part of Bond No. MIC60	587	wherei	n
Merchants Bonding Company (Mutual)		The State of the Control of the Cont	is named as Surety,
on behalf of RCL Construction Company, Inc.			as Principal,
in favor of City of Novi			in the sum of
One Hundred Fifteen Thousand One Hundred One Dollars and 50/100 (\$115	.101.50)		
	, dated		
IT IS HEREBY UNDERSTOOD AND AGREED that effecti	ve the 28		day of
July, 2014 the penalty of this bo		from:	day of
One Hundred Fifteen Thousand One Hundred One Dollars and 50/100		(\$115,	101.50) to
One Hundred Sixteen Thousand Three Hundred Seventy-Eight Dollars and			6,378,52).
Signed, sealed and dated this 2nd day of September	er ,2014	·	
	RCL Construction Com	oany, Inc.	
	BY: Dhilling	(Principal)	V.P.
	Merchants Bonding C	ompany (Mutual)	
	BY: Theresa (Thank	-
	Theresa A. Lamb		Attorney-in-Fact



Know All Persons By These Presents, that MERCHANTS BONDING COMPANY (MUTUAL) and MERCHANTS NATIONAL BONDING, INC., both being corporations duly organized under the laws of the State of lowa (herein collectively called the "Companies"), and that the Companies do hereby make, constitute and appoint, individually,

Andy D Prill; Brandon K Bush; Chad M Epple; Darlene Jakielski; Jim S Kuich; Jim W Doyle; Julie M Glover; Michael A Murphy; Nancy J Osborne; S M Scott; Steve Wagner; Theresa A Lamb

Bothell and State of Washington their true and lawful Attorney-in-Fact, with full power of and authority hereby conferred in their name, place and stead, to sign, execute, acknowledge and deliver in their behalf as surety any and all bonds, undertakings, recognizances or other written obligations in the nature thereof, subject to the limitation that any such instrument shall not exceed the amount of:

FIFTEEN MILLION (\$15,000,000.00) DOLLARS

and to bind the Companies thereby as fully and to the same extent as if such bond or undertaking was signed by the duly authorized officers of the Companies, and all the acts of said Attorney-in-Fact, pursuant to the authority herein given, are hereby ratified and confirmed.

This Power-of-Attorney is made and executed pursuant to and by authority of the following By-Laws adopted by the Board of Directors of the Merchants Bonding Company (Mutual) on April 23, 2011 and adopted by the Board of Directors of Merchants National Bonding, Inc., on October 24, 2011.

"The President, Secretary, Treasurer, or any Assistant Treasurer or any Assistant Secretary or any Vice President shall have power and authority to appoint Attorneys-in-Fact, and to authorize them to execute on behalf of the Company, and attach the seal of the Company thereto, bonds and undertakings, recognizances, contracts of Indemnity and other writings obligatory in

The signature of any authorized officer and the seal of the Company may be affixed by facsimile or electronic transmission to any Power of Attorney or Certification thereof authorizing the execution and delivery of any bond, undertaking, recognizance, or other suretyship obligations of the Company, and such signature and seal when so used shall have the same force and effect as though manually fixed."

In Wilness Whereof, the Companies have caused this instrument to be signed and sealed this 24thday of January, 2014.

OING CO Secondaria 14

MERCHANTS BONDING COMPANY (MUTUAL) MERCHANTS NATIONAL BONDING, INC.

STATE OF IOWA COUNTY OF POLK ss.

On this 24th day of January . 2014, before me appeared Larry Taylor, to me personally known, who being by me duly sworn did say that he is President of the MERCHANTS BONDING COMPANY (MUTUAL) and MERCHANTS NATIONAL BONDING, INC.; and that the seals affixed to the foregoing instrument is the Corporate Seals of the Companies; and that the said instrument was signed and sealed in behalf of the Companies by authority of their respective Boards of Directors.

In Testimony Whereof, I have hereunto set my hand and affixed my Official Seal at the City of Des Moines, lowa, the day and year first above written.

> MARANDA GREENWALT Commission Number 770312 My Commission Expires October 28, 2014

Notary Public, Polk County, lowa

STATE OF IOWA COUNTY OF POLK SS.

1. William Warner, Jr., Secretary of the MERCHANTS BONDING COMPANY (MUTUAL) and MERCHANTS NATIONAL BONDING, INC.. do hereby certify that the above and foregoing is a true and correct copy of the POWER-OF-ATTORNEY executed by said Companies, which is still in full force and effect and has not been amended or revoked,

In Wilness Whereof, I have hereunto set my hand and affixed the seal of the Companies on I'm day of September



William Harner Js.

POA 0014 (11/11)
