

CITY of NOVI CITY COUNCIL

Agenda Item I November 9, 2015

SUBJECT: Approval of the final payment to Asphalt Specialists, Inc. for the West Road Rehabilitation project in the amount of \$11,760.07, plus interest earned on retainage.

SUBMITTING DEPARTMENT: Department of Public Services, Engineering Division





| EXPENDITURE REQUIRED | \$ 11,760.07 | |
|----------------------|--------------------|--|
| AMOUNT BUDGETED | \$ 65,904.00 | |
| LINE ITEM NUMBER | 202-202.00-865.674 | |

BACKGROUND INFORMATION:

This project included the rehabilitation of West Road between West Park Drive and the City limits (in this case, the City limits fall just west of the CSX Railroad crossing of West Road). The rehabilitation included a mill and overlay and the addition of a pavement interlayer for the western 700-feet of this section of road that is in poor condition. The eastern portion of the road was in better condition and only required some minor crack treatment. The project also included the rehabilitation of the existing concrete entrance to the Beck North Corporate Park.

The construction contract was awarded for this project at the March 9, 2015 City Council meeting to Asphalt Specialists, Inc., in the amount of \$153,511.05.


Engineering staff worked with the engineering consultant for this project, Spalding DeDecker & Associates, Inc., to review and verify the final contract payment amount of \$11,760.07 that is due the contractor (Final Pay Estimate No. 4, attached). The City Attorney reviewed the documentation and found it to be in an acceptable form (Beth Saarela's October 19, 2015 letter, attached).

There were three (3) approved change orders issued for this project resulting in a net decrease of \$1,509.61 to the construction contract, or 1.0% under the awarded amount. Most changes were a result of decreased quantities and balancing of originally projected amounts. The approved change orders resulted in a final contract price of \$152,001.44.

RECOMMENDED ACTION: Approval of the final payment to Asphalt Specialists, Inc. for the West Road Rehabilitation project in the amount of \$11,760.07, plus interest earned on retainage.

| | 1 | 2 | Y | N |
|------------------------|---|---|---|---|
| Mayor Gatt | | | | |
| Council Member Burke | | | | |
| Council Member Casey | | | | |
| Council Member Markham | | | | |

| | 1 | 2 | Y | N |
|-----------------------|---|---|---|---|
| Council Member Mutch | | | | |
| Council Member Staudt | | | | |
| Council Member Wrobel | | | | |

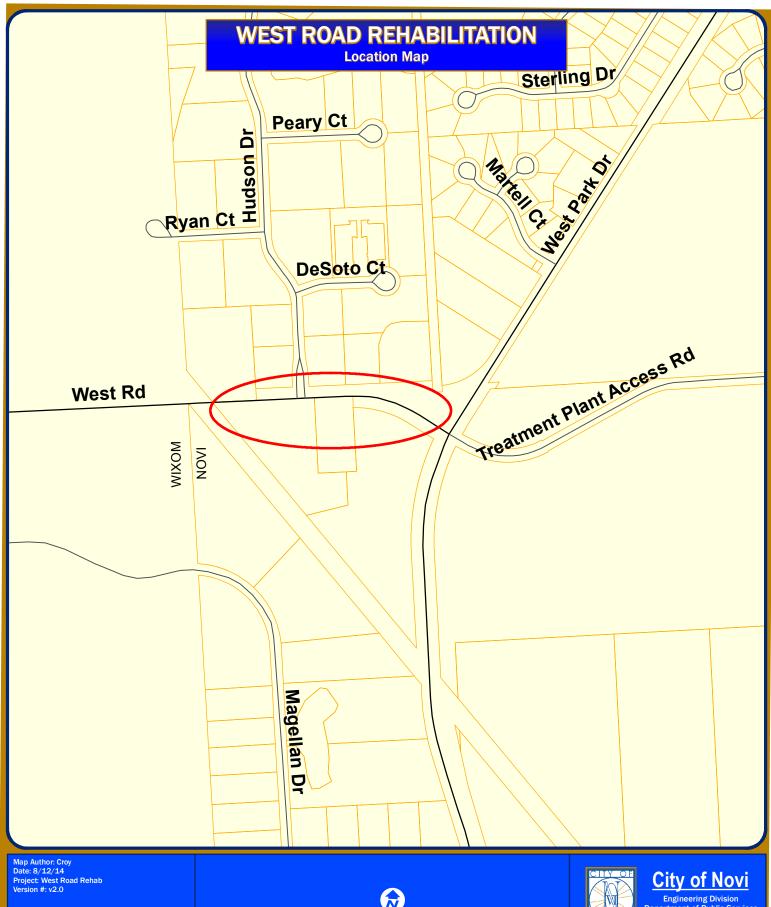

MAP INTERPRETATION NOTICE







Engineering Division
Department of Public Services
26300 Lee BeGole Drive
Novi, MI 48375
cityofnovi.org

WEST ROAD REHABILITATION – WEST PARK DRIVE TO CITY LIMITS (CSX RAILROAD)



West Road – Looking west from West Park Drive. Joint Repairs and long patches.



West Road – Looking east from City Limits (CSX Railroad). Full Asphalt Rehabilitation.



JOHNSON ROSATI SCHULTZ JOPPICH PC

27555 Executive Drive Suite 250 ~ Farmington Hills, Michigan 48331 Phone: 248.489.4100 | Fax: 248.489.1726

Elizabeth Kudla Saarela esaarela@jrsjlaw.com

www.jrsjlaw.com

October 19, 2015

Aaron Staup, Engineering Coordinator CITY OF NOVI Department of Public Services Field Services Complex 26300 Lee BeGole Drive Novi, MI 48375

Re: West Road Rehabilitation – Asphalt Specialists, Inc. Closing Documents

Dear Mr. Staup:

We have received and reviewed closing documents for the West Road Rehabilitation Project:

- 1. Application for Final Payment
- 2. Contractor's Sworn Statement
- 3. Waivers of Lien
- 4. Consent of Surety
- Maintenance and Guarantee Bond

Subject to approval of the Application for Final Payment by appropriate City staff, the closing documents appear to be in order.

We note that the General Contractor has not provided a Waiver of Lien and receipt of final payment in the amount should be conditioned upon receipt of this Waiver of Lien.

Aaron Staup, Construction Engineering Coordinator October 19, 2015 Page 2

Please feel free to contact me with any questions or concerns in regard to this matter.

Very truly yours,

JOHNSON ROSATI, SCHULTZ & JOPPICH, P.C.

Elizabeth Kudia Saarela

EKS

Enclosures

C: Maryanne Cornelius, Clerk (w/Enclosures)

Rob Hayes, Public Services Director (w/Enclosures)

Carl Johnson, Finance Director/Chief Financial Officer (w/Enclosures)

Brian Coburn, Engineering Manager (w/Enclosures)

Thomas R. Schultz, Esquire (w/Enclosures)

cityofnovi.org

CITY OF NOVI

Balance Due This Payment = \$ 11,760.07

PURCHASE ORDER NO. 94457 26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

APPLICATION FOR FINAL PAYMENT

PROJECT: V

West Road Rehabilitation

NOVI PROJECT NO.:

15-2302

PAYMENT NO .:

FINAL

OWNER:

City of Novi 45175 W. Ten Mile Road ENGINEER:

Spalding DeDecker & Associates 905 South Boulevard East

CONTRACTOR:

FROM:

Asphalt Specialists, Inc. 1780 E. Highwood

Novi, Michigan 48375

Rochester, Michigan 48037 (248) 844-5400

Pontiac, Michigan 48340 (248) 354-4570

CONTRACT AMOUNT FINAL COMPLETION DATES

DATES OF ESTIMATE

ORIGINAL:

\$153,511.05

ORIGINAL: REVISED:

June 18, 2015

_____ August 12, 2015

REVISED:

\$152,001.44

ACTUAL:

TO:

October 7, 2015

SECTION 1.

COST OF COMPLETED WORK TO DATE

| | SECTION 1. | | | | | | | | | OI OOMI EETED | | | | | | |
|------|------------------------------------|------|----------|------|------------|--------------|--------------------------|----|-----------|---------------|-------------|--------|---|---------------|--------------|------|
| Item | <u>GL# 202-202.00-865.674</u> | | c | ONTE | RACT ITEMS | (Original) | CONTRACT ITEMS (Revised) | | | | THIS PERIOD | | | TOTAL TO DATE | | |
| No. | Description of Item | Unit | Quantity | | ost/Unit | Total Amt | Quantity | (| Cost/Unit | Total Amt | Quantity | Amount | % | Quantity | Amount | % |
| .0 | Constr. Inspection "Crew Day" | CD | 16,00 | \$ | 640.00 | \$ 10,240.00 | 18.00 | \$ | 640.00 | \$ 11,520,00 | | | | 11.50 | \$ 7,360.00 | 64% |
| 1 | Bonds, Insurance & Mobilization | LS | 1.00 | \$ | 8,000.00 | \$ 8,000.00 | 1.00 | \$ | 8,000.00 | \$ 8,000.00 | | | | 1.00 | \$ 8,000.00 | 100% |
| 2 | Pre-Construction Audio-Visual | LS | 1.00 | \$ | 1,500.00 | \$ 1,500.00 | 0.00 | \$ | 1,500.00 | \$ - | | | | 0.00 | | |
| 3 | Soil Erosion Control Measures | LS | 1.00 | \$ | 2,500.00 | \$ 2,500.00 | 1.00 | \$ | 2,500.00 | \$ 2,500.00 | | | | 1.00 | \$ 2,500.00 | 100% |
| 4 | Maintaining Traffic | LS | 1.00 | \$ | 5,000.00 | \$ 5,000.00 | 1.00 | \$ | 5,000.00 | \$ 5,000.00 | | | | 1.00 | \$ 5,000.00 | 100% |
| 5 | Tree Protection Fencing | LF | 50.00 | \$ | 6.00 | \$ 300.00 | 0.00 | \$ | 6.00 | \$ - | | | | 0.00 | | |
| 6 | Pvmt Repair, Rem, Modified | SY | 267.00 | \$ | 16.00 | \$ 4,272.00 | 243,20 | \$ | 16.00 | \$ 3,891.20 | | | | 243.20 | \$ 3,891.20 | 100% |
| 7 | Remove Sidewalk | SY | 33.00 | \$ | 7.00 | \$ 231.00 | 37.00 | \$ | 7.00 | \$ 259.00 | | | | 37.00 | \$ 259.00 | 100% |
| 8 | Cold Mill HMA Pvmt, Special | SY | 3707.00 | \$ | 6.00 | \$ 22,242.00 | 4054.00 | \$ | 6.00 | \$ 24,324.00 | | | | 4054.00 | \$ 24,324.00 | 100% |
| 9 | Aggregate Base, 6-inch | SY | 42.00 | \$ | 17.00 | \$ 714.00 | 26.90 | \$ | 17.00 | \$ 457.30 | | | | 26.90 | \$ 457.30 | 100% |
| 10 | HMA, 5E1 | TON | 453.00 | \$ | 85.00 | \$ 38,505.00 | 462,00 | \$ | 85.00 | \$ 39,270.00 | | | | 462.00 | \$ 39,270.00 | 100% |
| 11_ | Interlayer | SY | 3374.00 | \$ | 4.40 | \$ 14,845.60 | 3287.44 | \$ | 4.40 | \$ 14,464.74 | | | | 3287.44 | \$ 14,464.74 | 100% |
| 12 | HMA Surface Repair | SY | 736.00 | \$ | 18.00 | \$ 13,248.00 | 345.00 | \$ | 18.00 | \$ 6,210.00 | | | | 345.00 | \$ 6,210.00 | 100% |
| 13_ | Pvmt Panel Replacement | SY | 242.00 | \$ | 60.00 | \$ 14,520.00 | 233,20 | \$ | 60.00 | \$ 13,992.00 | | | | 233.20 | \$ 13,992.00 | 100% |
| 14 | Longitudinal Joint Repair | LF | 63.00 | \$ | 82.00 | \$ 5,166.00 | 34.00 | \$ | 82.00 | \$ 2,788.00 | | | | 34.00 | \$ 2,788.00 | 100% |
| 15 | Transverse Joint Repair | LF | 40.00 | \$ | 95.00 | \$ 3,800.00 | 16.00 | \$ | 95.00 | \$ 1,520.00 | | | | 16.00 | \$ 1,520.00 | 100% |
| 16 | ADA Ramp, Conc, 6-inch | SF | 298.00 | \$ | 10.00 | \$ 2,980.00 | 242,00 | \$ | 10.00 | \$ 2,420.00 | | | | 242.00 | \$ 2,420.00 | 100% |
| 17_ | ADA Detectable Warning Plate | SF | 48.00 | \$ | 18.00 | \$ 864.00 | 48.00 | \$ | 18.00 | \$ 864.00 | | | | 48.00 | \$ 864.00 | 100% |
| 18 | Joint and Crack Cleanout, Modified | LF | 150.00 | \$ | 5.00 | \$ 750.00 | 140.00 | \$ | 5.00 | \$ 700.00 | | | | 140.00 | \$ 700.00 | 100% |
| 19 | Pvmt Mrkg, White, 4-inch | LF | 274.00 | \$ | 0.60 | \$ 164.40 | 2390.00 | \$ | 0.60 | \$ 1,434.00 | | | | 2390.00 | \$ 1,434.00 | 100% |
| 20 | Pvmt Mrkg, White, 6-inch | LF | 1659.00 | \$ | 0.75 | \$ 1,244.25 | 0.00 | \$ | 0.75 | \$ - | | | | 0.00 | | |
| 21 | Pvmt Mrkg, Yellow, 4-inch | LF | 2538.00 | \$ | 0.60 | \$ 1,522.80 | 3722.00 | \$ | 0.60 | \$ 2,233.20 | | | | 3722.00 | \$ 2,233.20 | 100% |
| 22 | Pvmt Mrkg, Yellow, 12-inch | LF | 90.00 | \$ | 4.00 | \$ 360.00 | 52.00 | \$ | 4.00 | \$ 208.00 | | | | 52.00 | \$ 208.00 | 100% |
| 23 | Pvmt Mrkg, Stop Bar, 24-inch | LF | 50,00 | \$ | 9.00 | \$ 450.00 | 46,00 | \$ | 9.00 | \$ 414.00 | | | | 46.00 | \$ 414.00 | 100% |
| 24 | Pvmt Mrkg, Lt-Turn Arrow Symb | EA | 2.00 | \$ | 150.00 | \$ 300.00 | 2.00 | \$ | 150.00 | \$ 300.00 | | | | 2.00 | \$ 300.00 | 100% |



26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

APPLICATION FOR FINAL PAYMENT

PROJECT: West Road Rehabilitation

NOVI PROJECT NO.:

15-2302

PAYMENT NO.:

FINAL

| | SECTION 1. | , | | | | | | | COST | OF (| COMPLETED | WORK TO | DATE | | | | | |
|----------|----------------------------------|----------|--|--------------|-----------|------------|--|--------------|------------|--|---|-------------|-------------|--------------|--|--|---------------|------|
| Item | GL# 202-202.00-865.674 | | | CONTRACT ITE | //S (Orig | inal) | | CONT | RACT ITEMS | (Revis | sed) | | THIS PERIOD | | | 1 | TOTAL TO DATE | |
| No. | Description of Item | Unit | Quantity | Cost/Unit | | Total Amt | Quantity | c | Cost/Unit | | Total Amt | Quantity | Amount | % | Quantity | | Amount | % |
| 25 | Pvmt Mrkg, "ONLY" Symbol | EA | 2.00 | \$ 150.0 | | 300,00 | 2.00 | \$ | 150.00 | | 300,00 | | | | 2.00 | \$ | 300.00 | 100% |
| 26 | Pvmt Mrkg, Rt-Turn Arrow Symb | EA | 3.00 | \$ 150.0 | 0 \$ | 450.00 | 3.00 | \$ | 150.00 | | 450.00 | | | | 3.00 | \$ | 450.00 | 100% |
| 27 | Pvmt Mrkg, Railroad Symbol | EA | 1.00 | \$ 350.0 | 0 \$ | 350.00 | 1.00 | \$ | 350.00 | \$ | 350.00 | | | | 1.00 | \$ | 350.00 | 100% |
| 28 | Restoration | LS | 1.00 | \$ 5,000.0 | 0 \$ | 5,000.00 | 1.00 | \$ | | \$ | 5,000.00 | | | | 1.00 | \$ | 5,000.00 | 100% |
| 29 | Railroad Flagging at Grade X-ing | LS | 1.00 | \$ 3,932.0 | 0 \$ | 3,932.00 | 1.00 | \$ | 3,932.00 | \$ | 3,932.00 | | | <u> </u> | 1.00 | \$ | 3,932.00 | 100% |
| | | | | <u> </u> | _ | | | | | | | | | | | <u> </u> | | |
| | | <u> </u> | | <u> </u> | | | | ┼ | **** | | | | | | | ļ | | |
| | | | | | - | | | | | | | | | | | <u> </u> | | |
| | | | | | | | | | | | | | | | | - | | |
| | | | | | _ | | | + | | | | | | | - | | | |
| | | - | | | _ | | _ | - | | | | | | | - | | | |
| | | - | | | | | _ | + | | | | | | - | + | | | |
| | | - | | | | | | + | | | | | | - | + | - | | |
| | | | | | | | | - | | | | | | | | 1 | | |
| | | | | | - | | | | | | | | | - | | | | |
| | | - | ļ | - | - | | | | | | | | | | | | | |
| | - | | | | - | | | + | | | | | | | + | + | | |
| | | + | | - | _ | | | + | | | | | | | | | | |
| | | | 1 | + | | | | + | | | | | | 1 | +- | | | |
| <u> </u> | | | | + | | | · | | | | | | | | | | | |
| | | | | 1 | | | | | | | | | | 1 | | + | - " | |
| | | | | + | - | | <u> </u> | | | | | | | | + | | | |
| | | | | | _ | | | 1 | | | | | | | +- | | | |
| | | 1 | | | | | | + | | | | | | 1 | + | - | | |
| | | | | | \vdash | | | \top | | - | | | | | + | + | | |
| | | 1 | | - | | | | | | | *************************************** | | | + | | 1 | | |
| | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | <u> </u> | | | | |
| _ | | | - | | | | | | | | | | | | | | | |
| | 1 - 1 | | | | | | | | | T | | | | | | | | i |
| | | 1 | | | | | | | | i – | | | | | | | | |
| | | | i | 1 | | | | 1 | | 1 | | | | | | 1 | | |
| | | | | | | | | | | | | | | | | 1 | **** | |
| | | | | 1 | | | | | | 1 | | | | | | 1 | | |
| | TOTAL FROM THIS SHEE | T T | | | \$ | 10,032.00 | | | | \$ | 10,032.00 | | \$ - | | | \$ | 10,032.00 | 1 |
| | TOTAL FROM OTHER SHEE | | | | \$ | 143,479.05 | | | | \$ | 131,249.44 | | \$ - | | | \$ | 131,249.44 | |
| | | | | | \$ | | | | | \$ | | | | | | • | | 100% |
| | SUBTOTA | L | | | \$ | 153,511.05 | | | | \$ | 141,281.44 | | \$ - | | | \$ | 141,281.44 | 100% |



26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

APPLICATION FOR FINAL PAYMENT

PROJECT: West Road Rehabilitation

NOVI PROJECT NO .:

15-2302

PAYMENT NO .:

FINAL

NEW CONTRACT ITEMS

| | SECTION 1. | | | | | COST | OF C | OMPLETED | WORK TO | DATE | | | | 1.0 | |
|------|----------------------------|------|----------|---------------|----------|--------------|---------------|------------|----------|-------------|---|---|-----|-------------|------|
| Item | | | | | | NEW CONTRAC | DNTRACT ITEMS | | | THIS PERIOD | | | тот | TAL TO DATE | |
| No. | Description of Item | Unit | Division | GL# | Quantity | Cost/Unit | | Total Amt | Quantity | Amount | % | Quantity | A | mount | % |
| 30 | | | 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | - | |
| 31 | Parking lot Asphalt Repair | LS | 0 | 0 | 1.00 | \$ 10,720.00 | \$ | 10,720.00 | | | | 1.00 | \$ | 10,720.00 | 100% |
| 32 | | | 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | - | |
| 33 | | | 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | - | |
| 34 | | | 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | - | |
| 35 | | | 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | | · |
| 36 | | | 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | - | |
| 37 | | | 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | - | |
| 38 | | | - 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | | |
| 39 | | | 0 | 0 | 0.00 | \$ | \$ | | | | | 0.00 | \$ | - | |
| 40 | | | 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | - | |
| 41 | | | 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | - | |
| 42 | | | 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | - | |
| 43 | | | 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | - | |
| 44 | | | 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | - | į |
| 45 | | | 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | - | |
| 46 | | | 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | - | |
| 47 | | | 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | - | |
| 48 | · | | 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | - | |
| 49 | | | 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | - | |
| 50 | | | 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | - | |
| 51 | | | 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | - | |
| 52 | | | 0 | 0 | 0.00 | \$ - | \$ | _ | | | | 0.00 | \$ | _ | |
| 53 | | | 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | - | |
| 54 | | | 0 | O | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | _ | |
| 55 | | | 0 | 0 | 0.00 | \$ - | \$ | - | | | | 0.00 | \$ | - | |
| 56 | | | 0 | 0 | 0.00 | \$ - | \$ | | | | | 0.00 | \$ | - | |
| 57 | | | 0 | 0 | 0.00 | \$ - | \$ | _ | | | | 0.00 | \$ | - | |
| | TOTAL FROM THIS SHEE | Т | | | | | \$ | 10,720.00 | | \$ - | | ,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,, | \$ | 10,720.00 | |
| | TOTAL FROM OTHER SHEET | rs . | | \$ 153,511.05 | | | \$ | 141,281.44 | | \$ - | | | \$ | 141,281.44 | |
| | GRAND TOTA | \L | | \$ 153,511.05 | | | \$ | 152,001.44 | | \$ - | | | \$ | 152,001.44 | 100% |



PURCHASE ORDER NO. 94457 26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

| Section 2. | | | | | | | |
|--|---------------------------|----------------|-----------------|---|-----------|---------------------|-------|
| | 1 | APPLICATION FO | OR FINA | AL PAYMENT | | | |
| PROJECT: West Road Rehabilitation | NOVI PROJE | | | | PAYM | ENT NO.: | FINAL |
| Original Contract Amount: | \$ | 153,511.05 | | CHANGE O | RDERS | | |
| Change Orders: | \$ | (1,509.61) | <u>No.</u> 1 | <u>Date</u> June 1, 2015 | \$ | Amount 10,720.00 | |
| Adjusted Contract Amount to Date: | \$ | 152,001.44 | 2 | July 27, 2015 August 6, 2015 | \$ | (12,229.61) | |
| Total Cost of Work Performed to Date: | \$ | 152,001.44 | | | \$ | - | |
| MINUS Retainage: MINUS Inspection "Crew Days": To Date This Pay | 0% \$ 11.50 \$ 0.00 | - | | | \$ | - - | |
| Net Amt. Earned of Contract and Extra Work to Date: | \$ | 152,001.44 | | | \$ \$ | - - | |
| MINUS L.D.'s: # of days over = \$ amount/day = \$600 | \$ | - | | | \$ \$ | | |
| Subtotal: | \$ | 152,001.44 | | | \$ | ** | |
| ADD Incentive "Crew Days", if under: | \$ | 4,160.00 | | тот | AL: \$ | (1,509.61) | |
| Subtotal: | \$ | 156,161.44 | | | | | |
| MINUS Amount of Previous Payments: 1 \$ 34,122.15 2 \$ 90,464.74 | \$ | 144,401.37 | | | | | |
| 3 \$ 19,814.48 • | | | | Inspection "Crew Days" All Additional "Crew Days" pe | | | |
| 5 \$ | | | | Total Inspection "Crew Days pe | | 18.00 | |
| 6 \$ - | | | | Inspection "Crew Days" Us | | 11.50 | |
| 7 \$ - 8 \$ - | | | | Inspection "Crew Days" Re | emaining: | 6.50 | |
| 9 \$ - | | | | | | | |
| 10 \$ - | | | | | | | |
| BALANCE DUE THIS PAYMENT: | \$ | 11,760.07 | | | | | |

\$4160 From 202-202.00-805.674



26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

Brian Coburn, PE., Engineering Senior Manager

Section 3. APPLICATION FOR FINAL PAYMENT PROJECT: West Road Rehabilitation NOVI PROJECT NO .: 15-2302 PAYMENT NO .: FINAL The undersigned CONTRACTOR certifies that: (1) Any previous progress payments received from Payment of the above AMOUNT DUE THIS APPLICATION OWNER on amount of Work done under the Contract referred to above have been applied to discharge is recommended. in full all obligations of CONTRACTOR incurred in connection with Work covered by prior Applications for Payment; (2) title to all Work, materials, and equipment incorporated in said Work of otherwise CITY OF NOVI listed in or covered by this Application for Payment will pass to OWNER at time of payment free and clear of all leins, claims, security interest, and encumberences (except such as are covered by Bond acceptable to OWNER indemnifying OWNER against any such lein, claim security interest, or Aaron J. Staup, Construction Engineering Coordinator encumberence); and (3) all Work covered by this Application for Payment is in accordance with Ву: the Contract Documents and not defective as that term is defined in the Contract Documents. Dated: Asphalt Specialists, Inc. Date: Contractor Company

Spalding DeDecker&Associates

Contractor Authorized Signature

Print Name

Consultant Firm

By:

Elleco Let Day

Date:

All Full Unconditional Waivers of lien have been received from each subcontractor and/or supplier, reviewed and approved by the Consultant. Also, attached to this Final Payment is a copy of the Contractor's Sworn Statement, Consent of Surety, and a new Maintenance and Guarantee Bond (if the amount is greater than the final contract price) or a Maintenance Bond Rider covering the difference between the final contract price and the awarded amount.

By:

Dated:

| CONSENT OF SURETY COMPANY TO FINAL PAYMENT AIA DOCUMENT G707 | Owner Architect Contractor Surety Other | X | Bond No. HGMW-10-177-0539 |
|---|---|---------------------------|--|
| PROJECT: West Road Rehabilitation ASI #15 (name; address) | -035 | | |
| TO: (Owner) | AR | CHITE | CT'S PROJECT NO: |
| City of Novi 45175 W. Ten Mile Road Novi, MI 48375-3024 | COI | NTRAC | T FOR: |
| | COI | NTRAC | T DATE: |
| CONTRACTOR: Asphalt Specialists Inc. 1780 E. Highwood Pontiac, MI 48340 | | | |
| In accordance with the provisions of the Contract be Hudson Insurance Company 100 William Street, 5th Floor New York, New York 10038 | etween the Owne | er and th | e Contractor as indicated above, the |
| on bond of there insert name and address of Contractor) Asphalt Specialists Inc. 1780 E. Highwood Pontiac, Michigan 48340 | | | ,CONTRACTOR, |
| hereby approves of the final payment to the Contract relieve the Surety Company of any of its obligations City of Novi 45175 W. Ten Mile Road Novi, Michigan 48375-3024 | | | |
| as set forth in the said Surety Company's bond. | | | |
| IN WITNESS WHEREOF, the Surety Company has hereunto set its hand this | 23rd (| lay of | September, 2015 |
| | | y Comp son Insu WWW | any arance Company Allan |
| | Signat | ture of Aut | horized Representative |
| Attest: (Seal): | Title | Kathle | en M. Irelan - Attorney-In-Fact |
| NOTE: This form is to be used as a companion document to AIA DEBTS AND CLAIMS, Current Edition | DOCUMENT (170 | 6, CONTI | ACTOR'S AFFIDAVIT OF PAYMENT OF |
| AIA DOCUMENT G707-CONSENT OF SURETY COMPANY PAGE \$31970-THE AMERICAN INSTITUTE OF ARCHITECTS, 1735 | | | and the second of the second o |



POWER OF ATTORNEY

KNOW ALL MEN BY THESE PRESENTS: That HUDSON INSURANCE COMPANY, a corporation of the State of Delaware, with offices at 100 William Street, New York, New York, 100038, has made, constituted and appointed, and by these presents, does make, constitute and appoint

Alan P. Chandler, Robert Trobec, Jeffrey A. Chandler, Kathleen M. Irelan, Ian J. Donald, Jennifer A. Gareffa of the State of Michigan

its true and lawful Attorney(s)-in-Pact, at New York City in the State of New York, each of them alone to have full power to act without the other or others, to make, execute and deliver on its behalf, as Surety, bid bonds for any and all purposes.

Such bid bonds, when duly executed by said Attorney(s)-in-Fact, shall be binding upon said Company as fully and to the same extent as if signed by the President of said Company under its corporate seal attested by its Secretary.

In Witness Whereof, HUDSON INSURANCE COMPANY has caused these presents to be of its Senior Vice President the reunto duly , on this 4th day of February, 20 14 at New York, New York. HUDSON INSURANCE COMPANY 1918 Dina Daskalalds, Corporate Secretary STATE OF NEW YORK COUNTY OF NEW YORK On the 4th day of February before me personally came Michael P. Gleeson to me known, who being by me duly sworn did , 20 14 denose and say that he is a Senior Vice President of HUDSON INSURANCE COMPANY, the Company described herein and which executed the above instrument, that he knows the seal of said Company, that the seal affixed to said instrument is the corporate spal of said Company, that it was so affixed by order of the Board of of suid Court Directors of said Company, and that he signed his name thereto by like order. AMCIA T. MOKINNEY Notary Public, State of New York No. 01MC6212495 KO11/C6212485 Qualified in New York County Commission Expires October 13, 2017 CERTIFICATION SS.

The undersigned Dina Daskalakis hereby certifies:

THAT the original resolution, of which the following is a true and correct copy, was duly adopted by unanimous written consent of the Board of Directors of Hudson Insurance Company dated July 27th, 2007, and has not since been revoked, amended or modified:

"RESOLVED, that the President, the Executive Vice Presidents, the Senior Vice Presidents and the Vice Presidents shall have the authority and discretion, to appoint such agent or agents, or attorney or attorneys-in-fact, for the purpose of carrying on this Company's surely business, and to empower such agent or agents, or attorneys-in-fact, to execute and deliver, under this Company's seal or otherwise, bonds obligations, and recognizances, whether made by this Company as surely thereon or otherwise, indemnity contracts, contracts and certificates, and any and all other contracts and undertaking made in the course of this Company's surely business, and renewals, extensions, agreements, waivers, consents or stipulations regarding undertakings so made; and

FURTHER RESOVLED, that the signature of any such Officer of the Company and the Company's seal may be affixed by facsimile to any power of attorney or certification given for the execution of any bond, undertaking, recognizance, contract of indemnity or other written obligation in the nature thereof or related thereto, such signature and seal when so used whether heretofore or hereafter, being hereby adopted by the Company as the original signature of such officer and the original seal of the Company, to be valid and binding upon the Company with the same force and effect as though manually affixed."

THAT the above and foregoing is a full, true and correct copy of Power of Attorney issued by said Company, and of the whole of the original and that the said Power of Attorney is still in full force and effect and has not been revoked, and furthermore that the Resolution of the Board of Directors, set forth in the said Power of Attorney is now in force.

Vitness the hand of the undersigned and the seal of said Company this 23rd day of September 2015.

SEAL 1918

By May Washinkis, Corporate Secretary

Form Bid 8 2010 (v3)

SWORN STATEMENT

STATE OF MICHIGAN COUNTY OF OAKLAND) SS

Diane Palazzola, being duly sworn, deposes and says:

That he or she makes the Sworn Statement on behalf of Asphalt Specialists, Inc., who is the (subcontractor) for an improvement to the following described real property situated in Oakland County, Michigan, and described as follows: (Insert legal description from Notice of Commencement)

West Road Rehabilitation - ASI #15035

That the following is a statement of each subcontractor and supplier and laborer, for which laborer the payment of wages or fringe benefits and withholdings is due but unpaid, with whom the (subcontractor) has (subcontracted) for performance under the contract with the owner or lessee thereof, and that the amounts due to the persons as of the date thereof are correctly and fully set forth

opposite their names, as follows:

| Name of Subcontractor, supplier, or laborer | Type of improvement furnished | Total contract price | Amount already paid | Amount currently owing |
|---|-------------------------------|----------------------|---------------------|------------------------|
| Cadillac | Asphalt | 28,180.39 | 28,180.39 | 0.00 |
| Cipparone | Concrete | 31,580.70 | 31,580.70 | 0.00 |
| Road Fabric | Road fabric | 14,984.22 | 14,984.22 | 0.00 |
| P.K. Contracting | Pavement marking | 6,623.78 | 6,623.78 | 0.00 |
| All labor, fringes, payroll taxes, and other payroll obligations paid in full | | | | |
| TOTALS | | 81,369.09 | 81,369.09 | 0.0 |

(Some columns are not applicable to all persons listed)

That the contractor has not procured material from, or subcontracted with, any person other than those set forth above and owes no money for the improvement.

Deponent further says that he or she makes the foregoing statement as the (subcontractor) or as Agent of the (subcontractor) for the purpose of representing to the owner or lessee of the above-described premises and his or her agents that the above-described property is free from claims of contraction liens, or the possibility of construction liens, except as specifically set forth above and except for claims of construction liens by laborers which may be provided pursuant to section 109 of the construction lien act, Act No. 497 of the Public Acts of 1980, as amended, being section 570.1109 of the Michigan Complied Laws.

WARNING TO OWNER: AN OWNER OR LESSEE OF THE ABOVE-DESCRIBED PROPERTY MAY NOT RELY ON THIS SWORN STATEMENT TO AVOID THE CLAIM OF A SUBCONTRACTOR, SUPPLIER, OR LABORER WHO HAS PROVIDED A NOTICE OF FURNISHING OR A LABORER WHO MAY PROVIDE A NOTICE OF FURNISHING PURSUANT TO SECTION 109 OF THE CONSTRUCTION LIEN ACT TO THE DESIGNEE OR THE OWNER OR LESSEE IF THE DESIGNEE IS NOT NAMED OR HAS DIED.

Diane Palazzola – Credit Manager

WARNING TO DEPONENT: A PERSON, WHO WITH INTENT TO DEFRAUD, GIVES A FALSE SWORN STATEMENT IS SUBJECT TO CRIMINAL PENALTIES AS PROVIDED IN SECTION 110 OF THE CONSTRUCTION LIEN ACT, ACT NO. 497 OF THE PUBLIC ACTS OF 1980, AS AMENDED, BEING SECTION 570.2220 OF THE MICHIGAN COMPLIED LAWS.

Subscribed and sworn to before me this 6th day of October, 2015

Notary Public, Oakland County Michigan
MCWU31, 2021

JULIE P. HOULIHAN NOTARY PUBLIC - STATE OF MICHIGAN COUNTY OF OAKLAND

My Commission Expires March 31, 2021 Acting in the County of <u>ウ</u>ィビネルの

| I/we have a contract with _ | Asphalt Specialist Inc. |
|---|---|
| _ | (Other contracting party) |
| to provide | Material Supplies |
| for the improvement to the property | described as |
| | West Road Rehab |
| | ASI Job #15-035 |
| having been fully paid and satisfied property are hereby waived and rele | , all my/our construction lien rights against such eased. |
| notice of furnishing from me/one of the owner, lessee, or designee has n the owner, lessee, or designee may n | y or the owner's or lessee's designee has received a f us or if I/we are not required to provide one, and not received this waiver directly from me/one of us, not rely upon it without contacting me/one of us, ersonally, to verify that it is authentic. |
| | <u>Cadillac Asphalt LLC</u> |
| | By: Kathlean & Pullips (Signature of lien claimant) |
| | |
| | Printed Name KATHIEER G. Phillips |
| | Title CRadit Manager |
| | Address: 2575 S. Haggerty Rd. Suite 100 |
| | Canton, MI 48188 |
| | Telephone: 586-203-2616 |

DO NOT SIGN BLANK OR INCOMPLETE FORMS. RETAIN A COPY.

Signed on: 10-7-15 (Date)

| I/we have a contract with | Asphalt Specialist Inc. |
|--|--|
| , | (Other contracting party) |
| | , 01 |
| to provide | Subcontractor Work |
| | |
| for the improvement to the propert | v described as |
| And the contract of the contra | |
| | West Road Rehab |
| ų. | |
| • | ASI Job #15-035 |
| V. 2 | |
| having been fully paid and satisfied property are hereby waived and rel | f, all my/our construction lien rights against such eased. |
| notice of furnishing from me/one o the owner, lessee, or designee has the owner, tessee, or designee may | ty or the owner's or lessee's designee has received a f us or if I/we are not required to provide one, and not received this waiver directly from me/one of us, not rely upon it without contacting me/one of us, ersonally, to verify that it is authentic. |
| | Printed Name (Signature of lien claimant) Title Virguesal S Address: 29200 Southfield Rd. Suite 100 |
| Ç. | |
| | Southfield, MI 48076 |
| ,,, | |
| | Telephone: 248-424-3888 |
| Signed on: 10/13/15 | |

DO NOT SIGN BLANK OR INCOMPLETE FORMS. RETAIN A COPY.

| I/we have a contract with _ | Asphalt Specialist Inc. |
|---|---|
| | (Other contracting party) |
| to provide | Subcontractor Work |
| for the improvement to the property | y described as |
| | West Road Rehab |
| | ASI Job #15-035 |
| having been fully paid and satisfied property are hereby waived and rele | l, all my/our construction lien rights against such eased. |
| notice of furnishing from me/one of the owner, lessee, or designee has r the owner, lessee, or designee may | y or the owner's or lessee's designee has received a f us or if I/we are not required to provide one, and not received this waiver directly from me/one of us, not rely upon it without contacting me/one of us, ersonally, to verify that it is authentic. Road Fabrics Inc. By: (Signature of lien claimant) Printed Name (Signature of lien claimant) Title M(M) Address: P.O. Box 87380 Carol Stream, IL 60188 |
| | m 1 1 (00 000 0111 |
| | Telephone: 630-293-3111 |
| Signed on: 10-12-15 (Date) | |

DO NOT SIGN BLANK OR INCOMPLETE FORMS. RETAIN A COPY.

| I/we have a contract with | Asphalt Specialist Inc. | |
|---|--|--|
| | (Other contracting party) | |
| to provide | Subcontractor Work | |
| for the improvement to the property described as | | |
| | West Road Rehab | |
| | ASI Job #15-035 | |
| having been fully paid and satisfied property are hereby waived and rel | i, all my/our construction lien rights against such eased. | |
| notice of furnishing from me/one of the owner, lessee, or designee has a the owner, lessee, or designee may | ty or the owner's or lessee's designee has received a f us or if I/we are not required to provide one, and not received this waiver directly from me/one of us, not rely upon it without contacting me/one of us, ersonally, to verify that it is authentic. | |
| | P.K. Contracting, Inc. | |
| | By: Luith Mr. | |
| | (Signature of lien claimant) Printed Name Kristen McDonald, Agent | |
| | Title | |
| | Address: 1965 Barrett Drive Troy, MI 48084 | |
| | Telephone: 248-362-2130 | |
| Signed on: $\frac{10/7/15}{\text{(Date)}}$ | | |

DO NOT SIGN BLANK OR INCOMPLETE FORMS. RETAIN A COPY.

MAINTENANCE AND GUARANTEE BOND

| KNOW ALL MEN BY THESE PRESENTS, that weAsphalt Specialists, Inc. | | | |
|---|--|--|--|
| hereinafter called the "Principal", and Hudson Insurance Company | | | |
| | | | |
| hereinafter called the "Surety," are held and firmly bound unto | | | |
| CITY OF NOVI, MICHIGAN | | | |
| Hereinafter called the "OWNER," as Obligee, for the just and full sum of One Hundred Fifty Three, Five Hundred Eleven and 05/100s Dollars (\$ 153,511.05) for the payment whereof, well and truly to be made, we bind ourselves, our heirs, executors, administrators, successors, and assigns, jointly and severally, firmly by these presents. | | | |
| WHEREAS, the above named Principal was awarded a Contract by the OWNER dated theday of, for the construction of | | | |
| West Road Rehabilitation | | | |
| AND WHEREAS, this Contract was awarded upon the express condition that the Principal would furnish a one (1) year Maintenance Bond from the date of formal acceptance by the City Council to repair or replace any deficiencies in Labor or Material; | | | |
| AND WHEREAS, the Principal warrants the workmanship and all materials used in the construction installation, and completion of said project to be of good quality and constructed and completed in a workmanlike manner in accordance with the standards, specifications and requirements of the said job; | | | |
| NOW, THEREFORE, the condition of this obligation is such that if the above Principal shall replace such defective material and shall repair all defects due to defective workmanship and/or materials that shall occur on or before one (1) year of final acceptance by OWNER through resolution of the City Council, then this obligation shall be void, otherwise to be and remain in full force, effect and virtue. | | | |
| If the Principal does not correct defects reported in writing by the OWNER to the Principal and Surety by repair or replacement as directed by the OWNER within the time required, which shall not be less than seven (7) days from service of the notice, the OWNER shall have the right to perform or secure the performance of the corrections, with all costs and expenses in doing so, including an administrative fee equal to twenty-five percent (25%) of the repair costs, charged to and to be received from the Principal or Surety. | | | |
| Emergency repairs that are necessary to protect life and property may be undertaken by the OWNER immediately and without advance notice to the Principal and Surety, with the cost and expense of the repair, plus the administrative fee, to be charged to and received from the Principal and Surety. | | | |



West Road Rehabilitation Page 30

Any repairs the OWNER may perform as provided in this Bond may be by OWNER employees, agents, or independent CONTRACTORS. The OWNER shall not be required to utilize competitive bidding unless otherwise required by applicable law, with labor cost and expense charges when OWNER employees are utilized to be based on the hourly cost to the OWNER of the employee(s) performing the repair.

It is further condition of this Bond that the Principal and Surety shall fully indemnify, defend, and hold the OWNER, its agents and other working on the OWNER'S behalf, harmless from all claims for damages or injuries to persons or property arising from or related to defects in work or materials, the correction of which are covered and guaranteed by this Bond, including claims arising under the worker's compensation laws of the State of Michigan.

| | Signed and Sealed this 19th | day ofMarch |
|-------------------------|-----------------------------|---|
| In the Presence | ce of: | |
| WITNESS WITNESS | Me Bonenshi | ASPHALT SPECIALISTS, INC. Principal BRUCE I SENER, Vice. Thesined |
| Meagan Kress | | Title Hudson Insurance Company Surety Title Jennifer A Gareffa, Attorney-In-Fact 100 William Street. 5th Floor |
| HGMW-10-177 Bond No. | -0539 | Address of Surety New York, NY 10038 City Zip Code |
| CITY OF | | • |



February 2015
