NOV cityofnovi.org

CITY of NOVI CITY COUNCIL

Agenda Item F August 25, 2014

SUBJECT: Approval of the final payment to Fonson, Inc. for the Novi Road Pathway Project (Nine Mile Road to Ten Mile Road) and 2013 ADA Compliance Program in the amount of \$17,620.49.

SUBMITTING DEPARTMENT: Department of Public Services, Engineering Division

CITY MANAGER APPROVAL:

EXPENDITURE REQUIRED	\$17,620.49						
AMOUNT BUDGETED	\$19,000 Novi Road Pathway						
	\$70,356 ADA Compliance Program						
	\$89,356 TOTAL						
LINE ITEM NUMBER	204-204.00-974.431 Novi Road Pathway						
	204-204.00-805.003 ADA Compliance Program						

BACKGROUND INFORMATION:

This project included the construction of approximately 1,800 feet of 6-foot wide concrete pathway to fill three gaps along the west side of Novi Road between Nine Mile Road and Ten Mile Road, identified as Segment 92 in the *Pathway and Sidewalk Prioritization Analysis and Process* report. A location map has been included for reference. Obtaining four permanent easements and four temporary easements was required to facilitate the construction and maintenance of this pathway.

This project also included the second construction season for the Americans with Disabilities Act (ADA) Compliance Implementation Program as recommended by the ADA Compliance Transition Plan adopted in March 2011 and funded in the 2012-13 fiscal year CIP. This year's ADA Compliance project targeted sidewalks along Novi Road adjacent to the pathway project. A location map of these facilities is also attached.

The construction contract was awarded for this project at the August 26, 2013 City Council meeting to Fonson, Inc. in the amount of \$179,186.87. Engineering staff worked with the engineering consultant for this project, Spalding DeDecker & Associates, Inc., to review and verify the final contract payment amount of \$17,620.49 that is due the contractor (Final Pay Estimate No. 2, attached). The City Attorney reviewed the documentation and found it to be in an acceptable form (Beth Saarela's August 7, 2014 letter, attached).


There were two (2) change orders issued for this project. Change Order No. 1 involved adjusting quantities to add storm sewer piping along Novi Road and decrease actual placed quantities from what was estimated, in the decreased amount of \$1,708.99. Change Order No. 2 simply balanced all remaining contract items, in the decreased amount of \$704.00. The approved change orders resulted in a final contract price of \$176,773.88.

RECOMMENDED ACTION: Approval of the final payment to Fonson, Inc. for the Novi Road Pathway Project (Nine Mile Road to Ten Mile Road) and 2013 ADA Compliance Program in the amount of \$17,620.49.

	1	2	Υ	N
Mayor Gatt				
Mayor Pro Tem Staudt				
Council Member Casey				
Council Member Fischer				

	1	2	Υ	N
Council Member Markham				
Council Member Mutch				
Council Member Wrobel				



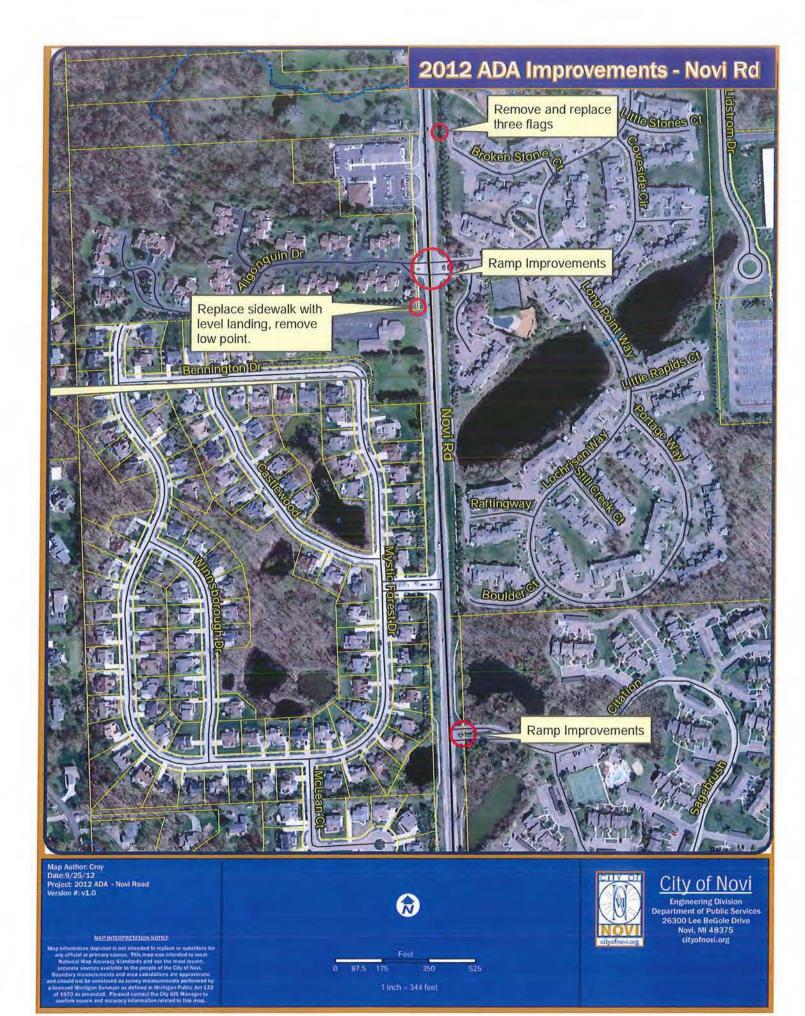



JOHNSON ROSATI SCHULTZ JOPPICH PC

27555 Executive Drive Suite 250 ~ Farmington Hills, Michigan 48331 Phone: 248.489.4100 | Fax: 248.489.1726

Elizabeth Kudla Saarela esaarela@jrsjlaw.com

www.johnsonrosati.com

August 7, 2014

Aaron Staup, Construction Engineering Coordinator City of Novi -- Department of Public Services Field Services Complex 26300 Lee BeGole Drive Novi, MI 48375

> RE: Novi Road Pathway Nine Mile to Ten Mile and 2013 ADA Compliance Program Fonson, Inc.

Dear Mr. Staup:

We have received and reviewed the following closing documents for the Novi Road Pathway Nine Mile to Ten Mile and 2013 ADA Compliance Program:

- Application for Final Payment
- Contractor's Sworn Statement
- Waivers of Lien Consent of Surety

Subject to approval of the Application for Final Payment by appropriate City staff, the closing documents appear to be in order.

If you have any questions regarding the above, please do not hesitate to contact me.

Very truly yours,

JOHNSON, ROSATI, SCHULTZ & JOPPICH, P.C.

Kudla Saarela

EĶS Enclosures

FARMINGTON HILLS | LANSING | MARSHALL

Elizabeth

Aaron Staup, Construction Engineering Coordinator August 7, 2014 Page 2

C: Maryanne Cornelius, Clerk (w/Enclosures)
Victor Cardenas, Interim City Manager (w/Enclosures)
Rob Hayes, DPS Director (w/Enclosures)
Carl Johnson, Finance Director (w/Enclosures)
Jessica Dorey, Deputy Finance Director (w/Enclosures)
Brian Coburn, Engineering Manager (w/Enclosures)
Ted Meadows, Spalding DeDecker (w/Enclosures)
Thomas R. Schultz, Esquire (w/Enclosures)



CONTRACT AMOUNT

CITY OF NOVI

26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

DATES OF ESTIMATE

APPLICATION FOR FINAL PAYMENT

PROJECT: 2013 Novi Road Pathway/ADA NOVI PROJECT NO .: 13-5001 PAYMENT NO .: FINAL

OWNER: City of Novi ENGINEER: Spalding DeDecker & Associates, Inc. CONTRACTOR: Fonson, Inc.

45175 W. Ten Mile Road 905 South Boulevard East 7644 Whitmore Lake Road Rochester Hills, Michigan 48307 Novi, Michigan 48375 Brighton, Michigan 48116 (810) 231-5188

(248) 844-5400 FINAL COMPLETION DATE

ORIGINAL: \$179,186.87 ORIGINAL: May 1, 2014 FROM: November 8, 2013

REVISED: \$176,773.88 REVISED: May 1, 2014 TO: May 1, 2014

SECTION 1. COST OF COMPLETED WORK TO DATE

Item	NOVI ROAD PATHWAY G.L.# 204-204.00-974.431	1		CONT	RACT ITEMS	(Orig	rinal)	(CON	TRACT ITEMS	(Re	vised)		THIS PERIOD				TOTAL TO DATE	
No.	Description of Item	Unit	Quantity		Cost/Unit		Total Amt	Quantity		Cost/Unit		Total Amt	Quantity	Amount	%	Quantity		Amount	%
0	Constr. Inspection "Crew Day"	CD	18.00	S	640.00	\$	11,520.00	19.50	\$	640.00	\$	12,480.00				21.00	S	13,440.00	108%
1	Bonds, Insur, & Mobilization (5%)	LS	1.00	\$	8,200.00	\$	8,200.00	1.00	\$	8,200.00	\$	8,200.00				1.00	\$	8,200.00	100%
2	Pre-Construction Audio-Visual	LS	1.00	\$	1,745.00	\$	1,745.00	1.00	\$	1,745.00	\$	1,745.00				1.00	s	1,745.00	100%
3	Soil Erosion and Sedimentation	LS	1.00	\$	5,440.00	S	5,440.00	1.00	S	5,440.00	S	5,440.00				1.00	S	5,440.00	100%
4	Tree Protection Fencing	LF	1560.00	\$	3.50	\$	5,460.00	1322.00	\$	3.50	\$	4,627.00				1322.00	s	4,627.00	100%
5	Temp. Traffic Control Devices	LS	1.00	5	10,880.00	S	10,880.00	1.00	5	10,880.00	S	10,880.00				1.00	S	10,880.00	100%
6	Clearing and Grubbing	STA	16.10	S	315.00	\$	5,071.50	16.10	\$	315.00	\$	5,071.50				16.10	\$	5,071.50	100%
7	Remove Tree (8"-18")	EA	3.00	s	230.00	\$	690.00	4.00	\$	230.00	\$	920.00			75	4.00	S	920.00	100%
8	Remove Concrete Curb and Gutter	LF	124.00	5	7.90	\$	979.60	124.00	\$	7,90	\$	979.60				124.00	\$	979.60	100%
9	Remove Concrete Sidewalk	SF	185.00	5	2.75	\$	508.75	201.00	\$	2.75	\$	552.75				201.00	\$	552,75	100%
10	Remove Asphalt Pavement	SF	285.00	\$	1.60	s	456,00	285,00	s	1.60	\$	456.00				285.00	s	456.00	100%
11	Adjust Structure, Complete	EA	2,00	\$	400.00	S	800.00	2,00	5	400,00	\$	800,00				2.00	\$	800.00	100%
12	Adjust Structure, Greater than 6"	VF	1.00	\$	600.00	S	600.00	2.00	\$	600.00	S	1,200.00				2.00	S	1,200,00	100%
13	Pathway Grading	STA	16.10	\$	1,175.00	\$	18,917.50	16.10	\$	1,175.00	\$	18,917.50				16.10	\$	18,917.50	100%
14	Undercut Excavation (as needed)	CY	145.00	\$	74.00	S	10,730.00	0.00	\$	74.00	\$				1	0.00	1::		
15	Embankment (CIP)	CY	150.00	\$	20.75	5	3,112,50	150.00	\$	20.75	\$	3,112.50				150.00	\$	3,112.50	100%
16	6" 21AA Limestone Agg. (CIP)	SY	1220.00	S	12,25	\$	14,945.00	1345.00	\$	12.25	\$	16,476.25				1345.00	\$	16,476.25	100%
17	Concrete Curb and Gutter	LF	99.00	S	24.00	\$	2,376.00	100.00	\$	24.00	s	2,400.00				100.00	\$	2,400.00	100%
18	4" Concrete Sidewalk	SF	9150.00	S	2.65	5	24,247,50	9208.00	\$	2.65	5	24,401.20				9208.00	\$	24,401.20	100%
19	6" Concrete Sidewalk	SF	163.00	S	3.05	s	497.15	163.00	s	3.05	S	497,15			1	163,00	\$	497.15	100%
20	ADA Ramp - 6" Concrete	SF	138.00	\$	3.05	\$	420.90	138.00	s	3.05	\$	420.90				138.00	\$	420.90	100%
21	Rip-Rap Spillway	SY	4.00	S	130.00	\$	520.00	6.00	\$	130.00	s	780.00	1			6.00	s	780.00	100%
22	Gravel Drive, 4-inch	SY	185.00	S	7.75	\$	1,433.75	185,00	5	7.75	5	1,433.75				185.00	s	1,433.75	100%
23	ADA Detectable Warning Plate	SF	32.00	s	33.00	\$	1,056.00	42.00	\$	33.00	\$	1,386.00				42.00	S	1,386.00	100%
24	Wood Back-Board on Existing	LF	290.00	s	14.00	\$	4,060.00	277.00	\$	14.00	\$	3,878.00				277.00	S	3,878.00	100%



26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

APPLICATION FOR FINAL PAYMENT

PROJECT: 2013 Novi Road Pathway/ADA NOVI PROJECT NO.: 13-5001 PAYMENT NO.: FINAL

	SECTION 1.									COST	OF (COMPLETED	WORK T	O DA	TE					
Item				CONTR	RACT ITEMS (Original)		CONTRACT ITEMS (Revised)							THIS PERIOD				TOTAL TO DATE	
No.	Description of Item	Unit	Quantity	С	ost/Unit	Tot	tal Amt	Quantity	())	Cost/Unit		Total Amt	Quantity		Amount	%	Quantity		Amount	%
25	Wooden Boardwalk, Complete	SF	272.00	\$	44.00	\$	11,968,00	272,00	5	44.00	\$	11,968.00					272.00	S	11,968.00	100%
26	Boardwalk Post - Add. Depth	VF	50.00	\$	25.00	5	1,250.00	44.00	S	25.00	\$	1,100.00					44.00	5	1.100.00	100%
27	8' Alum. Boardwalk Trans. Plate	EA	2.00	s	150.00	\$	300.00	2.00	\$	150.00	\$	300.00					2.00	\$	300.00	100%
28	Composite Ped. Railing (3-rail)	LF	99.00	S	32.00	\$	3.168.00	77.00	\$	32.00	\$	2,464.00	77.00	S	2,464.00	100%	77.00	S	2,464.00	100%
29	Concrete Spillway - Modified	SY	3.00	\$	200,00	s	600.00	5.50	\$	200.00	\$	1,100.00					5.50	\$	1,100.00	100%
30	Mulch Blanket	SY	1000.00	\$	1.80	\$	1,800.00	400.00	\$	1.80	\$	720.00					400.00	\$	720.00	100%
31	Taxus x media 'Densformis'	EA	5.00	\$	175.00	S	875.00	5.00	s	175.00	s	875.00					5.00	\$	875.00	1009
32	Viburnum carlesii	EA	3.00	\$	175,00	\$	525.00	3.00	S	175.00	\$	525.00			4		3.00	S	525,00	100%
33	Thuja occidentalis 'Rheingold'	EA	3.00	S	175.00	S	525.00	3.00	S	175.00	S	525.00					3.00	\$	525.00	1009
34	Berberis thun. 'Crimson Pygmy'	EA	6.00	S	175.00	\$	1.050.00	6.00	S	175.00	\$	1,050.00					6.00	S	1,050.00	1009
35	Restoration	LS	1.00	S	13,000.00	\$	13,000.00	1.00	\$	13,000.00	\$	13,000.00	0.50	\$	6,500.00	50%	1.00	S	13,000.00	100%
	2013 ADA COMPLIANCE PRO	GRAM (G.L	.# 204-204.00	0-805.0	003)				+		I			+						
36	Bonds, Insurance and Mob. (5%)	LS	1.00	\$	1,150.00	s	1,150.00	1.00	S	1,150.00	s	1,150.00					1.00	s	1,150.00	1009
37	Pre-Construction Audio/Visual	LS	1.00	\$	985.00	s	985.00	1.00	\$	985.00	\$	985.00					1.00	5	985.00	100
38	Soil Erosion and Sedimentation	LS	1.00	S	785.50	S	785.50	1.00	S	785.50	5	785.50					1.00	S	785.50	100
39	Temp. Traffic Control Devices	LS	1.00	\$	400.00	\$	400.00	1.00	s	400.00	\$	400.00					1.00	S	400.00	100
40	Remove Concrete Curb/Gutter	LF	136.00	\$	8.95	\$	1,217.20	137.00	\$	8.95	\$	1,226.15		3			137.00	S	1,226.15	100
41	Remove Concrete Sidewalk	SF	835.00	s	0.78	\$	651.30	1145.00	\$	0.78	\$	893.10					1145.00	S	893.10	100
42	Remove Concrete Pavement	SY	18.00	\$	15.74	\$	283.32	53.00	\$	15.74	s	834.22					53,00	S	834.22	100
43	Adjust Structure, Complete	EA	2.00	S	390.00	s	780.00	2.00	\$	390.00	s	780.00					2.00	S	780.00	100
44	Relocate Sprinkler Head w/Pipe	EA	1.00	\$	97.00	s	97.00	1.00	15	97.00	5	97.00					1.00	s	97.00	100
45	Undercut Excavation (as needed)	CY	4.00	\$	180.00	\$	720.00	0.00	S	180.00							0.00			
46	6" 21AA Limestone Agg. Base	SY	135.00	\$	17.20	s	2,322.00	147.00	S	17.20	5	2,528.40					147.00	s	2,528,40	100
47	Concrete Curb and Gutter	LF	136.00	S	24.00	\$	3,264.00	136,00	S	24.00	5	3,264.00					136.00	S	3,264.00	100
48	4" Concrete Sidewalk	SF	555.00	5	2.85	\$	1,581.75	792.00	\$	2.85	\$	2,257.20					792.00	s	2,257.20	100
49	ADA Ramp - 6" Concrete	SF	371.00	s	3.15	s	1,168.65	371.00	s	3.15	\$	1,168.65	III-E				371.00	s	1,168.65	100
50	Concrete Pavement	SY	18.00	5	58.50	\$	1,053.00	53.00	5	58,50	\$	3,100.50					53.00	S	3,100.50	100
51	ADA Detectable Warning Plate	SF	120.00	\$	33.00	S	3,960.00	120.00	s		s	3,960.00					120.00	\$	3,960.00	100
52	Restoration	LS	1.00	\$	560.00	\$	560.00	1.00	s	560.00	s	560.00	0.50	s	280.00	50%	1.00	s	560.00	100
									1											
	TOTAL FROM THIS SHEE	Т				\$	56,039.72				\$	57,616.72		S	9,244,00			\$	57,616.72	
	TOTAL FROM OTHER SHEE	T				S	123,147.15				\$	114,575.10		\$	178			\$	114,575.10	
	SUBTOTA	I.				S	179,186,87				S	172,191,82		S	9,244.00			s	172,191.82	100



26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

APPLICATION FOR FINAL PAYMENT

PROJECT: 2013 Novi Road Pathway/ADA

NOVI PROJECT NO .:

13-5001

PAYMENT NO .:

FINAL

NEW CONTRACT ITEMS

	SECTION 1.					COS	T OF	COMPLETED	WORK TO D	ATE					
tem	Description of Item	Description of Item Unit Division GL#		GL#	Quantity	NEW CONTRA	CT ITE	MS Total Amt	Quantity	% Quanti	TOTAL TO DATE Quantity Amount %				
3-1	Salvaged Fence Installation	LF	1	0	45.00	\$ 16.0	o s	720.00	- Cuminity	Amount	45.00	T	720.00	100	
4-1	Storm Sewer Extension	LS	1	0	1.00	\$ 1,997.0		1,997.00			1.00	1 12	1,997.00	100	
	Relocate Existing Push Button	LS	1	0	1.00	\$ 1,865.0		1,865.06			1.00		1,865,06	100	
			0	0	0.00	s -	s	4			0.00				
			0	0	0.00	s	s				0.00	_	4.1		
			0	O	0.00	s -	s	(40)			0.00		*		
			0	0	0.00	s -	s	*6			0.00	s	*		
			0	0	0.00	s -	\$	1*1			0.00		-		
			0	0	0.00	s -	\$				0.00	S			
			0	0	0.00	\$ -	s	740			0.00	s			
			0	0	0.00	s -	s	(*);			0.00	s			
			0	0	0.00	s -	s				0.00	S			
			0	0	0.00	s -	s				0.00	S			
			0	0	0.00	s -	s				0.00	s			
			0	0	0.00	s -	s	74			0.00	S	- 2		
			0	0	0.00	\$ -	s	(**)			0.00	s			
			0	0	0.00	\$ -	S				0.00	s	- 1		
			0	0	0.00	s -	\$				0.00) S			
			0	0	0.00	\$ -	\$				0.00) S			
			0	0	0.00	\$ -	s				0.00) \$			
			0	0	0.00	\$ -	s	190			0,00) \$	~		
		1	0	0	0.00	s -	s				0.00) s	-		
			0	0	0.00	\$ -	s				0.00	s			
			0	0	0.00	s -	s				0.00) \$			
Т			0	0	0.00	s -	\$	-			0.0) \$	102		
			0	0	0.00	s -	s	-			0.0	3	348		
			0	0	0.00	s -	s				0.0	\$	-		
			0	0	0.00	s -	s				0.0) s			
	TOTAL FROM THIS SHE	ET	17				\$	4,582.06		s -		\$	4,582.06		
	TOTAL FROM OTHER SHEE	TS		\$ 179,186.87			\$	172,191.82		9,244.00		\$	172,191.82		
	GRAND TOT	TAL		\$ 179,186.87			s	176,773.88		\$ 9,244.00		s	176,773.88	100%	



26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

Section 2. APPLICATION FOR FINAL PAYMENT 2013 Novi Road Pathway/ADA PROJECT: NOVI PROJECT NO .: 13-5001 PAYMENT NO .: FINAL CHANGE ORDERS Original Contract Amount: S 179,186.87 Change Orders: S (2,412.99)No. Date Amount \$ (1,708.99)November 12, 2013 Adjusted Contract Amount to Date: \$ S (704.00)176,773.88 2 May 1, 2014 Total Cost of Work Performed to Date: \$ 176,773.88 0% \$ MINUS Retainage: 21.00 \$ MINUS Inspection "Crew Days": To Date 960.00 This Pay 0.00 Net Amt. Earned of Contract and Extra Work to Date: 175,813.88 5 MINUS L.D.'s: # of days over = \$ \$ amount/day = \$600 Subtotal: S 175,813.88 TOTAL: (2,412.99)ADD Incentive "Crew Days", if under: 5 175,813.88 Subtotal: MINUS Amount of Previous Payments: 158,193,39 158,193.39 1 \$ 2 \$ 18.00 3 \$ Inspection "Crew Days" Allowed per Contract: 4 \$ Additional "Crew Days" per Change Orders: 1.50 Total Inspection "Crew Days" Allowed: 19.50 5 \$ Inspection "Crew Days" Used to Date: 21.00 6 \$ Inspection "Crew Days" Remaining: -1.50 7 8 BALANCE DUE THIS PAYMENT: 17,620.49 \$



26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454

Fax: (248) 735-5659

Section 3.

APPLICATION FOR FINAL PAYMENT

PROJECT:

2013 Novi Road Pathway/ADA

NOVI PROJECT NO .:

13-5001

01-111

PAYMENT NO .:

FINAL

The undersigned CONTRACTOR certifies that. (1) Any previous progress payments received from OWNER on amount of Work done under the Contract referred to above have been applied to discharge in full all obligations of CONTRACTOR incurred in connection with Work covered by prior Applications for Payment. (2) title to all Work materials, and equipment incorporated in said Work of otherwise listed in or covered by this Application for Payment will pass to OWNER at time of payment free and clear of all leins, claims, security interest, and encumberences (except such as are covered by Bond acceptable to OWNER indemnifying OWNER against any such lein, claim security interest, or encumberence), and (3) all Work covered by this Application for Payment is in accordance with the Contract Documents and not defective as that term is defined in the Contract Documents.

Fonson, Inc.	Date	8/3/14
Contractor Authorized Signature		2 2
By Ben Spada Print Name		
Spalding DeDecker & Associates, Inc. Consultant Firm	Date	3/5/14
Consultant Aluthonzed Signature		
By Ted Meadows	2	

Payment is recomm	of the above AMOUNT DUE TINIS APPLICATION nended
CITY OF	NOVI Law That
Ву	Aaron J. Staup, Construction Engineering Coordinator
Dated	8/11/14
1	512
Ву	Brian Coburn, PE., Engineering Manager
Dated	8/11/14

CONSENT TO FINAL PAYMENT BY OHIO FARMERS INSURANCE COMPANY

OHIO FARMERS INSURAN	CE COMPANY BOND NO. 6093070
OWNER:	OWNER'S PROJECT NO .:
City of Novi	
Novi, Michigan	DATE OF CONTRACT:
PROJECT: (Insert name, address and de	escription of Project)
Novi Road Pathway, 9 Mile to 10 Mi	lc.
and 2013 ADA Compliance Program	
5001, as Surety on bond of co (Insert name and address of Fonson, Inc. 7644 Whitmore Lake Road Brighton, MI 48116	mpany, P. O. Box 5001, One Park Circle, Westfield Center, Ohio 44251- contractor, Contractor)
shall not relieve Ohio Farmer (Insert name and address of	payment to the Contractor, and agrees that final payment to the Contract rs Insurance Company of any of its obligations to the owner, Owner)
City of Novi Novi, Michigan	
Novi, Michigan	
as stated in said Surety's bor	nd.
Dated: February 14, 2014	50m
	Ohio Farmers Insurance Company By: Heather M. Johnson, Attorney in Fact

General Power of Attorney

CERTIFIED COPY

POWER NO. 2140082 01

Westfield Insurance Co. Westfield National Insurance Co. Ohio Farmers Insurance Co.

Westfield Center, Ohio

Know All Men by These Presents, That WESTFIELD INSURANCE COMPANY, WESTFIELD NATIONAL INSURANCE COMPANY and OHIO FARMERS INSURANCE COMPANY, corporations, hereinafter referred to Individually as a "Company" and collectively as "Companies," duly organized and existing under the laws of the State of Ohio, and having its principal office in Westfield Center, Medina County, Ohio, do by these presents make, constitute and appoint DAN G. HINES, TERRI L. MAHAKIAN, HEATHER M. JOHNSON, JOINTLY OR SEVERALLY

of ANN ARBOR and State of MI its true and lawful Altorney(s)-in-Fact, with full power and authority hereby conferred in its name. place and stead, to execute, acknowledge and deliver any and all bonds, recognizances, undertakings, or other instruments or contracts of

THIS POWER OF ATTORNEY CANNOT BE USED TO EXECUTE NOTE GUARANTEE, MORTGAGE DEFICIENCY, MORTGAGE GUARANTEE, OR BANK DEPOSITORY BONDS.

and to bind any of the Companies thereby as fully and to the same extent as if such bonds were signed by the President, sealed with the corporate seal of the applicable Company and duly attested by its Secretary, hereby ratifying and confirming all that the said Attorney(s)-in-Fact may do in the premises. Said appointment is made under and by authority of the following resolution adopted by the Board of Directors of each of the WESTFIELD INSURANCE COMPANY, WESTFIELD NATIONAL INSURANCE COMPANY and OHIO FARMERS INSURANCE COMPANY:

"Be It Resolved, that the President, any Senior Executive, any Secretary or any Fidelity & Surety Operations Executive or other Executive shall be and is hereby vested with full power and authority to appoint any one or more suitable persons as Attorney(s)-in-Fact to represent and act for

and on behalf of the Company subject to the following provisions:

The Attorney-in-Fact may be given full power and authority for and in the name of and on behalf of the Company, to execute, acknowledge and deliver, any and all bonds, recognizances, contracts, agreements of indemnity and other conditional or obligatory undertakings and any and all notices and documents canceling or terminating the Company's liability thereunder, and any such instruments so executed by any such Attorney-in-Fact shall be as binding upon the Company as if signed by the President and sealed and attested by the Corporate Secretary."

"Be it Further Resolved, that the signature of any such designated person and the seal of the Company heretofore or hereafter affixed to any power of attorney or any certificate relating thereto by facsimile, and any power of attorney or certificate bearing facsimile signatures or facsimile seal shall be valid and binding upon the Company with respect to any bond or undertaking to which it is attached." (Each adopted at a meeting held on February 8, 2000)

In Witness Whereof, WESTFIELD INSURANCE COMPANY, WESTFIELD NATIONAL INSURANCE COMPANY and OHIO FARMERS INSURANCE COMPANY have caused these presents to be signed by their Senior Executive and their corporate seals to be hereto affixed this 09th day of AUGUST A.D., 2011

Corporate MSURAN Seals Affixed

State of Ohio County of Medina

STIONAL A ternennin.

WESTFIELD INSURANCE COMPANY WESTFIELD NATIONAL INSURANCE COMPANY OHIO FARMERS INSURANCE COMPANY

Ву Richard L. Kinnaird, Jr., National Surety Leader and Senior Executive

A.D., 2011, before me personally came Richard L. Kinnaird, Jr. to me known, who, being by me duly On this 09th day of AUGUST sworn, did depose and say, that he resides in Medina, Ohio; that he is Senior Executive of WESTFIELD INSURANCE COMPANY, WESTFIELD NATIONAL INSURANCE COMPANY and OHIO FARMERS INSURANCE COMPANY, the companies described in and which executed the above instrument: that he knows the seals of said Companies; that the seals affixed to said instrument are such corporate seals; that they were so affixed by order of the Boards of Directors of said Companies; and that he signed his name thereto by like order.

Notaria Seal Affixed

State of Ohio County of Medina

SS.



William J. Kahelin, Attorney at Law, Notary Public My Commission Does Not Expire (Sec. 147.03 Onio Revised Code)

Frank A. Carrino, Secretary of WESTFIELD INSURANCE COMPANY, WESTFIELD NATIONAL INSURANCE COMPANY and OHIO FARMERS INSURANCE COMPANY, do hereby certify that the above and foregoing is a true and correct copy of a Power of Attorney, executed by said Companies, which is still in full force and effect; and furthermore, the resolutions of the Boards of Directors, set out in the Power of Attorney are in full force and effect

In Witness Whereof, I have hereunto set my hand and affixed the seals of said Companies at Westfield Center, Ohio, this 14th day of

February A.D. 2014 MSURANC

MAL

Frank A. Carrino, Secretary

BPOAC2 (combined) (06-02)

SWORN STATEMENT BY CONTRACTOR

PROJECT NAME:_	Novi Road Pathway, 9 Mile to 1	0 Mile and 2013 A	ADA Compliance Progran
	PROJECT NUMBER:	13697	

STATE OF MICHIGAN COUNTY OF Livingston

Ben Spada being duly sworn, deposes and says that he is authorized to represent and act for Fonson Inc., the Contractor names in the foregoing invoice, having a Contract with the City of Novi located in the City of Novi, County of Oakland, and State of Michigan; that the following are the names of all subcontractors furnishing or which have furnished materials and labor for said Contractor in connection with said Contract, and that the amounts due or to become due to every subcontractor, for labor, methods, services, materials, equipment, transportation, or other facilities performed or furnished as of the date of the invoice attached hereto, are fully and correctly set forth opposite their respective names, to-wit:

SUPPLIER OR SUBCONTRACTOR		AMOUNT OF CONTRACT		AMOUNT PAID		CURRENT AMOUNT DUE	BALANCE DUE TO COMPLETE
Fonson Inc.	\$	101,163.67	\$	83,543.18	\$	17,620.49	\$
All labor, fringes, payroll taxes	and oth	ner payroll obligati	ons	paid in full thru 6/30/1	4		\$ <u> </u>
Aggregate Industries	\$	2,293.88	\$	2,293.88	\$		\$ -
Construction Video	\$	2,245.00	\$	2,245.00	\$	*	\$ *
Crimboli Nursery	\$	2,550.00	\$	2,550.00	\$		\$
Hanes/Geo	\$	3,441.08	\$	3,441.08	\$		\$
GAZ Contracting, Inc.	\$	846.25	\$	846.25	\$		\$
J. Ranck Electric, Inc.	\$	1,750.00	\$	1,750.00	\$		\$
Koal-T Construction	\$	43,955.60	\$	43,955.60	\$	·	\$ 1 €3
State Barricades	\$	1,722.40	\$	1,722.40	\$	-	\$ (20)
Thomas Bridge Construction	\$	15,846.00	\$	15,846.00			
A STATE OF THE STA					\$		\$ -0
Total	\$ \$	175,813.88	\$	158,193.39	\$	17,620.49	\$ *

And deponent further says that said Contractor has not procured material from, or subcontracted with, any person, firm, or

corporation other than those above mentioned and owes no more transportation, or other facilities performed or furnished in connection.	nies for labor, methods, services, materials, equipment
And deponent further says that he is employed in the capacity of	Project Manager by said Contractor and is
duly authorized by said Contractor to sign this affidavit.	Se de Conature
Subscribed and sworn to before me this 25th day of June, 2014	
Notary Public in and for the County	y of Washtenaw
My Commission expires: 6/4/17 SWNSTMT	

DEC 1 6 2013

My/our contract with	Fonson Inc.		
	(other contr	acting par	rty)
to provide	Material		
for the improvement to	the property described a	as	Fonson Job No. 13697
			Novi Road Pathway
			Novi, Michigan
			Oakland County
hereby waived and rele	eased.		
	:-		Aggregate Industries
	(las	when These CAROLYN PHELI
			(signature of lien claimant) CREDIT MANA LE
Signed on/	2.11-13	Address	Dept CH 16434
	(date)		Palatine, Illinois 60055-6434
		Telephone	11.0 2012056

DO NOT SIGN BLANK OR INCOMPLETE FORMS.
RETAIN A COPY

NOV 2 7 2013

FULL UNCONDITIONAL WAIVER

Our contract with Tonson, In	The state of the s
	has been fully paid and satisfied at / Lien Bond covering said Project and all of
our rights to pursue payment under the Pay	ment/Lien Bond Non/aissued
by n/a as princip	pal andn/a as surety,
	causes of action we may have against, are hereby fully waived and
	(if any) dated, and any
	Dwight C. Spengler its: President
STATE OF MICHIGAN) SS COUNTY OF Macomb)	
The signator is known to me and a	acknowledged the foregoing instrument this
18thay of <u>November</u> , 2013.	Karen L. Stachkunis Notary Public Macomb County, Michigan
	My commission expires:6/8/2020
	Acting In Macomb County
	KAREN L STACHKUNIS Notary Public - Michigan Macomb County My Commission Expires Jun 8, 2020 Acting in the County of

Our contract with TONSON,	INC. to furnish LABOR AND
materials to ROAD Project No. 13.	697 has been fully paid and satisfied
with respect to our rights under the Pay	ment / Lien Bond covering said Project and all of
	Payment/Lien Bond No issued
	incipal and as surety,
	or causes of action we may have against
	, are hereby fully waived and
	im" (if any) dated, and any
amendment(s) thereto, is hereby rescin	ded.
	C
	CRIMBOLI NURSKEY
	11/
	by: Abam Sucre
	its: GENERAL MANAGER
STATE OF MICHIGAN)	
COUNTY OF) SS	
,	
The signator is known to me a	nd acknowledged the foregoing instrument this
TH day of DECEMBER, 2013.	no acidowedged the loregoing matument this
day of vertex, 2012.	the p
	Notary Public County, Michigan
	My commission expires: 6/4/17
	Acting In LIVINGTON County

14 2014 JAN 0 1 RFC'D

RE

My/our contract with	Fonson Inc.		
	(other contra	acting pa	rty)
to provide	Material		
for the improvement to	the property described as	s	Fonson Job No. 13697
			Novi Road Pathway
			Novi, Michigan
			Oakland County
	-		Hanes Geo Components
			(Mas X Carmel
			(signature of lien claimant) KRIS CARSW
10	12	W.P.	CONTROLLER
Signed on 12 12		Address	500 N. McLin Creek Road
	(date)		Conover, NC 28613
	T	elephone	828 464 4673

DO NOT SIGN BLANK OR INCOMPLETE FORMS.
RETAIN A COPY

This waiver is specific only to the amount of goods shipped on the following Hanes Geo invoices:

Date Amount Invoice Invoice Date **Amount** Invoice Date **Amount** 9/23/2013 \$ 64 225233 1,485.48 64 230386 10/23/2013 \$ 1,715.61 64 232405 11/5/2013 \$ 111.94 64 232406 11/5/2013 72.08 64 232407 11/5/2013 \$ 55.97

Our contract with \overline{T}	ONSON, INC. to	furnish LABOR	ANA
materials to ROAD Project			
with respect to our rights un	nder the Payment / Lier	Bond covering said Pro	piect and all of
our rights to pursue payme			
by			
together with any rights,		s of action we may , are hereby fully	1970
released and the "Notice			
amendment(s) thereto, is h			
	4.		
OTATE OF MICHICAN	by,	JOSEPH A. GA PERSIDENT	AZDECKI
STATE OF MICHIGAN)) SS		
COUNTY OF)		
English and Artist and		ledged the foregoing in	strument this
16TH day of Decoure, 2	<u>ب</u> ا	County, M	, ,
	Ac	ting In Louiston (County

213138 Final

FULL UNCONDITIONAL WAIVER

RESIDE

DEC 2 6

Our contract	with Fonson, INC	. to furnish	LABOR	AND
materials to ROA	Project No. 1369	7 has be	en fully paid	and satisfied
with respect to our	rights under the Payment	t / Lien Bond cove	ering said Proj	ect and all of
our rights to pursue	e payment under the Payi	ment/Lien Bond N	10	issued
by	as principa	al and		_ as surety,
	rights, demands, or o			
released and the	"Notice of Lien Claim" (eto, is hereby rescinded.	if any) dated	k ELECT	_, and any
STATE OF MICHIG	la iss	its: CFO		
The signator day of Duu	is known to me and a		County, Michael County, Michael County	Notary Public chigan

Full Unconditional Waiver

I/We have a contract with Fonson, Inc. to provide: Concrete for the improvement to the property described as: Novi Road Pathway Project having been fully paid and satisfied, all my/our construction lien rights against such property are hereby waived and released.

Company: Koala-T Construction

(Signature of lien claimant) BRAO WATSON

(Job Position)

Telephone: 248 322 2751

Signed on: (date) 5 2014

Address 424 FOREP POSTIAC, MI 48341

Do not sign blank or incomplete forms - retain a copy

DEC 1 8 2013

Our contract with FONSON, INC. to furnish LABOR AND
materials to Novi Project No. 13697 has been fully paid and satisfied
with respect to our rights under the Payment / Lien Bond covering said Project and all of
our rights to pursue payment under the Payment/Lien Bond No Issued
by as principal and as surety.
together with any rights, demands, or causes of action we may have against
or, are hereby fully waived and
released and the "Notice of Lien Claim" (if any) dated, and any
amendment(s) thereto, is hereby rescinded.
STATE OF MICHIGAN) SS COUNTY OF Macomb) SS
The signator is known to me and acknowledged the foregoing instrument this
9 day of DEC , 20 13
Notary Public County, Michigan
My commission expires: My 51 2017
Acting In Macon & County
Notary Public - Michigan
Macomb County My Commission Expires My 31, 2017 Acting in the County of Macomb

FON

DEC 17

FULL UNCONDITIONAL WAIVER

RES

Our contract with Thousand Project with respect to our rights upon our rights to pursue payments.	ct No. 13697 nder the Payment / I	has be Lien Bond cove	en fully paid ering said Pro	and satisfied pject and all of
by	as principal	and		as surety,
together with any rights	or	uses of action	n we may hereby fully	have against waived and
released and the "Notice amendment(s) thereto, is h		any) dated		, and any
		Dy: John its: onne	T. 681	CONSTRUCTION YOUR BIRD CONT FFITHS
STATE OF MICHIGAN COUNTY OF)) SS)			
The signator is kn	own to me and ack	knowledged the	e foregoing i	nstrument this
Conday of December	20_13	Ord	1 (2)	11 1 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2
CHELSEA E HAI NOTARY PUBLIC - STATE O COUNTY OF OAKI My Commission Expires S Acting in the County of CA	OF MICHIGAN AND July 4, 2017	Oakland My commissi Acting In	County, I on expires: ak\and	July 4,2017
