CITY of NOVI CITY COUNCIL



Agenda Item M February 29, 2016

SUBJECT: Approval of the final payment to Nagle Paving Company for the Civic Center North Parking Lot and Power Park Pathways Rehabilitation project in the amount of \$12,000, plus interest earned on retainage.

SUBMITTING DEPARTMENT: Department of Public Services, Engineering Division BrC CAP Department of Parks, Recreation and Cultural Services

CITY MANAGER APPROVAL:

EXPENDITURE REQUIRED	\$ 12,000
AMOUNT BUDGETED	 \$ 53,000 (Civic Center Parking Lot) \$ 6,945 (Power Park Drainage Improvements) \$ 54,040 (Power Park Pathways) \$ 113,985 TOTAL
LINE ITEM NUMBER	101-442.10-971.100 (Civic Center Parking Lot) 210-211.00-865.294 (Drainage Improvements) 208-691.00-974.096 (Power Park Pathways)

BACKGROUND INFORMATION:

This project was a combination of two separate line items in the Capital Improvement Plan: 1) Civic Center North Parking Lot Improvements and 2) Power Park Pathways Rehabilitation.

Improvements to the north Civic Center Parking Lot included pavement replacement in areas that had shown significant deterioration, and crack repair and patching in other areas.

In Power Park, there was approximately 1,500 feet of asphalt pathway that had shown varying levels of deterioration. The original plan was to perform crack repairs on the portions of pathway that were in fair condition, while rehabilitating other areas by way of an asphalt overlay. At the time construction was to begin, further inspection revealed that an overlay would not be the prudent fix. It was determined and agreed to that the rehabilitated areas should be fully reconstructed. Therefore, those rehabilitation portions of pathway were deleted from the contract. The Parks, Recreation and Cultural Services Department will release a future project entailing a reconstructed effort when more funding becomes available.

The construction contract was awarded for this project at the May 11, 2015 City Council meeting to Nagle Paving Company in the amount of \$96,006.00.


Engineering staff worked with the engineering consultant for this project, URS Corporation, to review and verify the final contract payment amount of \$12,000 that is due the contractor (Final Pay Estimate No. 3, attached). The City Attorney reviewed the documentation and found it to be in an acceptable form (Beth Saarela's February 2, 2016 letter, attached).

There were two (2) approved change order issued for this project resulting in a net decrease of \$19,263.50 to the construction contract, or 20.1% under the awarded amount. Most changes were a result of decreased quantities due to removing the areas of pathways in Power Park that are to be reconstructed in the future and balancing of originally projected amounts. The approved change orders resulted in a final contract price of \$76,742.50.

RECOMMENDED ACTION: Approval of the final payment to Nagle Paving Company for the Civic Center North Parking Lot and Power Park Pathways Rehabilitation project in the amount of \$12,000, plus interest earned on retainage.

	1	2	Υ	Ν
Mayor Gatt				
Mayor Pro Tem Staudt				
Council Member Burke				
Council Member Casey				

	1	2	Υ	Ν
Council Member Markham				
Council Member Mutch				
Council Member Wrobel				

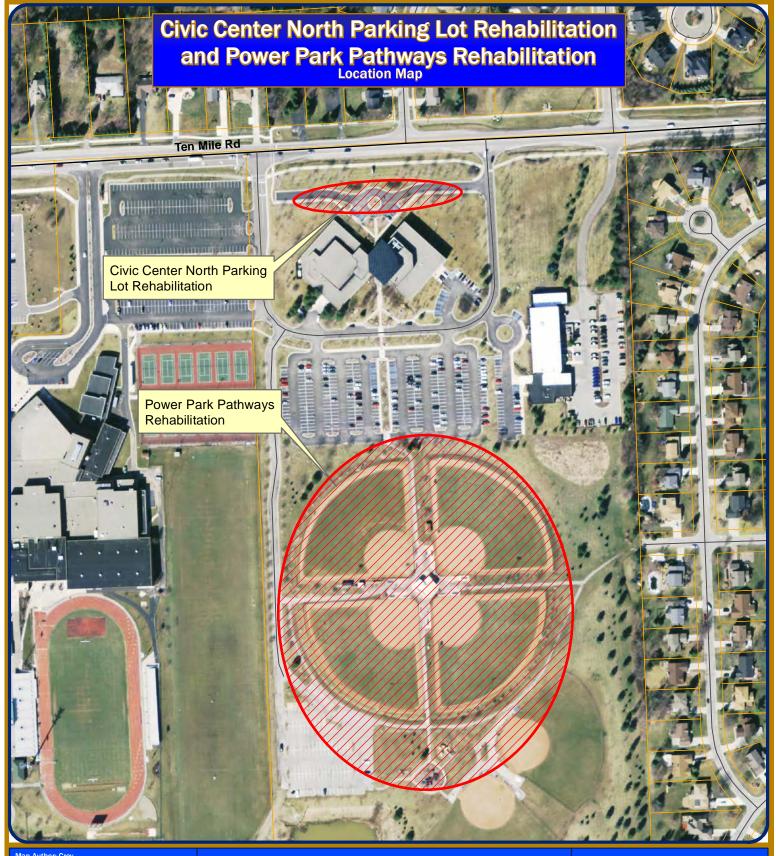

Map Author: Croy Date: 10/13/14 Project: Civic Center / Power Park Version #: v1.0

Amended By: Date: Department:

> MAP INTERPRETATION NOTICE ap information depicted is not intended to replace or substitute for any official or primary source. This map was intended to meet National Map Accuracy Standards and use the most recent, accurate sources available to the people of the City of Novi. Boundary measurements and area calculations are approximate dishould not be construed as survey measurements performed by licensed Michigan Surveyor as defined in Michigan Public Act 132 of 1970 as amended. Please contact the City GiS Manager to





City of Novi Engineering Division Department of Public Services 26300 Lee BeGole Drive Novi, MI 48375 cityofnovi.org

CIVIC CENTER NORTH LOT AND POWER PARK PATHWAYS REHABILITATION



Looking east towards Civic Center – North Parking Lot from Novi Way



Looking east along handicapped lot towards North Lot circle



New Power Park Pathway spur from playground to ball fields



Rehabilitated Power Park Pathway intersection at north end of playground



JOHNSON ROSATI SCHULTZ JOPPICH PC

27555 Executive Drive Suite 250 ~ Farmington Hills, Michigan 48331 Phone: 248.489.4100 | Fax: 248.489.1726

Elizabeth Kudla Saarela esaarela@jrsjlaw.com

www.jrsjlaw.com

February 2, 2016

Aaron Staup, Engineering Coordinator CITY OF NOVI Department of Public Services Field Services Complex 26300 Lee BeGole Drive Novi, MI 48375

Re: *Civic Center North Lot/Power Park Paths Project – Nagle Paving Closing Documents*

Dear Mr. Staup:

We have received and reviewed closing documents for the Civic Center North Lot/Power Park Paths Project:

- 1. Application for Final Payment
- 2. Contractor's Sworn Statement
- 3. Consent of Surety
- 4. Waivers of Lien

Subject to approval of the Application for Final Payment by appropriate City staff, the closing documents appear to be in order. The existing Maintenance Bond amount is adequate for the final project cost. The General Contractor has provided its final waiver of lien.

Please feel free to contact me with any questions or concerns in regard to this matter.

Very truly yours, JOHNSON, ROSATI, SCHULTZ & JOPPICH, P.C. Élizabeth K. Saarela

EKS

C:

.

Enclosures

,

Maryanne Cornelius, Clerk (w/Enclosures) Rob Hayes, Public Services Director (w/Enclosures) Carl Johnson, Finance Director/Chief Financial Officer (w/Enclosures) Brian Coburn, Engineering Manager (w/Enclosures) Mark Koskinen, URS Corporation (w/Enclosures) Thomas R. Schultz, Esquire (w/Enclosures)

cityota	Norte Contraction of the Contrac		OF N		-	\$ 12,000.00			PURC	HASE OF -94378 94.4	>	NO]	<u></u>	Novi, Mi Tel: (24	ee BeGole chigan 483 8) 347-045- 8) 735-5659	375 4	
					Α	PPLICAT		DR	FINA	_ PAY	MEN	IT						
PROJE	ECT: Civic Ctr N Lot/Power Park	Paths		NOVI PR	ROJECT	ſ NO.:	15-8401						PAYMENT NO .:	and the second second of the design	FINAL			Discontine Soliteiron de la contraction
OWNE	45175 W. Ten Mile Road Novi, Michigan 48375			ENGINE				nklin Mich	Road, Suite nigan 48034				CONTRACTOR:		39525 V	higan 4837	d, Suite 300	
CONTR	RACT AMOUNT			FINAL C	OWPLE	ETION DATES							DATES OF ESTI	MALE				
ORIGI	NAL:\$96,006.00		-	ORIGIN/ REVISE					July 25, 20 August 15, 2				FROM:			Augus	t 13, 2015	
REVIS	ED:\$76,742.50			ACTUAL	<u>L:</u>				August 11, 2				то:			Januar	y 13, 2016	
	SECTION 1.			COST OF COMPLETED WORK TO DATE														
Item	Division 1 - Civic Center North Parking Lot GL#101-442,10-971,100			CONTRACT ITEMS (Original)			CONTRACT ITEMS (Revised)					THIS PERIOD	TOTAL TO DATE					
No.	Description of Item	Unit	Quantity	Cost/	/Unit	Total Amt	Quantity	1	Cost/Unit	Total A	mt	Quantity	Amount	%	Quantity	Am	ount	%
0	Constr. Inspection "Crew Day"	CD	12.00		640.00	\$ 7,680.00	12.00	\$	640.00	\$ 7	,680.00				16.50	\$	10,560.00	138%
1	Traffic Control and Access	LS	1.00		,000.00		1.00	\$	1,000.00		,000.00		L		1.00	\$	1,000.00	100%
2	Pavt Removal, Modified	SY	650.00	\$	7.00		592.00	\$	7.00		,144.00				592.00		4,144.00	100%
3	Cold Milling HMA Surface	SY	1291.00	\$	6.00		1344.00	\$	6.00		064.00				1344.00		8,064.00	100%
4	Hand Patching	TON	20.00		135.00		18.00	\$	135.00		,430.00		<u> </u>		18.00	\$	2,430.00	100%
5	HMA, 13A	TON	225.00	\$	90.00		227.03	\$	90.00		,432.70				227.03		20,432.70	100%
6	HMA, 3C	TON	82.00	\$	90.00		113.32	\$,198.80		<u> </u>		113.32	\$	10,198.80	100%
7	Curb and Gutter Inlet Filter	EA	4.00		110.00	······································	5.00	\$	110.00		550.00				5.00	\$	550.00	100%
8	Pavement Markings	LS	1.00	\$	500.00	\$ 500.00	1.00	\$	500.00	\$	500.00				1.00	\$	500.00	100%
								\vdash						<u> </u>	<u> </u> -			
								╀										
		1											ļ			<u> </u>		·
															<u> </u>			
		<u> </u>					<u> </u>	_						<u> </u>				
				<u> </u>			<u> </u>					ļ		+		<u> </u>		
	-			<u> </u>			<u> </u>		~~~~			<u> </u>	<u> </u>					
							<u> </u>						<u> </u>					
 	<u> </u>		+										<u> </u>					
L						L	L			l	<u>0</u>	1	<u> </u>		J]	
	TOTAL THIS SHEET	г				\$ 44,566.00				\$ 47	7,319.50		\$ -			\$	47,319.50	100%



26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

		APPLICA	ATION FO	R FINAL PAYMENT		
PROJECT:	Civic Ctr N Lot/Power Park Paths	NOVI PROJECT NO .:	15-8401	PAYMENT NO.:	FINAL	

····	SECTION 1.								COST	OF	COMPLETED	WORK TO	DATE				·	·······	
Item	<u>Division 2 - Power Park Pathwa</u> GL#208-691.00-974.096	vs		CONT	RACT ITEMS	(Original)		CONT	TRACT ITEMS			THIS PERIOD				TOTAL TO DATE			
No.	Description of Item	Unit	Quantity		Cost/Unit	Total Amt	Quantity		Cost/Unit		Total Amt	Quantity	Amount		%	Quantity		Amount	%
9	Traffic Control and Access	LS	1.00	\$	2,500.00	\$ 2,500.00	1.00	\$	2,500.00	\$	2,500.00					1.00	\$	2,500.00	100%
10	HMA Surface, Removal	SY	260.00	\$	15.00	\$ 3,900.00	187.00	\$	15.00	\$	2,805.00					187.00	\$	2,805.00	100%
11	Cold Milling HMA Surface	SY	18.00	\$	40.00	\$ 720.00	0.00	\$	40.00							0.00			
12	Pathway Grading	FT	350.00	\$	12.00	\$ 4,200.00	260.00	\$	12.00	\$	3,120.00					260,00	\$	3,120.00	100%
13	Pavement, Cleaning	LS	1.00	\$	850,00	\$ 850.00	1.00	\$	850.00	\$	850,00					1.00	\$	850.00	100%
14	Subgrade Undercutting, Type II	CY	10.00	\$	55.00	\$ 550.00	0.00	\$	55.00					-		0.00	<u> </u>		
15	Agg Base, 21AA, Limestone, 6"	SY	275.00	\$	16.00	\$ 4,400.00	258.00	\$	16.00	\$	4,128.00					258,00	\$	4,128.00	100%
16	Overband Crack Seal, Special	FT	1550.00	\$	2.00	\$ 3,100.00		\$	2.00		2,620,00	····				1310.00		2.620.00	100%
17	Hand Patching	TON	12.00	\$	160.00	\$ 1,920.00	0.00	\$	160.00		· · · · · · · · · · · · · · · · · · ·		1			0.00			
18	HMA, 13A	TON	178.00	\$	125.00	\$ 22,250.00		\$		\$	7,100.00		1			56.80	\$	7,100.00	100%
19	24-inch Drain Basin	EA	1.00	\$	1,500.00	\$ 1,500.00	1.00	\$	1,500.00	\$	1,500.00					1.00	\$	1,500.00	100%
20	8-inch N-12 Sewer	FT	32.00	\$	50.00	\$ 1,600.00		\$	50.00	\$	1,300.00						\$	1,300.00	100%
21	Surface Restoration	LS	1.00	\$	3,500,00	\$ 3,500.00	1.00	\$	3,500.00	\$	3,500,00					1.00	\$	3,500.00	100%
22	Silt Fence	FT	150.00	\$	3.00	\$ 450.00	0.00	\$	3.00	<u> </u>						0.00			
				1															
		· · · ·	1	1															
				1															
				1									—				<u> </u>		
				-											·····				
	1		<u> </u>	1												<u> </u>	1		
										<u> </u>			<u> </u>			-	1		
				1				-		<u> </u>							-		
				+		······································				<u> </u>									
				1			1	1		t				-		1	1		
		<u> </u>	<u> </u>	1			+	1-		<u> </u>									
			1	-		<u> </u>													
				┼──		·		+		1									
				-				1								<u> </u>			
				+			+	-								<u> </u>			
	<u> </u>	<u> </u>					<u>+</u>										<u> </u>		
		<u> </u>	<u> </u>	+				-	~	<u> </u>				-+		<u> </u>			
			1	1			+			+			1			+			
			<u> </u>	+			+	+		+		<u> </u>							
				+	_	<u> </u>	+	+		+						+	+		
				+				+		\vdash							+		
L	TOTAL FROM THIS SHEET		,	_l		\$ 51,440.00		_!~		\$	29,423,00	L	\$			-l	\$	29,423.00	
	TOTAL FROM OTHER SHEET					\$ 44,566.00				Ψ \$	47,319,50		\$	-			ŝ	47,319.50	
										÷	,		\$				\$ \$	76,742.50	100%
	SUBTOTAL					\$ 96,006.00				\$	76,742.50		Φ	-			Ф	/0,/42.50	100%

35 36

37

38_

39

40

46

47

48

49

50

CITY OF NOVI

26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

TOTAL TO DATE

-

%

Amount

PROJECT:	Civic Ctr N Lot/Power Pa	ark Paths	N	IOVI PROJECT NO .:	15-8401			ſ	PAYMENT NO .:		FINAL	
					NEW CONT	RACT ITEM	S					
	SECTION 1.					COS	T OF COMPLETED	WORK TO	DATE			
Item No.	Description of Item	Unit	Division	GL#	Quantity	NEW CONTRA	CT ITEMS Total Amt	Quantity	THIS PERIOD	%	Quantity	
23			0	0	0.00	\$ -	s -	Quantity	Anoun	/8	0.00	\$
24			0	0	0.00	s -	<u> </u>				0.00	\$
25			0	0	0.00	\$ -	\$ -				0.00	\$
26			0	0	0.00	\$ -	\$ -				0.00	\$
27			0	0	0.00	\$ -	\$ -		······································		0.00	\$
28			0	0	0.00	\$ -	\$ -				0.00	\$
29			0	0	0.00	\$-	\$ -				0.00	\$
30			0	0	0.00	\$	\$				0.00	\$
31			0	0	0.00	\$	\$ -				0.00	\$
32			0	0	0.00	\$	\$ -				0.00	\$
33			0	0	0.00	\$	\$				0.00	\$
34			0	0	0.00	\$ -	\$ -				0.00	\$

0	0	0.00	\$ -	\$ - 1	1		0.00	\$ -	
0	0	0.00	\$ -	\$ _			0.00	\$ -	
0	0	0.00	\$ -	\$ -			0.00	\$ -	
0	0	0.00	\$ -	\$ -			0.00	\$ -	
0	0	0.00	\$ -	\$ -			0.00	\$ -	
0	0	0.00	\$ -	\$ -			0,00	\$ -	
0	0	0.00	\$ -	\$ -			0.00	\$ -	
0	0	0.00	\$ -	\$ -			0.00	\$ -	
0	0	0.00	\$ -	\$ -			0.00	\$ -	
0	0	0.00	\$ -	\$ 			0.00	\$ -	
0	0	0.00	\$ -	\$ _			0.00	\$ -	
0	0	0.00	\$ -	\$ -			0.00	\$ -	
0	0	0.00	\$ -	\$ 			0.00	\$ -	
0	0	0.00	\$ -	\$ -			0.00	\$ -	
0	0	0.00	\$ -	\$ ~			0.00	\$ -	
0	0	0.00	\$ ŧ	\$ -			0.00	\$ 	1
0	0	0.00	\$ -	\$ -			0.00	\$ -	l
0	0	0.00	\$ -	\$ -			0.00	\$ -	i
0	0	0.00	\$ -	\$ -			0.00	\$ -	ĺ
0	0	0.00	\$ -	\$ 			0.00	\$ -	ĺ

TOTAL FROM THIS SHEET TOTAL FROM OTHER SHEETS GRAND TOTAL

\$ 96,006.00 \$ 96,006.00 \$ \$ \$

-

76,742.50

76,742.50

\$

\$

\$

-

-

-

\$ \$ \$

76,742.50 76,742.50 _100%

APPLICATION FOR FINAL PAYMENT

CITY	OF NOVI	Ī	PUR	24978- -94978- 944491			26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659
Section 2.							
	AI	PPLICATION FO	DR FINA	L PAYMENT			
PROJECT: Civic Ctr N Lot/Power Park Paths	NOVI PROJECT				PAYMENT N	0.:	FINAL
Original Contract Amount:	\$	96,006.00 🦟		CHANGE ORDE	ERS		
Change Orders:	\$	(19,263.50)	<u>No.</u> 1	<u>Date</u> July 29, 2015		<u>10unt</u> (22,017.00)	1
Adjusted Contract Amount to Date:	\$	76,742.50	l	July 29, 2015 August 18, 2015	\$ \$	2,753.50	` /
Total Cost of Work Performed to Date:	\$	76,742.50			3 S S	-	
MINUS Retainage: MINUS Inspection "Crew Days": To Date This Pay	0% \$ 16.50 \$ 0.00	2,880.00 🛩			↓ \$ \$	-	
Net Amt. Earned of Contract and Extra Work to Date:	\$	73,862.50 🛩			\$	-	
MINUS L.D.'s: # of days over = \$ amount/day = \$600	\$	-			\$ \$	-	
Subtotal:	\$	73,862.50			\$	_	<u></u>
ADD Incentive "Crew Days", if under:	\$	-		TOTAL:	\$	(19,263.50) control
Subtotal:	\$	73,862.50 🛩					
MINUS Amount of Previous Payments: 🧶 🗸 1 \$ 23,330.70 2 \$ 38,531.80 ✓	\$	61,862.50 🛩					
3 \$ -				Inspection "Crew Days" Allowe		12.00	
4				Additional "Crew Days" per Ch		0.00	_
5\$ -				Total Inspection "Crew Days" A Inspection "Crew Days" Used t		12.00	-
6 7\$-				Inspection "Crew Days" Used to Inspection "Crew Days" Remai		-4.50	4
/ 3 - 8 \$ -				Inspection orew Days Kenta	n m 19.		
9\$ -							
10 \$ -	<u></u>						
BALANCE DUE THIS PAYMENT:	\$	12,000.00					



CITY OF NOVI

26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

FINIAL

Section 3.

APPLICATION FOR FINAL PAYMENT

PROJECT: Civic Ctr N Lot/Power Park Paths

er Park Paths

NOVI PROJECT NO .: 15-8401

-14-2016

PAYMENT NO .:

Payment of the above AMOUNT DUE THIS APPUCATION

The undersigned CONTRACTOR certifies that: (1) Any previous progress payments received from QWNER on amount of Work done under the Contract referred to above have been applied to discharge in full all obligations of CONTRACTOR incurred in connection with Work covered by prior Applications for Payment; (2) tills to all Work, materials, and equipment incorporated in said Work of otherwise listed in or covered by this Application for Payment will pass to OWNER at time of payment free and clear of all leins, claims, security interest, and encumberances (except such as are covered by Bond acceptable to OWNER indemnifying OWNER egainst any such lein, claim security interest, or encumberance), and (3) all Work covered by this Application for Payment is in accordance with the Contract Documents and not defective as that term is defined in the Contract Documents.

Nagle Paving Company Date ringetor Compa Contractor Authorized Signature By:

29-16

Date

is recomm	
By:	Aaron J. Staup, Construction Engineering Coordinato
Dated:	1 29 16
//-	312
By:	Brian Coburn, PE., Engineering Senior Manager
Dated:	43/16

URS Corporation Consultant Firm Obnaultant Alenonized Signature By: Mank Kaskingn Print Name

All Full Unconditional Waivers of lien have been received from each subcontractor and/or supplier, reviewed and approved by the Consultant, Also, attached to this Final Payment is a copy of the Contractor's Swom Statement, Consent of Surety, and a new Maintenance and Guarantee Bond (If the amount is greater than the final contract price) or a Maintenance Bond Rider covering the difference between the final contract price and the awarded amount.

	Casher	
CONSENT OF	Architect	
SURETY COMPANY	Contractor	
TO FINAL PAYMENT	Surety	
ALA DOCUMEN E G207	Odwr	Bond No 929613670
PROJECT: Civic Center Parking Lot and Por institute address)	ver Park Pathways R	
TO: (Unite) City of Novi	ARCHITEC	T'S PROJECT NO:
45175 West Ten Mile Road	CONTRACT	f for:
Novi, MI 48375		
	COMPRACY	i date:
CONTRACTOR:		
Nagle Paving Company 39525 West 13 Mile Road Novi, MI 48377		
In accordance with the provisions of the Contract be	ween the Owner and the	Contractor as indicated above, the
Western Surety Company		
Оле Towne Square, Suite 1075 Southfield, MI 48076		SURETY COMPANY
on bond of their insertance and matrice of Conceptor)		
Nagle Paving Company		
39525 West 13 Mile Road Novi, MI 48377		CONTRACTOR,
hereby approves of the final payment to the Contract reheve the Surety Company of any of its obligations		
City of Novi		
45175 West Ten Mile Road Novi, MI 48375		,OWNER.
as set forth in the said Surety Company's bond.		
IN WITNESS WHEREOF,		
the Surety Company has hereinto set its hand this	13th day:of Ja	nuary, 2016
	Surety Compa Western Sur	ety Company
	Grand	> <u>></u>
	Separate of Auth	anzeel Representative
isterie	Susan L Sma	II, Attorney-in-Fact
NOTE: This form is to be used as a comparison document to ARV in DEMS AND CLAIMS, Corrent a dation	RULTHING STATISTIC	ACTOR'S ALL DAVITOR PAY MENT OF
AIA DXCUMENT G007-CONSULT OF SURTY COMPANY O PAGE 2010/01/11 AMERICAN INSTITUTE OF ARCHITECTS 1935		

a,

. .



POWER OF ATTORNEY APPOINTING INDIVIDUAL ATTORNEY-IN-FACT

Know All Men By These Presents, That WESTERN SURETY COMPANY, a South Dakota corporation, is a duly organized and existing corporation having its principal office in the City of Sioux Falls, and State of South Dakota, and that it does by virtue of the signature and seal herein affixed hereby make, constitute and appoint

Steven K Brandon, T J Griffin, William A Pirret, John L Budde, Terence J Griffin, Susan L Small, Patrick Williams, Individually

of Farmington Hills, MI, its true and lawful Attorney(s)-in-Fact with full power and authority hereby conferred to sign, seal and execute for and on its behalf bonds, undertakings and other obligatory instruments of similar nature

- In Unlimited Amounts -

and to bind it thereby as fully and to the same extent as if such instruments were signed by a duly authorized officer of the corporation and all the acts of said Attorney, pursuant to the authority hereby given, are hereby ratified and confirmed.

This Power of Attorney is made and executed pursuant to and by authority of the By-Law printed on the reverse hereof, duly adopted, as indicated, by the shareholders of the corporation.

In Witness Whereaf, WESTERN SURETY COMPANY has caused these presents to be signed by its Vice President and its corporate seal to be hereto affixed on this 25th day of June, 2015.



WESTERN SURETY COMPANY

Paul T. Bruflat, Vice President

State of South Dakota County of Minnehaha

55

On this 25th day of June, 2015, before me personally came Paul T. Bruflat, to me known, who, being by me duly swom, did depose and say: that he resides in the City of Sioux Falls, State of South Dakota; that he is the Vice President of WESTERN SURETY COMPANY described in and which executed the above instrument; that he knows the seal of said corporation; that the seal affixed to the said instrument is such corporate seal; that it was so affixed pursuant to authority given by the Board of Directors of said corporation and that he signed his name thereto pursuant to like authority, and acknowledges same to be the act and deed of said corporation.

My commission expires

February 12, 2021



WESTE'RN SURETY COMPANY

S. Reland L. Nelson, Assistant Secretary

CERTIFICATE

Eich Notary Public

I, L. Nelson, Assistant Secretary of WESTERN SURETY COMPANY do hereby certify that the Power of Attorney hereinabove set forth is still in force, and further certify that the By-Law of the corporation printed on the reverse hereof is still in force. In testimony whereof I have hereunto subscribed my name and affixed the seal of the said corporation this 13 day of _ anua

Form F4280-7-2012

STATE OF MICHIGAN)

)SS COUNTY OF OAKLAND)

Larry Brennan, being duly sworn, deposes and says:

That he makes Sworn Statement on behalf of NAGLE PAVING who is the (contractor) (subcontractor) for an improvement to the following described real property situated in Oakland County Michigan, and described as follows: (Insert legal description from Notice of Commencement) City of Novi Civic Center

Novi, MI

That the following is a statement of each subcontractor and supplier and laborer, for which laborer the payment of wages or fringe benefits and withholdings is due but unpaid, with whom the (contractor) (subcontractor) has (contracted) (subcontracted) for performance under the contract with the owner of lessee thereof, and that the amounts due to the persons as of the date thereof are correctly and fully set forth opposite their names as follows:

Name of subcontractor, supplier or taborer	Type of improvement furnished	Total contract price	Amount already paid	Amount currently owing	Balance to complete (opt)	Amt of Jabor wages due but unpaid	Amt of labor fringe benefits & withholding due but unpaid
Nagle Paving	Asphalt Paving	68,462,50	56,462.50	12.000.00	0.00	0.00	0.00
H.G. Sartor Asphalt Paving	Paving Path	5,400.00	5,400.00	0.00	0.00	0.00	0.00
Nagle Paving	Paving	All labor, fr	inges, payroll	taxes and oth	er payroll o	obligation	is paid in full
TOTALS		73,862.50	61,862.50	12,000.00	0.00	0.00	0,00

That the contractor has not procured material from, or subcontracted with, any person other than those set forth above and owes no money for the improvement.

Deponent further says that he or she makes the foregoing statement as the (contractor) (subcontractor) or as Vice President of the (contractor) (subcontractor) for the purpose of representing to the owner or lessee of the above-described premises and his or her agents that the above-described property is free from claims of construction liens, or the possibility of construction liens, except as specifically set forth above and except for claims of construction liens by laborers which may be provided pursuant to section 109 of the construction lien act. Act No. 497 of the Public Acts of 1980. as amended, being section 570,1109 of the Michigan Complied Laws.

WARNING TO OWNER: AN OWNER OR LESSEE OF THE ABOVE-DESCRIBED PROPERTY MAY NOT RELY ON THIS SWORN STATEMENT TO AVOID THE CLAIM OF A SUBCONTRACTOR, SUPPLIER, OR LABORER WHO HAS PROVIDED A NOTICE OF FURNISHING OR A LABORER WHO MAY PROVIDE A NOTICE OF FURNISHING PURSUANT TO SECTION 109 OF THE CONSTUCTION LIEN ACT TO THE DEIGNEE OR THE OWNER OR LESSEE IF THE DESIGNEE IS NOT NAMED OR HAS DIED.

WARNING TO DEPONENT; AN PERSON, WHO WITH INTENT TO DEFRAUD, GIVES A FALSE SWORN STATEMENT IS SUBJECT TO CRIMINAL PENALTIES AS PROVIDED IN SECTION 110 OF THE CONSTRUCTION LIEN ACT, ACT NO. 497 OF THE PUBLIC ACTS OF 1980, AS AMENDED, BEING SECTION 570.2220 OF THE MICHIGAN COMPLIED LAWS.

Subscribed and sworn to before me this 18th Day of January, 2016 **Notary Public**

Macomb County, Michigan

My commission expires: December 27, 2018

DAWN M. GONLON NOTARY PUBLIC - STATE OF MICHIGAN COUNTY OF MACOMB My Commission Explored Dec, 27 Acting in the County of

PARTIAL CONDITIONAL WAIVER

.

	contract with asphalt paving	City of Novi (other contracting) parly)	
for the impre	ovement to the p	property described as: Novi Civic	Ctr N Lot/Power Park Paths	
and hereby	waive my/our co	nstruction lien to the amount of	\$12,000.00 for labor and materials provided	
through	January 13,	•		
me/us for co	r, together with ntract improven			
		•	Larry Brennan, Vice Presid)ent
		By:	(Elenetre or tier telement)	
		Address:	39525 W 13 Mile Road Ste 300	
			Novi, MI 48377	
		Telephone:	248 553 0600	
Signed on: _	1-18- (date)	16	e e e e y source e e e e e e e e e e e e e e e e e e	

DO NOT SIGN BLANK OR INCOMPLETE FORMS. RETAIN A COPY.

THE CONSTRUCTION ASSOCIATION OF MICHIGAN EXPRESSLY DISCLAIMS ANY LIABILITY FOR CHANGES MADE TO THIS FORM BY LEGISLATIVE ENACTMENTS OR JUDICIAL DECISIONS.

FULL UNCONDITIONAL WAIVER

My/our contract with		Nagle Pa	ving Company	and the second	And billing to a second a second s
to provide	Paving Work		(other contracting party)		2022-00224-00-40225-00-0225-00-02
for the imp	rovement to the	property described as:	ىرىمى ئىرىمى بىرىمى بىرىكى مۇرىيىتى بىرىمىيى بىرىكى بىرىكى بىرىكى بىرىكى بىرىكى بىرىكى بىرىكى بىرىكى بىرىكى بىر ئىرىكى بىرىكى	سی می واقع این می واقع می واقع این می واقع این می واقع می واقع می واقع می واقع این می واقع این می واقع این می واقع این می واقع این می واقع این واقع ای	
			Novi Civic Cente	er	

having been fully paid and satisfied, all my/our construction lien rights against such property are hereby waived and released.

	H.G. Sartor Asphalt Paying				
By:	H.G.S Owner				
Address: PO Box 543					
	Walled Lake MI 48390				
Telephone:	248 669 6611				

Signed on: 12-6-2015

DO NOT SIGN BLANK OR INCOMPLETE FORMS. RETAIN A COPY.

THE CONSTRUCTION ASSOCIATION OF MICHIGAN EXPRESSLY DISCLAIMS ANY LIABILITY FOR CHANGES MADE TO THIS FORM BY LEGISLATIVE ENACTMENTS OR JUDICIAL DECISIONS.
