

CITY of NOVI CITY COUNCIL

Agenda Item L May 9, 2016

SUBJECT: Approval of the final payment to Nagle Paving Company for the 2014 Neighborhood Road Program-Contract 1A project in the amount of \$32,443.25, plus interest earned on retainage.

SUBMITTING DEPARTMENT: Department of Public Services, Engineering Division

C

ITY	MANAGER	APPROVAL:	OB	
CALLS:			1 3857 2000	۰

EXPENDITURE REQUIRED	\$ 32,443.25
AMOUNT BUDGETED	\$ 350,853.00
LINE ITEM NUMBER	203-203.00-865.434

BACKGROUND INFORMATION:

A construction contract for the 2014 Neighborhood Roads-Contract 1 (Asphalt) was awarded to Pavex Corporation in the amount of \$1,166,945. The project included all of the streets in the Haverhill Farms Subdivision as well as the streets listed in the table below. A Notice-to-Proceed was issued to the contractor on August 11, 2014 and the contractor was required to complete the project by November 9, 2014. Unfortunately, the contractor failed to meet the schedule and was only able to complete the work in Haverhill Farms, which was also behind schedule after many delays.

The construction contract allows the City to remove work from the contract. Two change orders removing the incomplete portions of the project were issued in January 2015 resulting in a decrease of \$500,225 for the original Contract 1 project. The remainder of the work was re-bid as 2014 Neighborhood Roads Contract 1A (Asphalt) to Nagle Paving Company and included these streets:

Road Segment	From	То	Material	Treatment
Malott Dr.	Meadowbrook Rd.	W. LeBost Dr.	Asphalt	Reconstruct
W. LeBost Dr.	Malott Dr.	200 feet	Asphalt	Reconstruct
Wedgewood Dr.	Pontiac Trail	Springlake Blvd.	Concrete to Asphalt	Reconstruct

The construction contract was awarded for this project at the February 9, 2015 City Council meeting to Nagle Paving Company in the amount of \$431,235.25.

Engineering staff worked with the engineering consultant for this project, Spalding DeDecker & Associates, Inc., to review and verify the final contract payment amount of \$32,443.25 that is due the contractor (Final Pay Estimate No. 5, attached). The City Attorney reviewed the documentation and found it to be in an acceptable form (Beth Saarela's April 27, 2016 letter, attached).

There were three (3) approved change order issued for this project resulting in a net decrease of \$59,089.07 from the construction contract, or 13.7% under the awarded amount. The approved change orders resulted in a final contract price of \$372,146.18.

RECOMMENDED ACTION: Approval of the final payment to Nagle Paving Company for the 2014 Neighborhood Road Program-Contract 1A project in the amount of \$32,443.25, plus interest earned on retainage.

	1	2	Y	N
Mayor Gatt				
Mayor Pro Tem Staudt				
Council Member Casey				
Council Member Markham				

	1	2	Y	Z
Council Member Mutch				
Council Member Burke				
Council Member Wrobel				

2014 NEIGHBORHOOD ROAD PROGRAM **CONTRACT 1A** February 2015 Fourteen Mile Rd W Ponffac Til Wedgewood Drive South Lake De Ų Twelve Mile Rd alve Mile Rd Twelve Mile Rd Grand River Ave **791**1 f D Malott & W.Lebost City of Novi Project: 2014 NRP Contract 1A Version #: v3.0 Engineering Division Department of Public Services 26300 Lee BeGole Drive Novi, MI 48375 cityofnovi.org MAP INTERPRETATION NOTICE Map Legend 0 750 1,500


1 inch = 3,850 feet

2014 Asphalt

2014 NRP – Asphalt Streets – Contract 1A




Wedgewood Drive – Looking north from Springlake Boulevard.

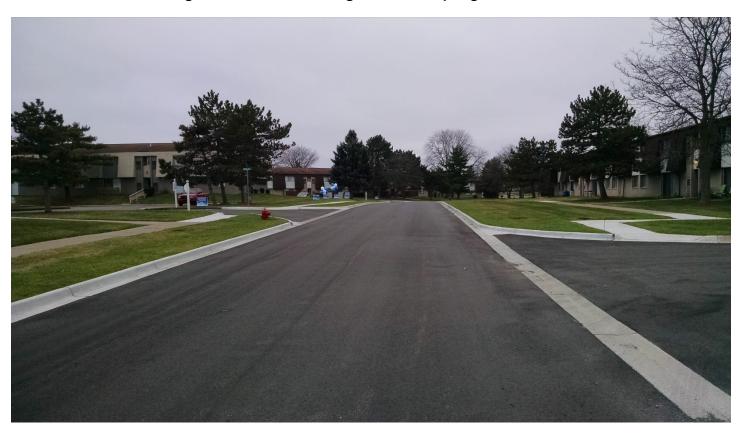

Wedgewood Drive – Looking south from Pontiac Trail.



Wedgewood Drive – Looking south

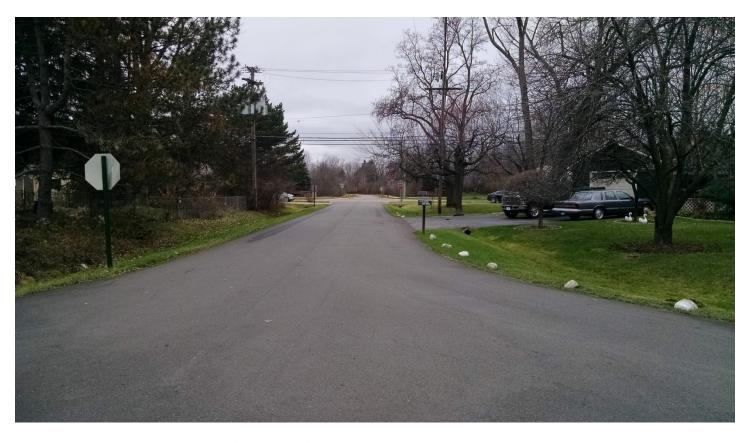

Malott Drive – Looking west towards Meadowbrook Road.



West LeBost Drive – Looking south.



JOHNSON ROSATI SCHULTZ JOPPICH PC

27555 Executive Drive Suite 250 ~ Farmington Hills, Michigan 48331 Phone: 248.489.4100 | Fax: 248.489.1726

Elizabeth Kudla Saarela esaarela@jrsjlaw.com

www.jrsjlaw.com

April 27, 2016

Aaron Staup, Engineering Coordinator CITY OF NOVI Department of Public Services Field Services Complex 26300 Lee BeGole Drive Novi, MI 48375

Re: 2014 Neighborhood Roads Program – Asphalt 1A – Nagle Paving Closing Documents

Dear Mr. Staup:

We have received and reviewed closing documents for the 2014 Neighborhood Roads- Asphalt 1A- Project:

- 1. Application for Final Payment
- 2. Contractor's Sworn Statement
- 3. Consent of Surety
- 4. Waivers of Lien

Subject to approval of the Application for Final Payment by appropriate City staff, the closing documents appear to be in order. The existing Maintenance Bond amount is adequate on the basis that the contract price was not increased during the term of the contract. The General Contractor must provide its final waiver of lien time it receives final payment.

Please feel free to contact me with any questions or concerns in regard to this matter.

Very truly yours,

Elizabeth Kudla Saarela

JOHNSON, ROSATI, SCHULTZ & JOPPICH, P.C.

Aaron Staup, Construction Engineering Coordinator April 27, 2016 Page 2

EKS

Enclosures

C: Maryanne Cornelius, Clerk (w/Enclosures)

Rob Hayes, Public Services Director (w/Enclosures)

Carl Johnson, Finance Director/Chief Financial Officer (w/Enclosures)

Brian Coburn, Engineering Manager (w/Enclosures)

John E. Becht, Nagle Paving (w/Enclosures)

Thomas R. Schultz, Esquire (w/Enclosures)



Balance Due This Payment = \$ 32,443.25 PURCHASE ORDER NO. 94446

26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

APPLICATION FOR FINAL PAYMENT

PROJECT:

2014 NRP - Asphalt Contract 1A

45175 W. Ten Mile Road

Novi, Michigan 48375

NOVI PROJECT NO.:

15-2101

PAYMENT NO .:

FINAL

OWNER:

City of Novi

ENGINEER:

Spalding DeDecker & Associates 905 South Boulevard East

CONTRACTOR:

Nagle Paving Company 39525 W. 13 Mile, Suite 300

Rochester, Michigan 48037 (248) 844-5400

Novi, Michigan 48377 (248) 553-0600

CONTRACT AMOUNT

FINAL COMPLETION DATES

DATES OF ESTIMATE

ORIGINAL:

\$431,235.25

ORIGINAL: REVISED:

June 27, 2015

FROM:

September 18, 2015

REVISED:

\$372,146.18

ACTUAL:

July 13, 2015 September 23, 2015

TO:

Completion

SECTION 1.

COST OF COMPLETED WORK TO DATE

 CONTRACT ITEMS (Original)	CONTRACT ITEMS (Revised)	

Item			C	CONTRACT	ITEMS (C	Original)	(CONTR	RACT ITEMS	(Rev	/ised)		TH	IIS PERIOD			T	OTAL TO DATE	
No.	Description of Item	Unit	Quantity	Cost/U	nit	Total Amt	Quantity	c	Cost/Unit		Total Amt	Quantity		Amount	%	Quantity		Amount	%
0	Constr. Inspection "Crew Day"	CD	37.00	\$ 64	40.00	\$ 23,680.00	37.00	\$	640,00	\$	23,680.00					60.25	\$	38,560.00	163%
1	Bonds, Insurance & Mobilization	LS	1.00	\$ 14,00	00.00	\$ 14,000.00	1.00	\$	14,000.00	\$	14,000.00					1.00	\$	14,000.00	100%
2	Pre-Construction Audio/Video	LS	1.00	\$ 1,20	00.00	\$1,200.00	1.00	\$	1,200.00	\$	1,200.00					1.00	\$	1,200.00	100%_
3	Soil Erosion Control Measures	LS	1.00	\$ 5,20	00.00	\$ 5,200.00	1.00	\$	5,200.00	\$	5,200.00	0.50	\$	2,600.00	50%	1.00	\$	5,200.00	100%
4	Maintaining Traffic	LS	1.00	\$ 6,00	00.00	\$ 6,000.00	1.00	\$	6,000.00	\$	6,000.00					1.00	\$	6,000.00	100%
5	Tree Protection Fencing	LF	1158.00	\$	3.00	\$3,474.00	940.00	\$	3.00	\$	2,820.00					940.00	\$	2,820.00	100%
6	Remove Sidewalk	SF	900.00	\$	1.00	\$ 900.00	1266.41	\$	1.00	\$	1,266.41					1266.41	\$	1,266.41	100%
7	HMA Surface, Remove	SY	1400.00	\$	3.50	\$4,900.00	1251.41	\$	3.50	\$	4,379.94					1251.41	\$	4,379.94	100%
8	Pavement, Remove	SY	3815.00	\$	6.00	\$ 22,890.00	3375.42	\$	6.00	\$	20,252.52					3375.42	\$	20,252.52	100%
9	Excavation, Earth	CY	2380.00	\$	14.00	\$ 33,320.00	1914.42	\$	14.00	\$	26,801.88		Ι.			1914.42	\$	26,801.88	100%
10	Subgrade Undercut (as needed)	CY_	700.00	\$.	40.00	\$ 28,000.00	378.03	\$	40.00	\$	15,121.20					378.03	\$	15,121.20	100%
11	Aggregate Base, 6-inch	SY	1325.00	\$	7.50	\$ 9,937.50	988.28	\$	7.50	\$	7,412.10					988,28	\$	7,412.10	100%
12	Aggregate Base, 8-inch	SY	5695.00	\$	7.50	\$ 42,712.50	4914.23	\$	7.50	\$	36,856.73	354.67	\$	2,660.03	7%	4914.23	\$	36,856.73	100%
13	Geogrid	SY	4435.00	\$	4.05	\$ 17,961.75	4435.00	\$	4.05	\$	17,961.75					4435.00	\$	17,961.75	100%
_14	Underdrain, 6-inch, w/Geowrap	LF	3075.00	\$	12.00	\$ 36,900.00	2568.00	\$	12.00	\$	30,816.00			•		2568.00	\$	30,816.00	100%
15	Driveway Opening, Conc, Det M	LF	404.00	\$	15.00	\$6,060.00	288.50	\$	15.00	\$	4,327.50					288.50	\$	4,327.50	100%
16	Curb and Gutter, Conc, Det F-2	LF	2221.00	\$	13.50	\$ 29,983.50	2045.50	\$	13.50	\$	27,614.25					2045.50	\$	27,614.25	100%
17	HMA, 3C	TON	550.00	\$	72.50	\$ 39,875.00	473.52	\$	72,50	\$	34,330.20					473.52	\$	34,330.20	100%
18	HMA, 5E1	TON	540.00	\$	80.00	\$ 43,200.00	449.86	\$	80.00	\$	35,988.80					449.86	\$	35,988.80	100%
_19	Interlayer	SY	4310.00	\$	4.50	\$ 19,395.00	3809.56	\$	4.50	\$	17,143.02					3809.56	\$	17,143.02	100%
20	Sidewalk Grading	STA	13.90	\$ 7	00.00	\$ 9,730.00	13.90	\$	700.00	\$	9,730.00					13.90	\$	9,730.00	100%
21	Sidewalk, Conc, 4-inch	SF	7640.00	\$	3.40	\$ 25,976.00	7929.38	\$	3.40	\$	26,959.89					7929.38	\$	26,959.89	100%
22	ADA Ramp, Conc, 6-inch	SF	1140.00	\$	5.50	\$ 6,270.00	583.00	\$	5.50	\$	3,206.50					583.00	\$	3,206.50	100%
23	ADA Detectable Warning Plate	SF	50.00	\$	22.00	\$ 1,100.00	50.00	\$	22.00	\$	1,100.00					50.00	\$	1,100.00	100%
24	Str Rehab Type 1: Point Up	EA	2.00	\$ 2	50.00	\$ 500,00	3.00	\$	250.00	\$	750.00					3.00	\$	750.00	100%



26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

APPLICATION FOR FINAL PAYMENT

PROJECT: 2014 NRP - Asphalt Contract 1A

NOVI PROJECT NO .:

15-2101

PAYMENT NO .:

FINAL

	SECTION 1.							COST OF COMPLETED WORK TO DATE												
Item				CONT	RACT ITEMS	(Origir	nal)	CONTRACT ITEMS (Revised)						Τŀ	IS PERIOD		TOTAL TO DATE			
No.	Description of Item	Unit	Quantity		Cost/Unit		Total Amt	Quantity		Cost/Unit		Total Amt	Quantity		Amount	%	Quantity		Amount	%
25	Str Rehab Type 2: Cover Adjust	EA	4.00	\$	350.00	\$	1,400.00	7.00	\$	350.00	\$	2,450.00					7.00	\$	2,450.00	100%
26	Str Rehab Type 3: Reconstruct	EA	9.00	\$	700.00	\$	6,300.00	2.00	\$	700.00	\$	1,400.00					2.00	\$	1,400.00	100%
27	Dr. Structure Cover, Type B	EA	6.00	\$	550.00		3,300.00	6.00	\$	550.00		3,300.00					6.00	\$	3,300.00	100%
_28	Restoration	LS	1.00	\$	10,500.00	_	10,500.00	1.00	\$	10,500.00		10,500,00	0.50	\$	5,250.00	50%	1.00	\$	10,500.00	100%
29	Permit Allowance (RCOC)	LS	1.00	\$	250.00	\$	250.00	1.00	\$	250.00	\$	250.00	1.00	\$	250.00	100%	1.00	\$	250.00	100%
_																				
				+					+					-						
				+-																
				_					+					 				ļ		
				+					+											
				-					+					<u> </u>						
		-		+-		-			+					-						
				+					+	· · · · · · · · · · · · · · · · · · ·				_						
	TOTAL FROM THIS SHEE	T T		上	~~	\$	21,750.00		1		\$	17,900.00		\$	5,500.00			\$	17,900.00	
	TOTAL FROM OTHER SHEE	ET .				\$	409,485.25				\$	351,238.68		\$	5,260.03			\$	351,238.68	
	SUBTOTA	AL.				\$	431,235.25				\$	369,138.68		\$	10,760.03			\$	369,138.68	100%



26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454

Fax: (248) 735-5659

			VMEN	

PROJECT:

2014 NRP - Asphalt Contract 1A

NOVI PROJECT NO .:

15-2101

PAYMENT NO .:

FINAL

NEW CONTRACT ITEMS

	SECTION 1.					COST OF COMPLETED WORK TO DATE												
Item						:	NEW CONTRAC				THIS PERIOD			тот	AL TO DATE			
No.	Description of Item	Unit	Division	GL#		Quantity Cost/Unit Total Amt		Quantity Amount %		%	Quantity Amount		Amount	%				
30			0	0		0.00	\$	\$	-				0.00	\$	-			
31	Lebost Culvert Replacement	LS	0	0		1.00	\$ 3,007.50	\$	3,007.50				1.00	\$	3,007.50	100%		
32			0	0		0.00	\$ -	\$					0.00	\$				
33			0	0		0.00	\$	\$	-				0.00	\$				
34			0	0		0.00	\$ -	\$					0.00	\$				
35			0	0		0.00	\$ -	\$					0.00	\$	-			
36			0	0		0.00	\$ -	\$					0.00	\$	-			
_37			0	0		0.00	\$ -	\$					0.00	\$				
38			0	0		0.00	\$ -	\$					0.00	\$				
39			0	0		0.00	\$ -	\$					0.00	\$	-			
40			0	0		0.00	\$ -	\$					0.00	\$				
41			0	0		0.00	\$ -	\$					0.00	\$				
42			0	0		0.00	\$ -	\$					0.00	\$	-			
_43			0	0		0.00	\$ -	\$	-				0.00	\$				
44			0	0		0.00	\$ -	\$					0.00	\$	-			
45			0	0		0.00	\$ -	\$					0.00	\$				
46			0	0		0.00	\$ -	\$					0.00	\$	-	ļ		
47			0	0		0.00	\$ -	\$					0.00	\$	-	ļ		
48			0	0		0.00	\$ -	\$					0.00	\$				
49			0	0		0.00	\$ -	\$					0.00	\$				
50			0	0		0.00	\$ -	\$					0.00	\$				
51			0	0_		0.00	\$ -	\$					0.00	\$	- '			
52			0	0		0.00	\$ -	\$					0.00	\$		ļ		
53			0	0		0.00	\$ -	\$					0.00	\$				
54			0	0		0.00	\$ -	\$	-				0.00	\$		<u> </u>		
_55			0	0		0.00	\$ -	\$					0.00	\$				
_56			0	0		0.00	\$ -	\$					0.00	\$				
_57			0	0		0.00	\$	\$			<u> </u>		0.00	\$				
	TOTAL FROM THIS SHEE	ET		-				\$	3,007.50		\$ -			\$	3,007.50			
	TOTAL FROM OTHER SHEET	rs		\$	431,235.25			\$	369,138.68		\$ 10,760.03			\$	369,138.68			
	GRAND TOTA	AL.		\$	431,235.25			\$	372,146.18		\$ 10,760.03			\$	372,146.18	100%		



PURCHASE ORDER NO. 94446 26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

Section 2.							
		APPLICATION	FOR FIN	IAL PAYMENT			
PROJECT: 2014 NRP - Asphalt Contract 1A	NOVI PROJ	ECT NO.: 15-210	1	pagapun kenabasah mati kepaban paraban pendapan dan dalam da bahar	PAYM	ENT NO.:	FINAL
Original Contract Amount:	\$	431,235.25		CHANGE OF	RDERS		
Change Orders:	\$	(59,089.07)	<u>No.</u> 1	<u>Date</u> June 1, 2015	\$	Amount 3,007.50	
Adjusted Contract Amount to Date:	\$	372,146.18	2	August 20, 2015 December 12, 2015	\$ \$	(578.20) (61,518.37)	
Total Cost of Work Performed to Date:	\$	372,146.18		·	\$ \$	-	
MINUS Retainage: MINUS Inspection "Crew Days": To Date This Pay	0% \$ 60.25 \$ 0.00	14,880.00			\$ \$ \$	-	
Net Amt. Earned of Contract and Extra Work to Date:	\$	357,266.18			\$ \$	-	
MINUS L.D.'s: # of days over = \$ \$ amount/day = \$ \$600	\$	-			\$ \$	-	
Subtotal:	\$	357,266.18			\$		_
ADD Incentive "Crew Days", if under:	\$	-		ТОТА	AL: \$	(59,089.07)
Subtotal:	\$	357,266.18					
MINUS Amount of Previous Payments: 1 \$ 47,036.30 2 \$ 69,153.10	\$	324,822.93					_
3 \$ 135,343.97 4 \$ 73,289.56				Inspection "Crew Days" All Additional "Crew Days" per			
5 \$ -				Total Inspection "Crew Day	ys" Allowed:	37.00	
6 \$ - 7 \$ -				Inspection "Crew Days" Us Inspection "Crew Days" Re		60.25 -23.25	
8 \$ - 9 \$ - 10 \$ -					_	···-	
BALANCE DUE THIS PAYMENT:	\$	32,443.25					



26300 Lee BeGale Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

Sect	ion	з.

APPLICATION FOR FINAL PAYMENT CT NO.: 15-2101

PROJECT:

2014 NRP - Asphalt Contract 1A

NOVI PROJECT NO .:

PAYMENT NO .:

is recommended.

CITY OF NOVI

Payment of the above AMOUNT DUE THIS APPLICATION

Aaron J. Staup, Construction Engineering Coordinator

The undersigned CONTRACTOR certifies that: (1) Any previous progress payments received from OWNER on amount of Work done under the Contract referred to above have been applied to discharge in full all obligations of CONTRACTOR incurred in connection with Work covered by prior Applications for Payment; (2) title to all Work, materials, and equipment incorporated in said Work of otherwise listed in or covered by this Application for Payment will pass to OWNER at time of payment free and clear of all leins, claims, security interest, and encumberences (except such as are covered by Bond acceptable to OWNER indemnifying OWNER against any such lein, claim security interest, or encumberence); and (3) all Work covered by this Application for Payment is in accordance with the Contract Documents and not defective as that term is defined in the Contract Documents.

		2 1-11	Dated:	41	26 16
lagle Paving Company	Date:	3-1-16		^ - <i>(</i>	Digitally signed by Brian Coburn DN: cn=Brian Coburn, o=City of Novi,
Contractor Company			H	5-11	ou=Department of Public Services, email=bcoburn@cityofnovi.org, C=US Date: 2016.04.27 16:24:29 -04'00'
Contractor Authorized Signature					
Print Name			By:	Brian Coburn, PE., Er	igineering Senior Manager
		/ /	Dated:		
Spalding DeDecker & Associates	Date:	03/29/2016			
Consultant Firm		/ /			
fre L. Beld		All Full Unconditional Waivers of lien have been received from			
Consultant Authorized Signature		the Consultant. Also, attached to this Final Payment is a copy a new Maintenance and Guarantee Bond (if the amount is gre	of the Contra	actor's Swom Statement, C	onsent of Surety, and aintenance Bond Rider
BY: / JOHN B BECHT		covering the difference between the final contract price and the			antendroe bord rider
✓ Print Name					

CONSENT OF SURETY COMPANY TO FINAL PAYMENT MAIXXXVIII NI 0200 Obster Architect Contractor Surely Other

Bond No 929606865

PROJECT: 2014 Neighborhood Road Program - Asphalt - Contract 1A (name, midress)

TO: (charge)

ARCHITECT'S PROJECT NO:

City of Novi

45175 West Ten Mile Road

CONTRACT FOR:

Novi, MI 48375

CONTRACT DATE: 2/10/2015

CONTRACTOR:

Nagle Paving Company 39525 West 13 Mile Road Novi, MI 48377

In accordance with the provisions of the Contract between the Owner and the Contractor as indicated above, the

Western Surety Company One Towne Square, Suite 1075 Southfield, MI 48076

SURETY COMPANY

no bond of their shear rame and added of Contractor)

Nagle Paving Company 39525 West 13 Mile Road Novi, MI 48377

CONTRACTOR,

hereby approves of the final payment to the Contractor, and agrees that final payment to the Contractor shall not relieve the Strety Company of any of its obligations to these eventuage and address of Owner)

City of Novi 45175 West Ten Mile Road Novi, MI 48375

OWNER.

as set forth in the said Surety Company's bond.

IN WITNESS WHEREOF.

the Surety Company has hereinto set its hand this

16th

day of December, 2015

Surety Company
Western Surety Company

Signature of Authorized Representative

titest:

Susan L Small, Attorney-in-Fact

Tetle

NOTE THE Earn is to be real as a comparion decement or ATV DOLD MENT GOOD, CONTRACTOR'S APPROADED PAYMENT OF DEBTE AND LEARNING, Concernable of

MA DOX LAGNE GROWGINSLIN LOG STIRFFY COMPANY TO FEAR PAYMENT-APPRIL 1970 FOR HORION-AGAP PAGE 480

A PROBABILIA MERICAN INSTITUTE OF ARCHITECUS, 1735 MEW YORK, AVE., NW, WASHINGTON, D.C. 2000b

Western Surety Company

POWER OF ATTORNEY APPOINTING INDIVIDUAL ATTORNEY-IN-FACT

Know All Men By These Presents, That WESTERN SURETY COMPANY, a South Dakota corporation, is a duly organized and existing corporation having its principal office in the City of Sioux Falls, and State of South Dakota, and that it does by virtue of the signature and seal herein affixed hereby make, constitute and appoint

Steven K Brandon, T J Griffin, William A Pirret, John L Budde, Terence J Griffin, Susan L Small, Patrick Williams, Individually

of Farmington Hills, MI, its true and lawful Attorney(s)-in-Fact with full power and authority hereby conferred to sign, seal and execute for and on its behalf bonds, undertakings and other obligatory instruments of similar nature

- In Unlimited Amounts -

and to bind it thereby as fully and to the same extent as if such instruments were signed by a duly authorized officer of the corporation and all the acts of said Attorney, pursuant to the authority hereby given, are hereby ratified and confirmed.

This Power of Attorney is made and executed pursuant to and by authority of the By-Law printed on the reverse hereof, duly adopted, as indicated, by the shareholders of the corporation.

In Witness Whereof, WESTERN SURETY COMPANY has caused these presents to be signed by its Vice President and its corporate seal to be hereto affixed on this 25th day of June, 2015.

SEAVE THE RESERVE

WESTERN SURETY COMPANY

Paul T Bruflat Vice President

State of South Dakota County of Minnehaha . s

On this 25th day of June, 2015, before me personally came Paul T. Bruflat, to me known, who, being by me duly sworn, did depose and say: that he resides in the City of Sioux Falls, State of South Dakota; that he is the Vice President of WESTERN SURETY COMPANY described in and which executed the above instrument; that he knows the seal of said corporation; that the seal affixed to the said instrument is such corporate seal; that it was so affixed pursuant to authority given by the Board of Directors of said corporation and that he signed his name thereto pursuant to like authority, and acknowledges same to be the act and deed of said corporation.

February 12, 2021



S. Eich, Notary Public

CERTIFICATE



WESTERN SURETY COMPANY

J. Nelson, Assistant Secretary

Authorizing By-Law

ADOPTED BY THE SHAREHOLDERS OF WESTERN SURETY COMPANY

This Power of Attorney is made and executed pursuant to and by authority of the following By-Law duly adopted by the shareholders of the Company.

Section 7. All bonds, policies, undertakings, Powers of Attorney, or other obligations of the corporation shall be executed in the corporate name of the Company by the President, Secretary, and Assistant Secretary, Treasurer, or any Vice President, or by such other officers as the Board of Directors may authorize. The President, any Vice President, Secretary, any Assistant Secretary, or the Treasurer may appoint Attorneys in Fact or agents who shall have authority to issue bonds, policies, or undertakings in the name of the Company. The corporate seal is not necessary for the validity of any bonds, policies, undertakings, Powers of Attorney or other obligations of the corporation. The signature of any such officer and the corporate seal may be printed by facsimile.

SWORN STATEMENT

STATE OF MICHIGAN)
)SS
COUNTY OF OAKLAND)

Rob Nagle, being duly sworn, deposes and says:

That he makes Sworn Statement on behalf of NAGLE PAVING who is the (contractor) (subcontractor) for an improvement to the following described real property situated in Oakland County Michigan, and described as follows: (Insert legal description from Notice of Commencement)

Novi Neighborhood Roads

That the following is a statement of each subcontractor and supplier and laborer, for which laborer the payment of wages or fringe benefits and withholdings is due but unpaid, with whom the (contractor) (subcontractor) has (contracted) (subcontracted) for performance under the contract with the owner of lessee thereof, and that the amounts due to the persons as of the date thereof are correctly and fully set forth opposite their names as follows:

Name of subcontractor, supplier or laborer	Type of improvement furnished	Total contract price	Amount already paid	Amount currently owing	Balance to complete (opt)	Amt of labor wages due but unpaid	Amt of labc fringe benefits & withholding due but unpaid
Nagle Paving	Asphalt Paving	313,011.18	280,567.93	32,443.25	0.00	0.00	0.00
Road Fabrics	Interlayer	16,348.00	16,348.00	0.00	0.00	0.00	0.00
CSI Geoturf	Geogrid	22,162.00	22,162.00	0.00	0.00	0.00	0.00
Gaz Contracting	Sawcutting	1,275.00	1,275.00	0.00	0.00	0.00	0.00
Tyler Companies	Landscape	4,470.00	4,470.00	0.00	0.00	0.00	0.00
Nagle Paving	Paving	All labor, fringes, payroll taxes and other payroll obligations paid in full					
TOTALS		357,266.18	324,822.93	32,443.25	0.00	0.00	0.00

That the contractor has not procured material from, or subcontracted with, any person other than those set forth above and owes no money for the improvement.

Deponent further says that he or she makes the foregoing statement as the (contractor) (subcontractor) or as Vice President of the (contractor) (subcontractor) for the purpose of representing to the owner or lessee of the above-described premises and his or her agents that the above-described property is free from claims of construction liens, or the possibility of construction liens, except as specifically set forth above and except for claims of construction liens by laborers which may be provided pursuant to section 109 of the construction lien act, Act No. 497 of the Public Acts of 1980, as amended, being section 570.1109 of the Michigan Complied Laws.

WARNING TO OWNER: AN OWNER OR LESSEE OF THE ABOVE-DESCRIBED PROPERTY MAY NOT RELY ON THIS SWORN STATEMENT TO AVOID THE CLAIM OF A SUBCONTRACTOR, SUPPLIER, OR LABORER WHO HAS PROVIDED A NOTICE OF FURNISHING OR A LABORER WHO MAY PROVIDE A NOTICE OF FURNISHING PURSUANT TO SECTION 109 OF THE CONSTUCTION LIEN ACT TO THE DEIGNEE OR THE OWNER OR LESSEE IF THE DESIGNEE IS NOT NAMED OR HAS DIED.

Deponent

WARNING TO DEPONENT: AN PERSON, WHO WITH INTENT TO DEFRAUD, GIVES A FALSE SWORN STATEMENT IS SUBJECT TO CRIMINAL PENALTIES AS PROVIDED IN SECTION 110 OF THE CONSTRUCTION LIEN ACT, ACT NO. 497 OF THE PUBLIC ACTS OF 1980, AS AMENDED, BEING SECTION 570.2220 OF THE MICHIGAN COMPLIED LAWS.

Mbscribed and sworn to before me this 7th

DXXXXXII

Macomb County, Michigan

My commission expires: 12-27-2018

DAWN M. CONLON NOTARY PUBLIC - STATE OF MICHIGAN COUNTY OF MACOMB

My Commission Expires Dec., Acting in the County of

FULL UNCONDITIONAL WAIVER

My/our cor	ntract with	Nagle	e Paving			
to provide	Landscape		(ollier contracting pa	ny)	and the second s	
for the imp	rovement to t	the property described as:	N	lovi Roads		
having bee	n fully paid a	nd satisfied, all my/our cons	struction Ilen	rìghts against such	property are herei	эу
waived and	d released.					
			 By:	CAZL	Companies	
			Address:	- I wanted	Box 930617	
			radigos.	and provide a property of the second	m, MI 48393	<u></u>
		Ĩ	elephone:		882 5303	
Signed on:	3-4	1.2016	• *************************************	TODD Presi		-
Signice on		date)		tresi	DENT	•

DO NOT SIGN BLANK OR INCOMPLETE FORMS. RETAIN A COPY.

THE CONSTRUCTION ASSOCIATION OF MICHIGAN EXPRESSLY DISCLAIMS ANY LIABILITY FOR CHANGES MADE TO THIS FORM BY LEGISLATIVE ENACTMENTS OR JUDICIAL DECISIONS.

FROM NAGLE PAYING

(THU) MAR @ 2018 8:18/51, 8:17/No. TOXO0109A7 P A

FULL UNCONDITIONAL WAIVER

My/our cor	itract with	Nagle Paving	
to provide	saw outling	(alhar confrecting berly)	retirement of the second secon
for the imp	rovement to the prope	rty described as:	t testes and a second s
		Novi Roads	
having bee	n fully paid and satisfic	ed, all my/our construction flen rig	hts against such property are hereby
waived and	released.		
			GAZ Contracting
		Ву:	Jerry Jan (1912)
		Address:	31095 Schoolcraft
		Account of the Control of the Contro	Livonia, MI 48150
		Telephone:	734 425 1555
			JOE GAZDECKI
Signed on:	3-3-16 (delo)	AL-STROMOTOR	PRESIDENT

DO NOT SIGN BLANK OR INCOMPLETE FORMS. RETAIN A COPY.

THE CONSTRUCTION ASSOCIATION OF MICHIGAN EXPRESSLY DISCLAIMS ANY LIABILITY FOR CHANGES MADE TO THIS FORM BY LEGISLATIVE ENACTMENTS OR JUDICIAL DECISIONS,

FROM NAGLE PAVING

FULL UNCONDITIONAL WAIVER

My/our contract with		Nagle	Paving Compa	
to provide	Geogrid Materi	als	(other contracting)	рапу)
for the imp	rovement to the	property described	as:	Novi Neighborhood Roads
)				
having bee waived and		satisfied, all my/our	construction lier	rights against such property are hereby
			Ву: _	CSI/Geoturf
			Address:	P.O. Box 668
			-	Highland, MI 48357
			Telephone:	248 887 6767 phone 248 887 0855
Signed on:	3/3/1	6		Tom Rosinson Contractor

DO NOT SIGN BLANK OR INCOMPLETE FORMS. RETAIN A COPY.

THE CONSTRUCTION ASSOCIATION OF MICHIGAN EXPRESSLY DISCLAIMS ANY LIABILITY FOR CHANGES MADE TO THIS FORM BY LEGISLATIVE ENACTMENTS OR JUDICIAL DECISIONS.

FULL UNCONDITIONAL WAIVER

My/our contract with Na	egle Paving	مددد
to provide paving grade fabric	(other contracting party)	
for the improvement to the property described as:	s:	
	Novi Neighborhood Roads	
having been fully paid and satisfied, all my/our co	onstruction lien rights against such property are hereby	
waived and released.		
	Road tabrics	وشف
	By: (signalure of lian Balmani)	All conserve
	Address: PØ Box 87380	
	Carol Stream, IL 60188-7380	
	Telephone: (630) 293 3111	مستاكة
3-3.11-	PAT WOJTOWICZ	
Signed on: 2-3-16	CONTROLLER	

DO NOT SIGN BLANK OR INCOMPLETE FORMS. RETAIN A COPY.

THE CONSTRUCTION ASSOCIATION OF MICHIGAN EXPRESSLY DISCLAIMS ANY LIABILITY FOR CHANGES MADE TO THIS FORM BY LEGISLATIVE ENACTMENTS OR JUDICIAL DECISIONS.
